


Progress for the Month

June 2026


- Civil work update: Richmond Road for Portion 1 between Townson Road and Alderton Drive.
- Ongoing utility investigations at various locations in Portion 2 between Alderton Drive and M7
- Site establishment in Area 15
- Utility and geotechnical investigation update:
 - 8/32 boreholes remaining
 - 10 potholing/trenches remaining

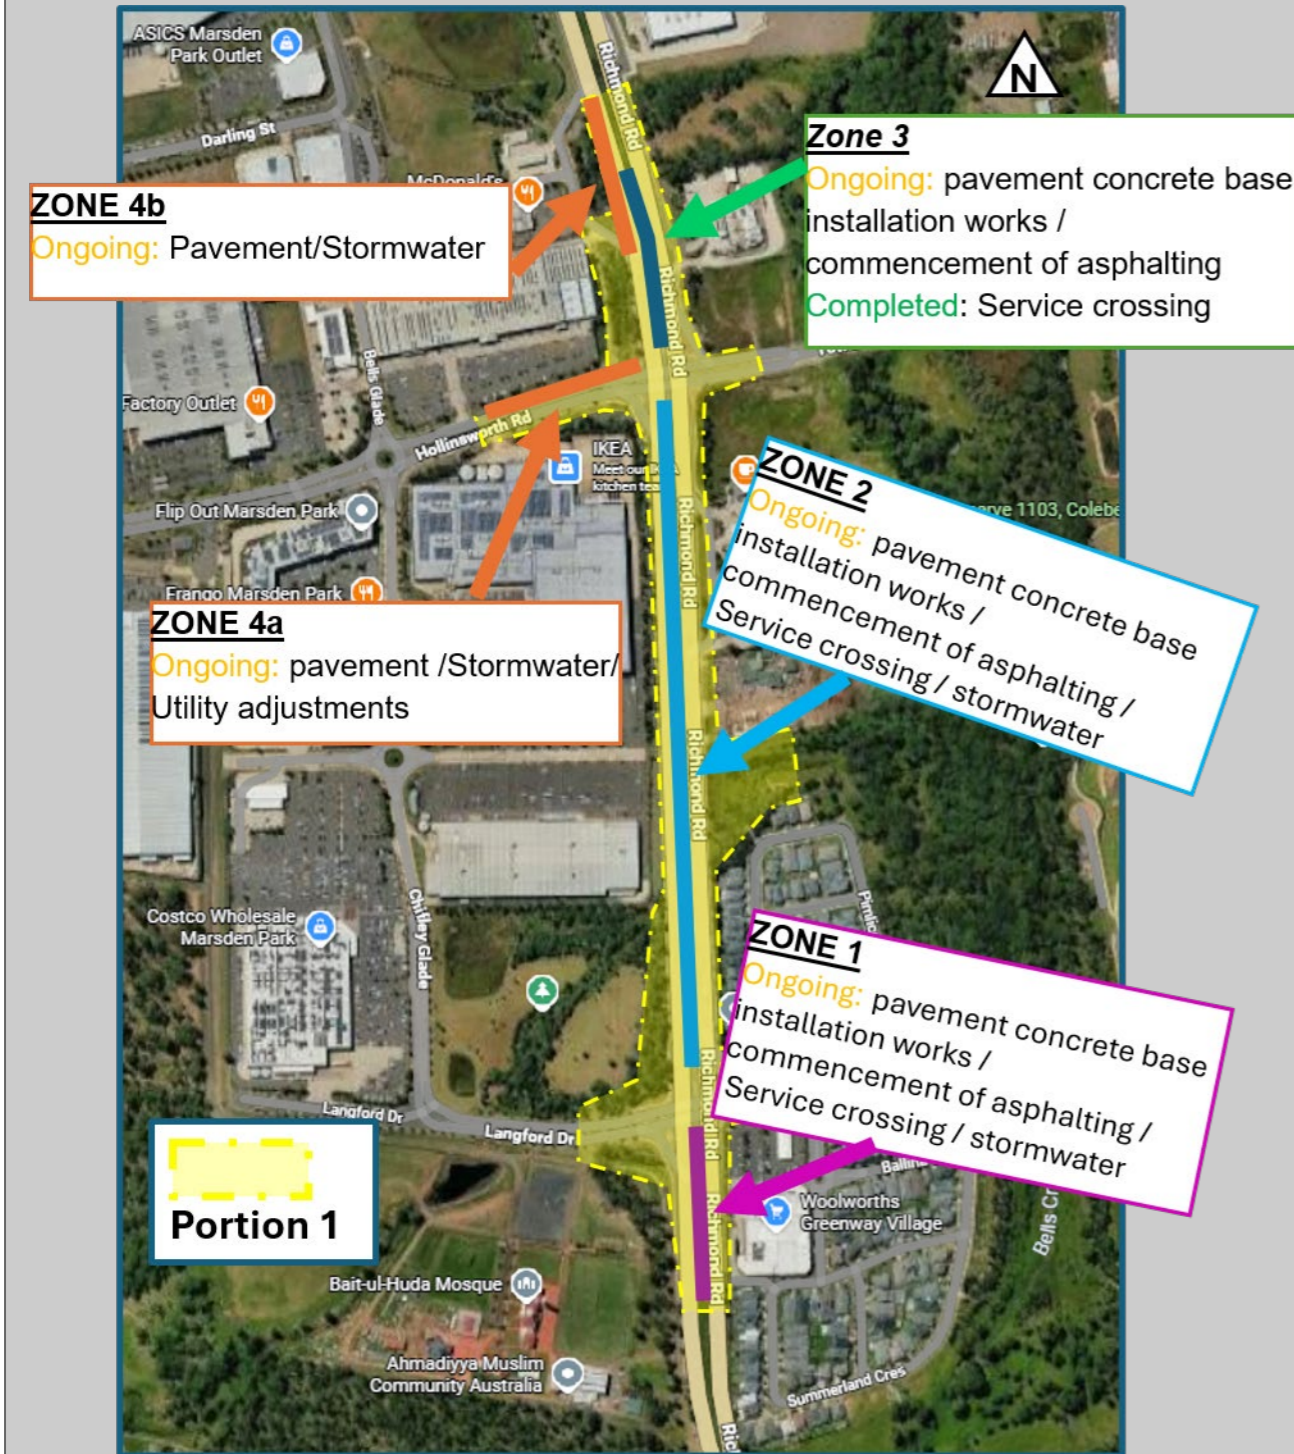

Progress for the Month

Program for July 2026

NBN works

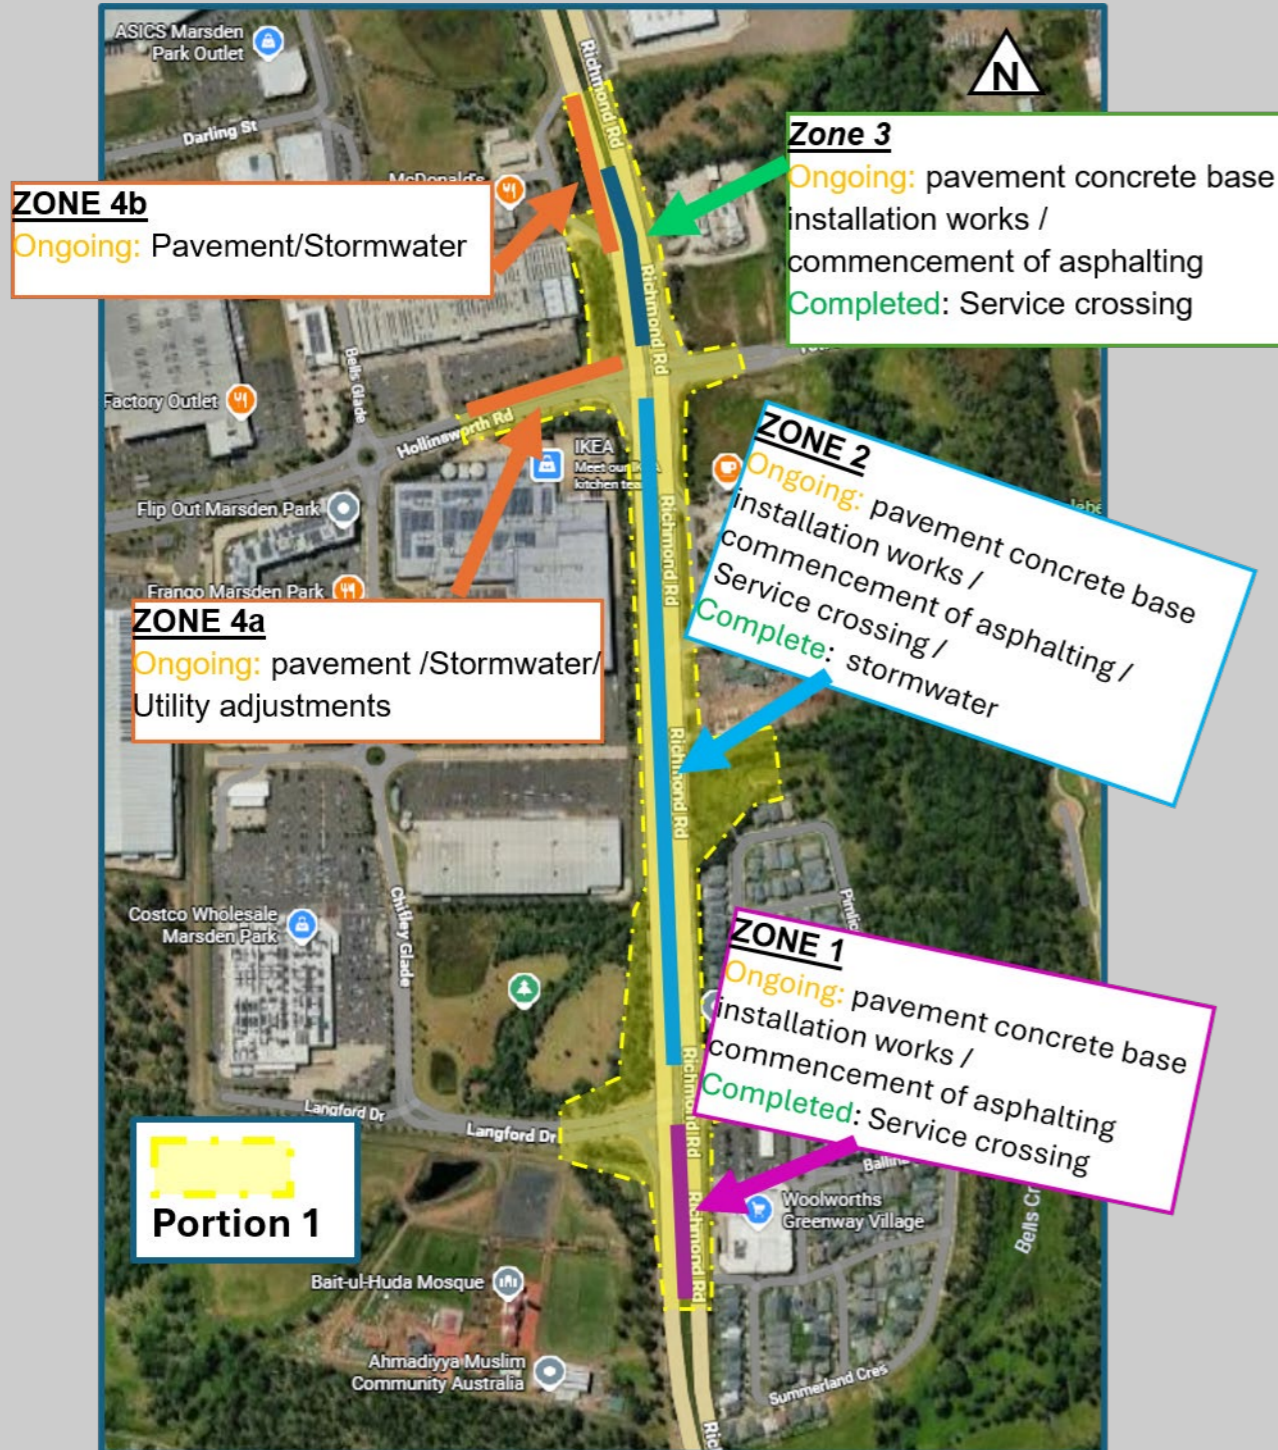

Pavement works in Zone 3



Drainage works in Zone 4B



Hollinsworth – culvert precast installation in May

