



Construction Impacts Meeting 07.31.2026



TDP – Work Package #01 – Apron Demolition

Weekly Progress

- Demolition of available apron complete

Upcoming Work

- West apron paving demolition (after reinstating RON positions)
- Demo contractor demobilized until 09.2026



TDP – Work Package #02 – Mass Excavation, Utility Demolition & Early Foundations

Weekly Progress

- Continued mass excavation along VSR road (West side)
- Continued mass excavation and backfill around end of concourse
- Continued rough grade existing terminal connector for last mud slab
- Began cutting grade for South Loading Dock

Upcoming Work

- Continued mass excavation around building perimeter
- Earthwork and piers for the Circulation Corridor



TDP – Work Package #03b – Below Level 1 Utilities/Structure

Weekly Progress

- Continued installing utilities throughout crawlspace
- Continued installing subgrade drainage and storm collectors
- Forming escalator and elevator pit at GTC

Upcoming Work

- GTC Connector underground MEP install
- GTC foundations
- SOG placement Connector East C8-C2



TDP – Work Package #04 – Structural Steel & Mass Timber

Weekly Progress

- Continued steel erection through Ticket Hall
- Continued Installation of Glulam Fish Bellies and CLT in the Mercado and Ticket Hall
- Completed erection of Steel Zone 6
- Continued decking Zone 6
- Nearing completion of Steel Zone 10 in Terminal Connector
- Continued Deck and Detail activities through Ticket Hall.
- Began setting stairs inside Concourse
- Began erecting steel in the Welcome Plaza



TDP – Work Package #04 – Structural Steel & Mass Timber

- Upcoming Work
 - Set elevator machine beams
 - Continue setting interior and exterior stairs



TDP – Work Package #05 – Foundations Above Piers & Level 1 Concrete

Weekly Progress


- Placing level 3 area 4 in Ticket Hall
- Place Slab on metal deck level 2 area 21 Ticket Hall
- Reinforce Slab on metal deck 23 Ticket Hall
- Reinforce Slab on metal deck 7 level 3 Ticket Hall

Upcoming Work


- Place Slab on metal deck 19 on level 2
- Slab on deck 24 Terminal Connector shoring and pans
- Slab on void 25 Terminal Connector
- Place Slab on metal deck 7 level 3 Ticket Hall



TDP – Level 1 Concrete

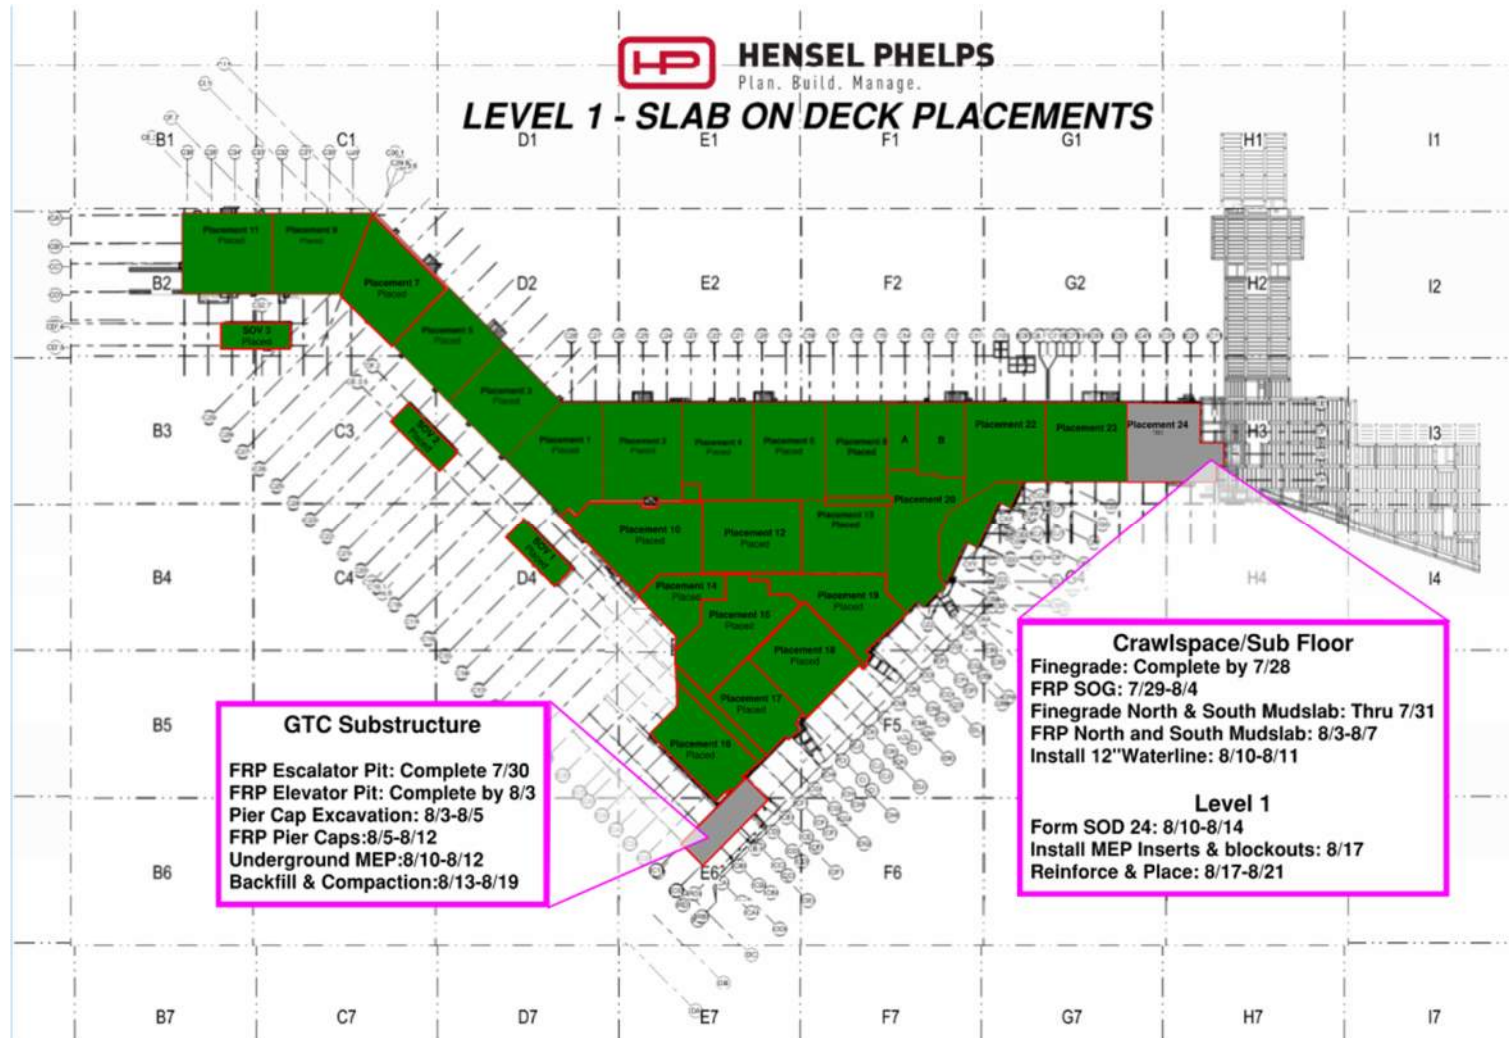

TDP – Level 2 Concrete

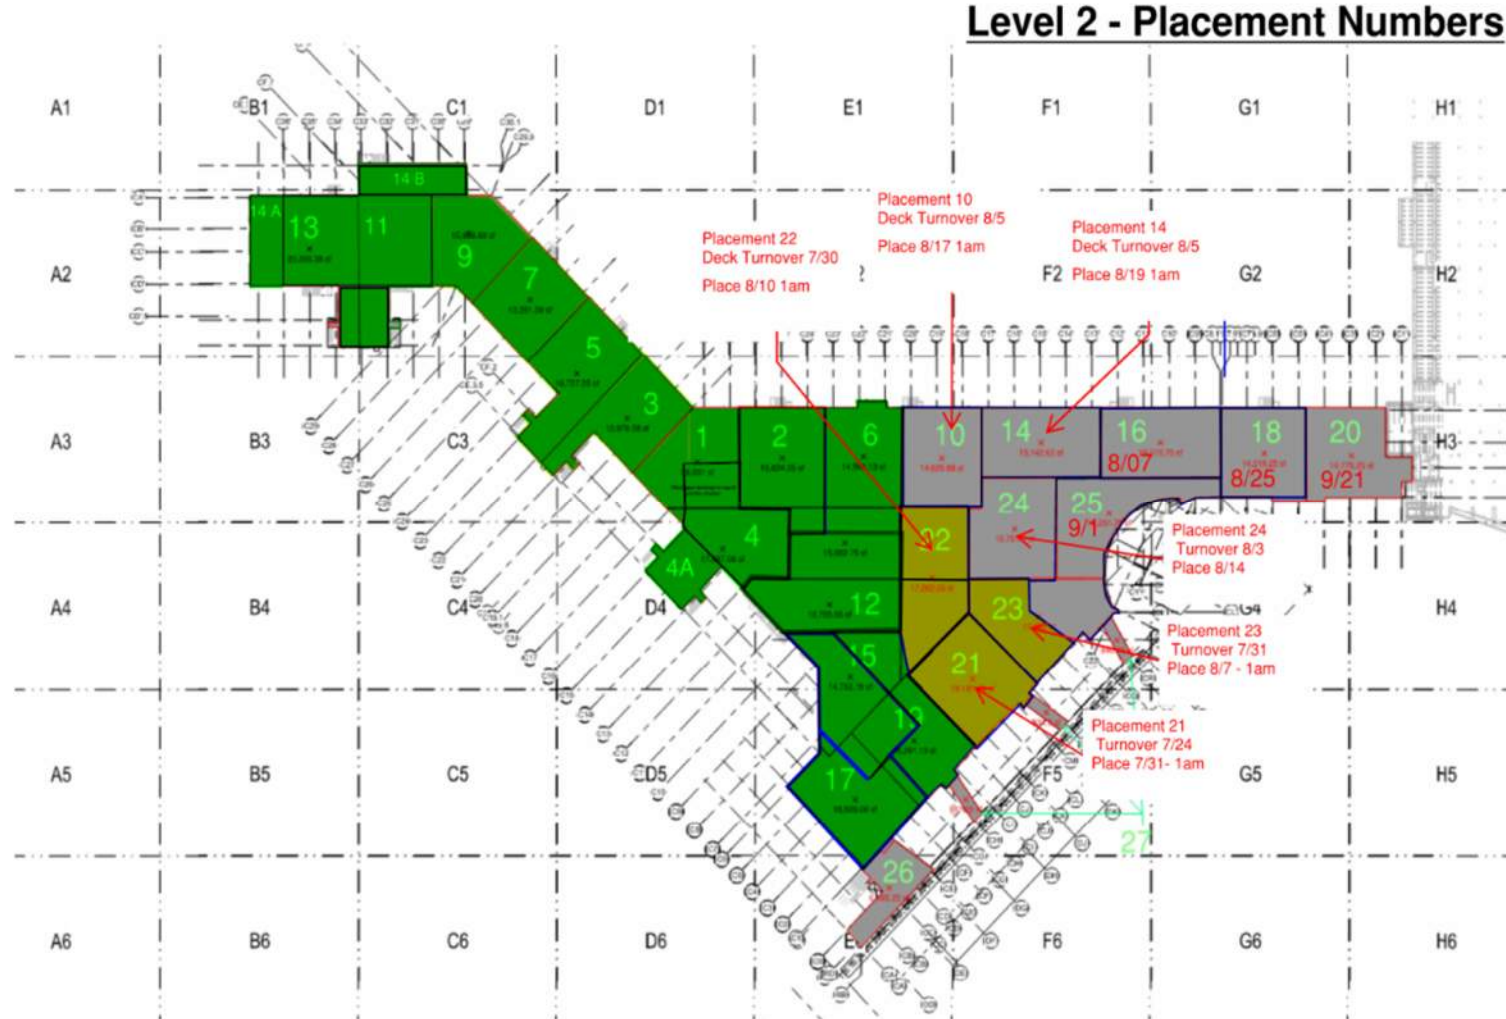


TDP – Low Roof Concrete



HENSEL PHELPS

Plan. Build. Manage.

Low Roof - Placement Numbers

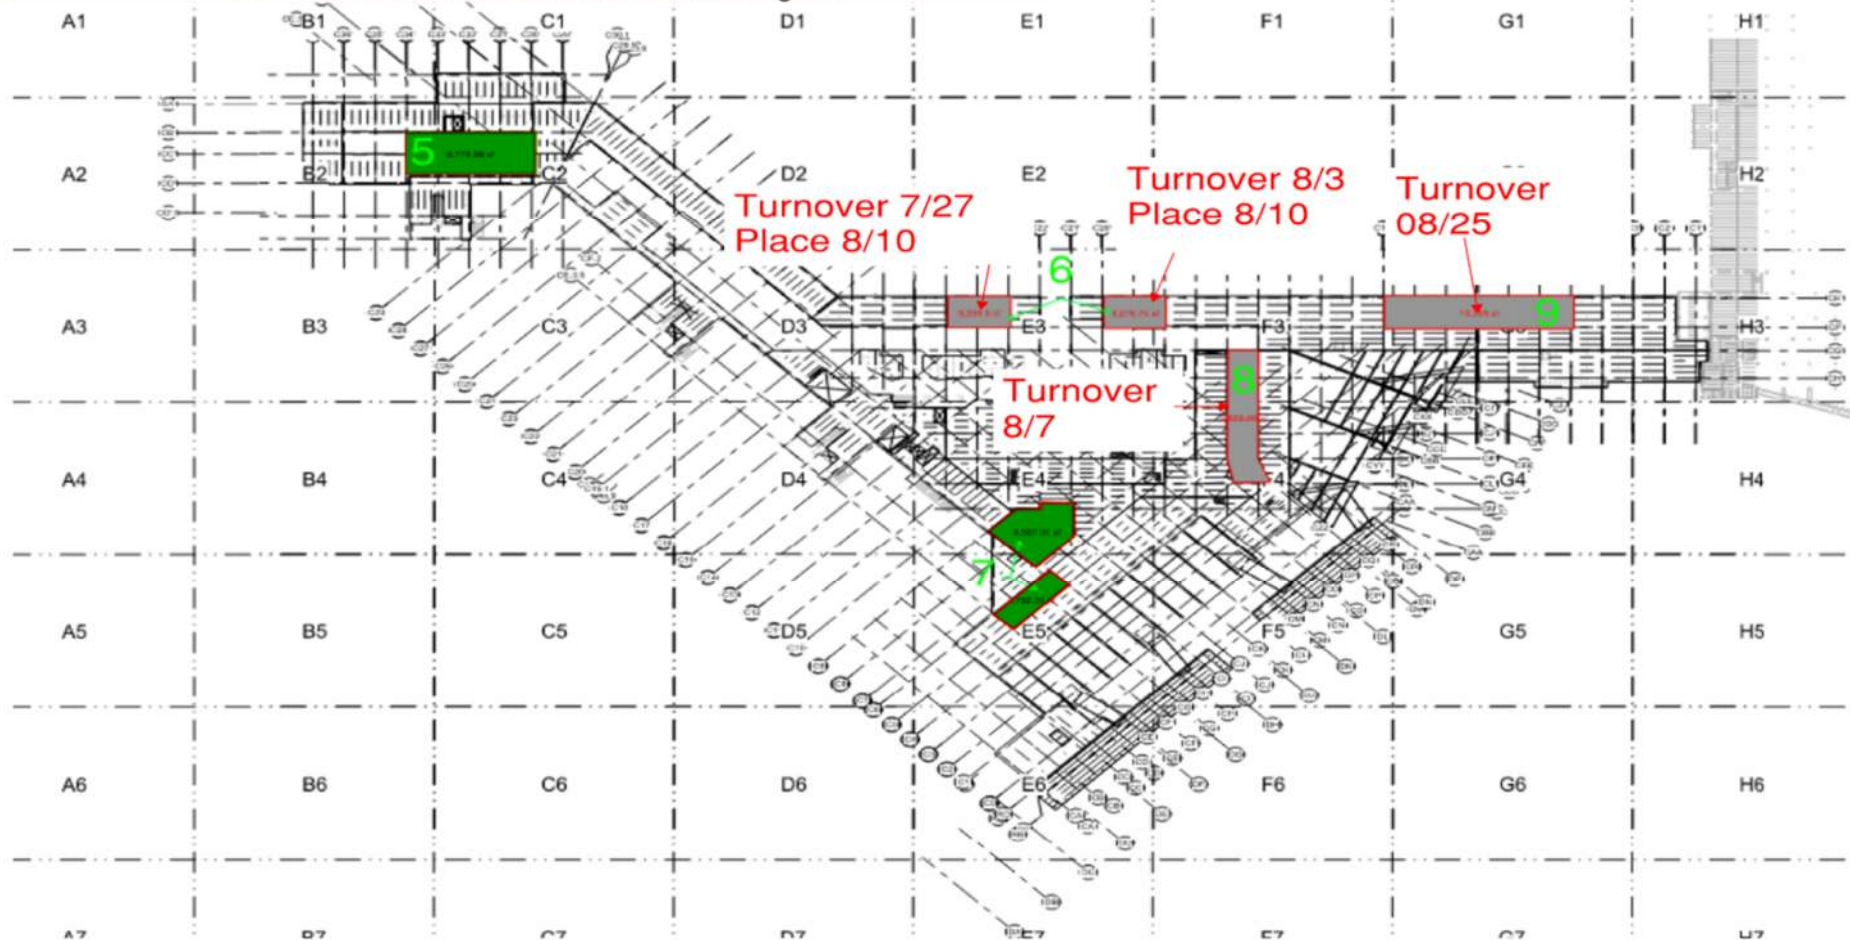

TDP – Work Package #05 – Underground Utilities



Weekly Progress

- Continued installation of electrical fueling duct banks
- Continued installing CIP anchor slabs and walls for trench drain A.E1 – A.E4
- Completed casting lids to storm junction boxes for junction box W01 – W03
- Completed placements for Cast in place storm junction boxes (slab and walls)
- Completed Installation of RCP between storm junction boxes

Upcoming Work

- Place Junction Box W01 – W03 lids after curing period
- Install underdrain Trench Drain A.E01 – A.E07

TDP – Work Package #05 – Nakoma Lot



Weekly Progress

- Place remaining fabric for parking lot
- Place remaining flex base material

Upcoming Work

- Complete fabric install for parking lot
- Complete flex base material placement
- Awaiting permit approval
- Install retainage pond liner
- Install concrete driveways (2)

TDP – Work Package #05 – Underground Utilities – CPS Energy

Weekly Progress

Terminal C

- Zachry continued installation for conduit work
- Flowable fill placed 07.30
- Required lane closure

Upcoming Work

Terminal C Switchgear

- PMCM Team to coordinate with facilities and ITSD regarding utility locates (water, power, IT/communications) in work area
- Conduit installation between manholes and for equipment pads
- Lane closure to continue for 2 – 3 weeks while conduit work is completed




TDP – Work Package #06 – Apron Paving

Weekly Progress

- Continued P-209 installation on East Apron
- Continued P-304 CTB install Sequence 2
- Placed fixed form control strip (07.27)
- Placed Slip form control strip (07.28)
- Continued cement concrete paving in Sequence 1 and 2
- Completed C94 Uniformity testing (4 rds)
- Began CTS (P-156) in Sequence 3B




TDP – Work Package #06 – Apron Paving

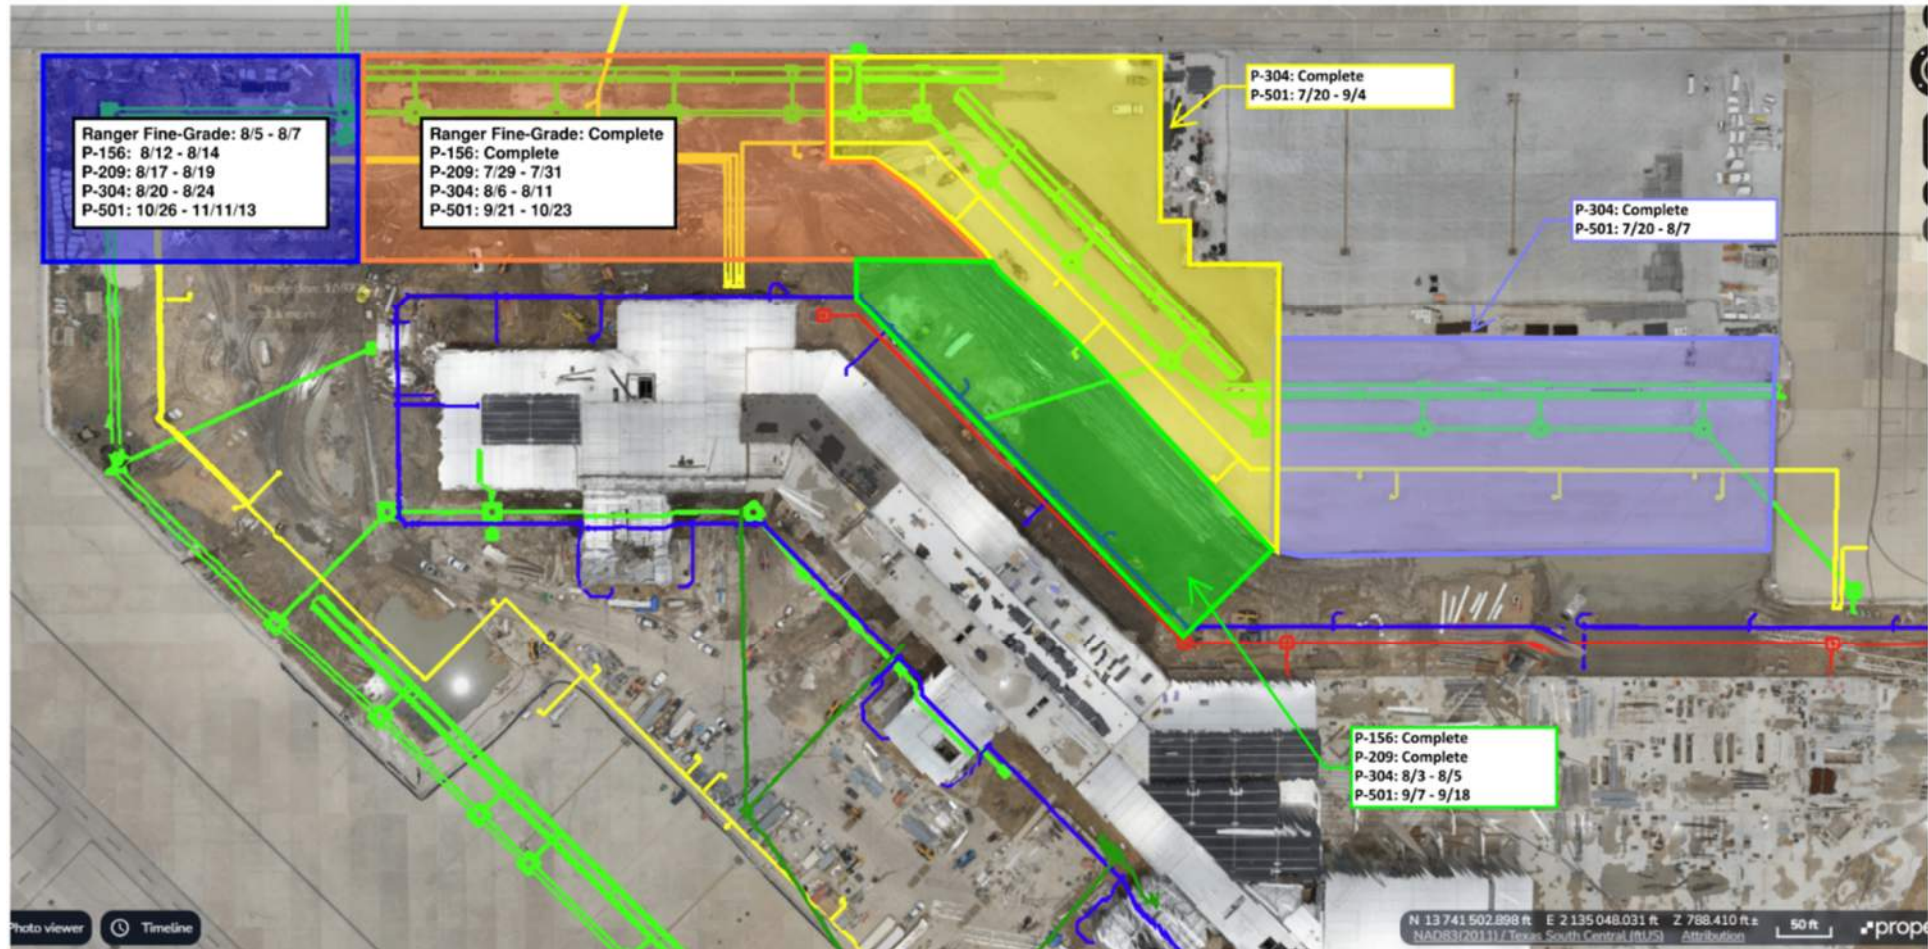

TDP – Work Package #06 – Apron Paving

Upcoming Work

- P-501 Cement concrete paving continuing next week, Sequence 1
- Fine grade remaining area in Sequence 3 Part 3B
- CTS install Sequence 3 Part 3B

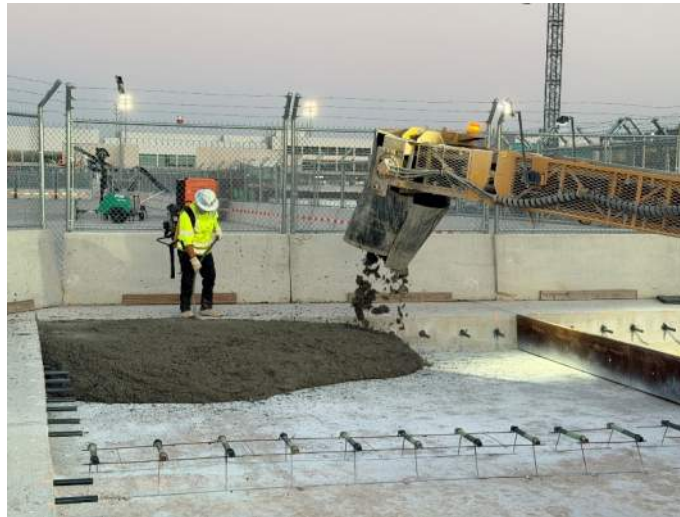


TDP – Work Package #06 – Mechanical, Electrical, Plumbing & Fire Protection Systems & Building Exterior Envelope

Weekly Progress


- Continued installation of IMP panels on level 2 framing Concourse East
- Framing priority walls on Level 1 and 2
- Continued install of Fire Pipe in Checked Bag Inspection System (CBIS)
- Continued install of Hydroponic Piping in CBIS
- Began install of Duct Work in CBIS
- Began installing fire pipe in Primary/Secondary
- Continued installing roofing and forming crickets above Concourse
- Setting roof curbs for MEP equipment above Concourse



TDP – Work Package #06 – Building Exterior Envelope

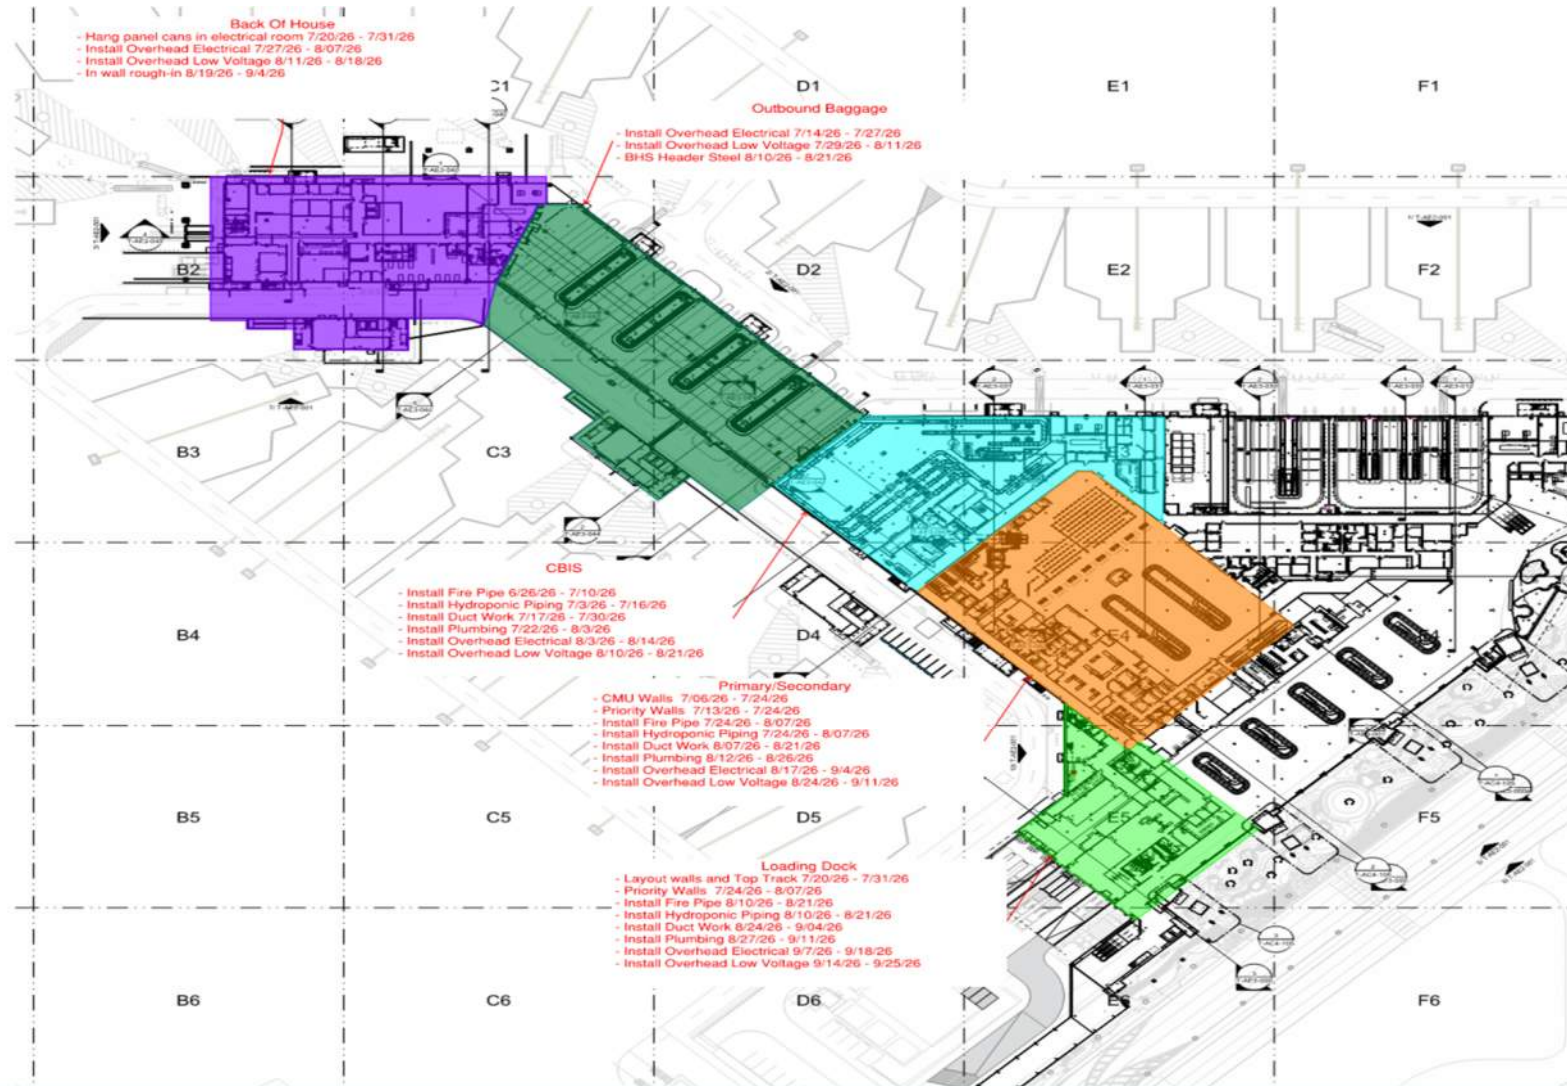



TDP – Work Package #06 – Building Exterior Envelope

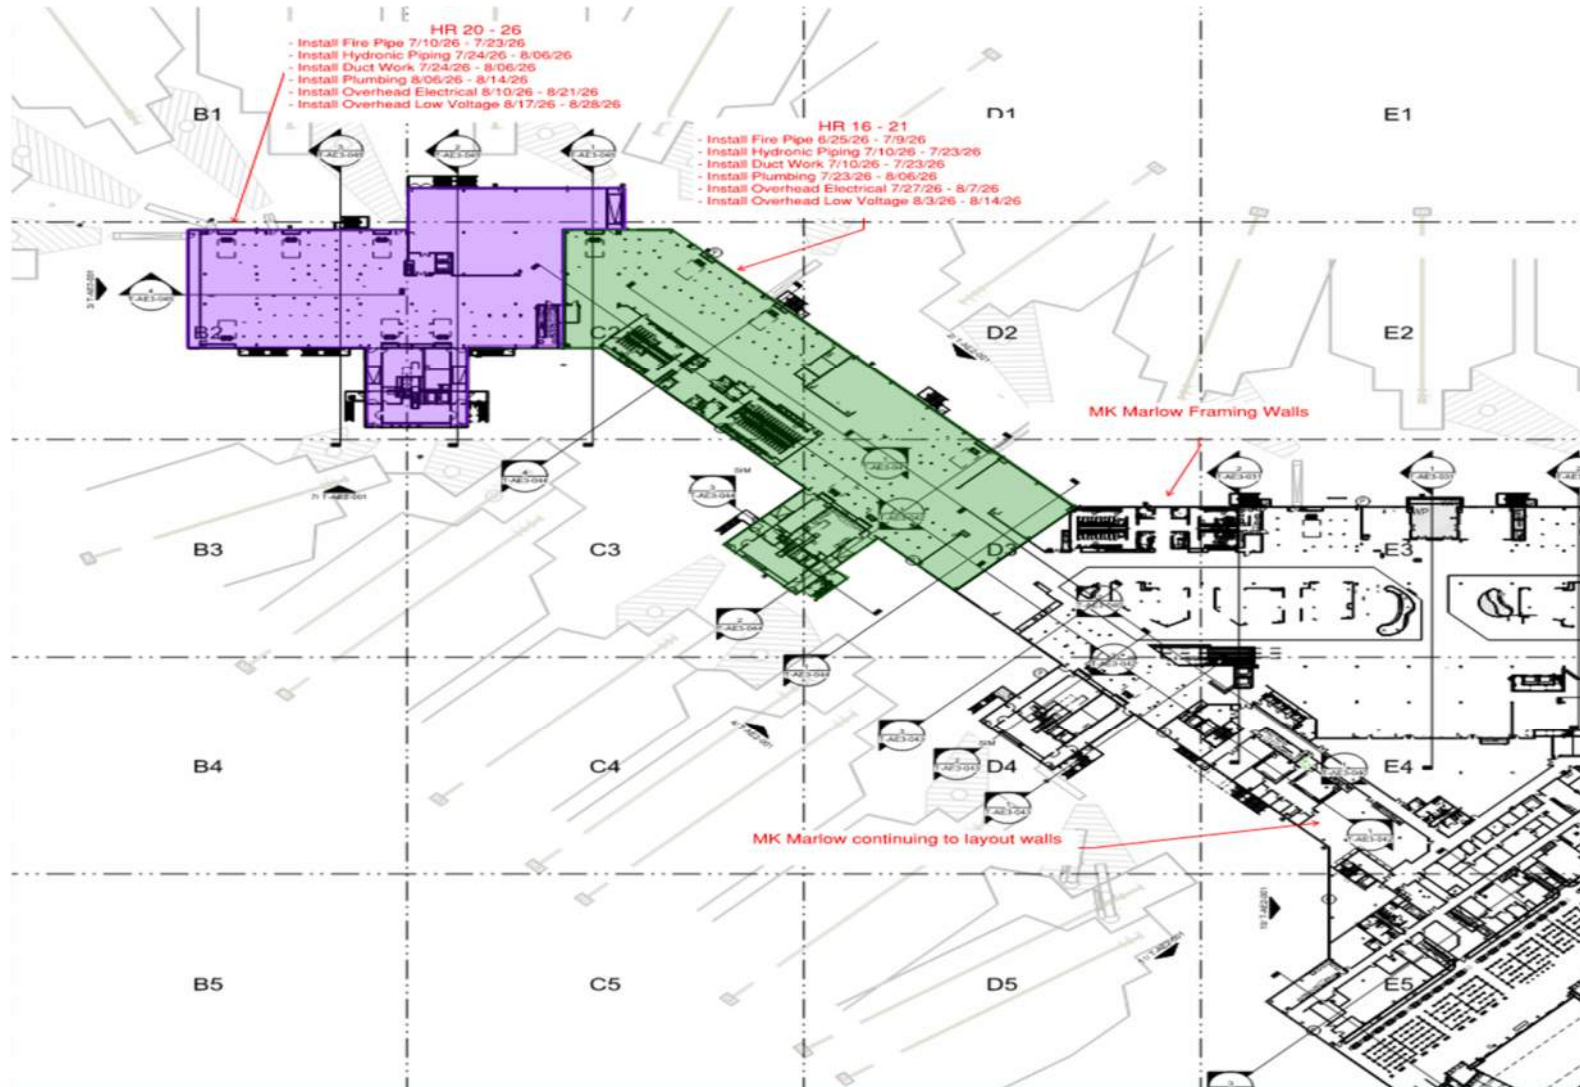

TDP – Work Package #06 – Mechanical, Electrical, Plumbing & Fire Protection Systems & Building Exterior Envelope

Weekly Progress

- Continue exterior CFMF install at Ticket Hall East and West Level 2 Phase 1
- Continue waterproofing Level 1 Phase 1 East and West side of Concourse
- Continue installing fire pipe in Back of House
- Continue installing hydronic piping
- Continued installation of IMP panels on level 2 framing Concourse East
- Framing priority walls on Level 1 and 2

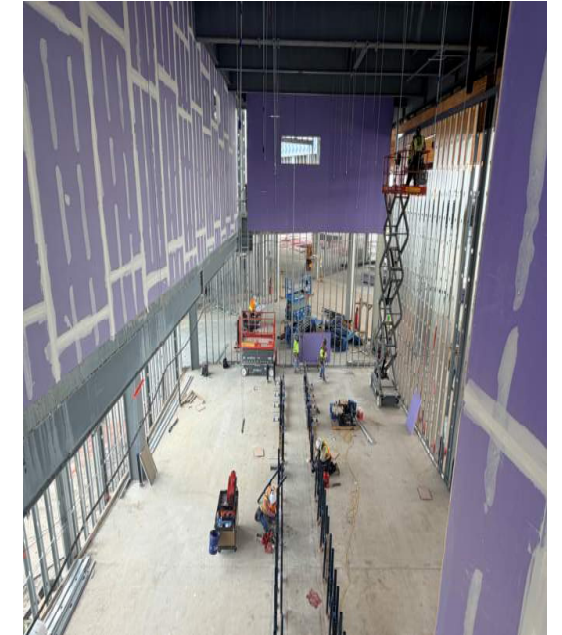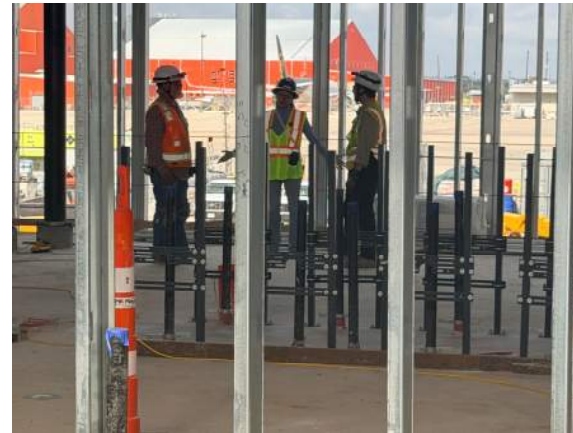

TDP – Work Package #06 – Mechanical, Electrical, Plumbing & Fire Protection Systems & Building Exterior Envelope

Upcoming Work

- Roofing above Ticket Hall (08.03 target)
- Burnished block installation
- IMP level 2 installation West side of Concourses
- Plumbing, overhead electrical, and low voltage install in CBIS




TDP – Work Package #06 – Central Utility Plant (CUP) Upgrades

Weekly Progress

- Continued installation of UG hydronic lines.
- Continued plumbing installation
- Placed concrete foundations for WTB
- WTB pad preparation
- Installing UG utilities for WTB
- Setting electrical panel boards in existing structure
- Forming and reinforcing foundations for new cooling tower

Upcoming Work

- Erection of WTB steel

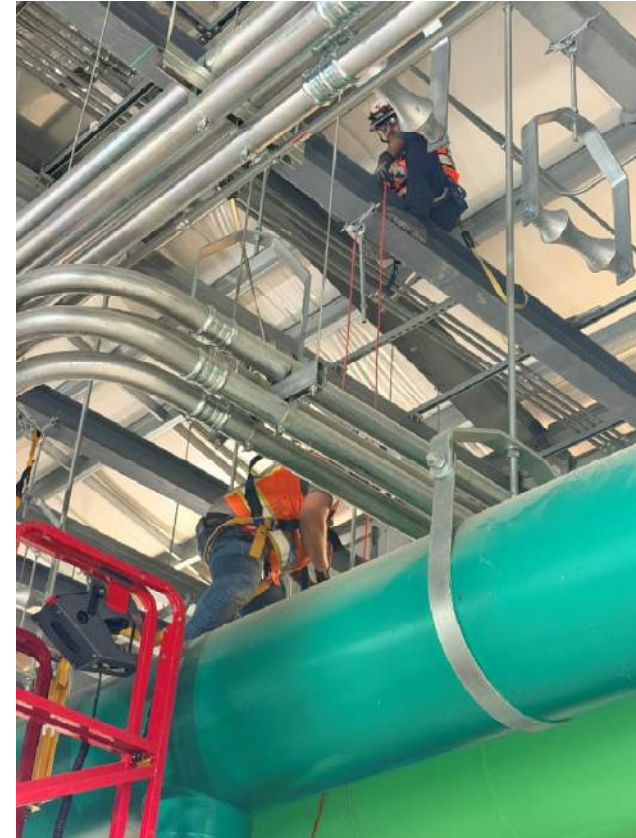

TDP – Work Package #06 – Central Utility Plant (CUP) Upgrades




TDP – Work Package #06 – Triturator

Weekly Progress

- Continued backfill to bottom of SOG
- Began underground utility install (plumbing)
- Delivery of structure components (Trusses)

Upcoming Work

- Backfill utilities
- FRP foundations/slab on grade

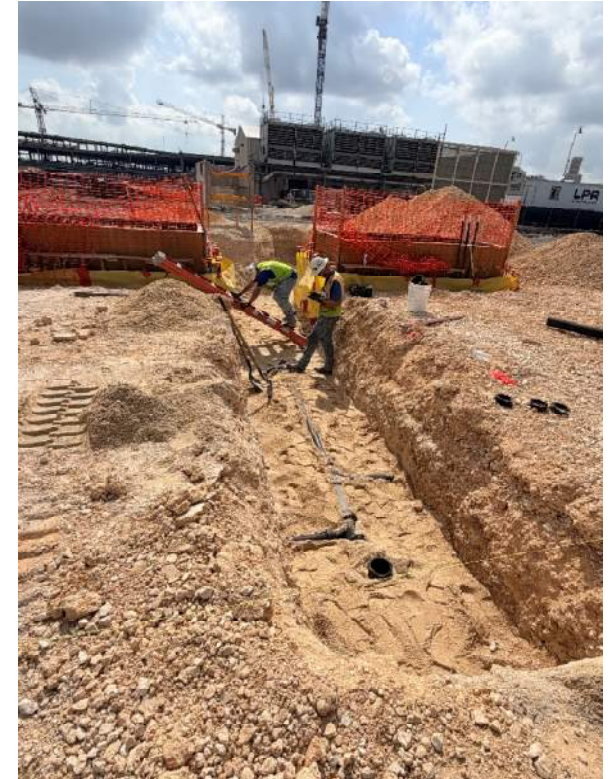

Terminal A – Electrical System Expansion

Weekly Progress

- The new main switchboards MSB 1-A , 1B and distribution panels have been commissioned and tested by the Siemens technicians.
- New switchboard MSB-1B is has been connected to the CPS utility transformer via CT cabinets and metering equipment.
- The interconnection of MSB-1A and MSB-1B with conduits and feeders has started this week.
- CPS is scheduled to make cable terminations in utility transformer for MSB-1B switchboard and metering equipment this week.

Upcoming Work

- The interconnection of MSB-1A and MSB-1B with conduits and feeders to be finished next week.
- CPS is scheduled to reenergize utility transformer feeding MSB-1B and metering equipment on Monday August 3rd 11pm – 2am
- Discussions for future power outage procedures are ongoing with CPS and the electrical contractor.



Terminal C Parking Garage – Site Prep Work 90 DAY OUTLOOK

- GARAGE B BUILDING PAD MASS EXCAVATION: 7/1 – 7/14/26
- GARAGE B BUILDING PAD FILL & COMPACTION: 7/17 – 8/24/26
- GARAGE A BUILDING PAD MASS EXCAVATION: 7/14 – 8/11/26
- GARAGE A BUILDING PAD FILL & COMPACTION: 8/11 - 9/22/26
- TOLL PLAZA & SOUTH LOT MASS EXCAVATION: 8/17 – 8/31/26
- TOLL PLAZA & SOUTH LOT FILL & COMPACTION: 9/1 – 9/15/26
- GARAGE B STORM SYSTEM INSTALL: 8/27 – 9/24/26
- DRILLED PIERS AT GTC LOBBY: 8/27 – 9/10/26
- DRILLED PIERS AT GARAGE B BUILDING PAD: 9/18 – 10/8/26
- GARAGE A & SOUTH LOT STORM SYSTEM INSTALL: 9/25 – 11/12/26
- DRILLED PIERS AT GARAGE A BUILDING PAD: 10/16 – 11/05/26

Schedule Impacts:

Weather delay 005-07.13.26

Weather delay 006-07.14.26

Weather delay 007-07.15.26

Weather delay 008-07.16.26

Weather delay-009-07.17.26


Weather delay-010-07.20.26

Weather delay-011-07.24.26

Soil Impact Zone A (West Area B)

Soil Impact Zone B (East Area B)

Existing Pier Foundations Removal

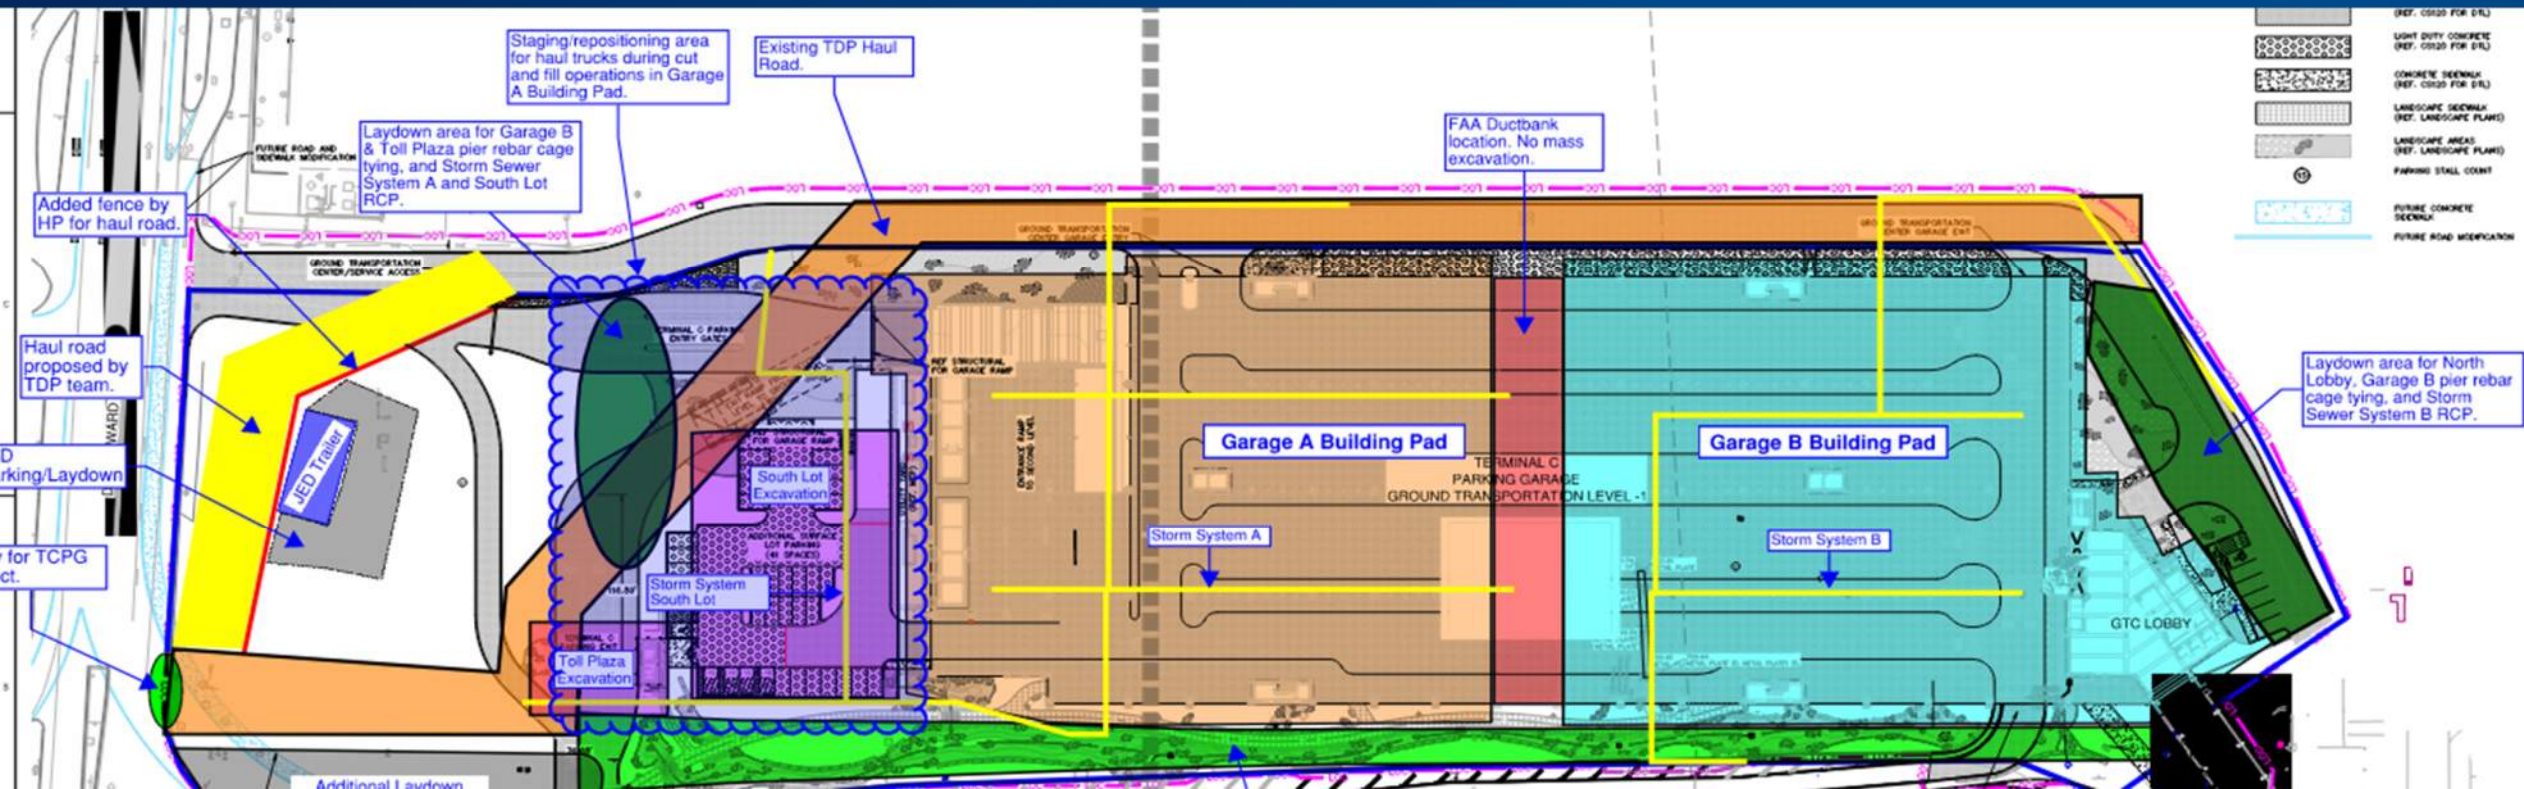

Terminal C Parking Garage – Site Prep Work



Operational Readiness, Activation & Transition

Operational Change Assessment Registration Form



Please **Scan the QR code** to register for an **Operational Change Assessment session**.

Thank you to everyone who attended the last ORAT session where we walked through operational flows and touchpoints. These August workshops will build on July's work by focusing on key operational changes for Terminal C and assessing how existing processes will shift for the new terminal. Previous attendees and Staff with operational knowledge are encouraged to attend.

- **Tuesday, August 18th | 1:00 PM – 2:30 PM**
- **Thursday, August 20th | 8:30 AM – 10:00 AM**

<https://forms.cloud.microsoft/r/MQHYqP7MXd>
