



Construction Impacts Meeting 10.16.2026



TDP – Work Package #01 – Apron Demolition

Weekly Progress

- Striping completed for new RON positions
- Completed temporary AOA fence move 10.12
- Security to perform AOA fence inspection
- Begin West Apron demo on 10.12

Upcoming Work

- Continue West Apron demo and of existing utility removal
- Concrete spoils to be delivered to concrete stockpile near end of RWY 22




TDP – Work Package #02 – Mass Excavation, Utility Demolition & Early Foundations

Weekly Progress

- Resumed mass excavation along VSR road (West side). Currently working down the Concourse towards the Ticket Hall

Upcoming Work

- Earthwork Circulation Corridor
- Circulation Corridor utility demo

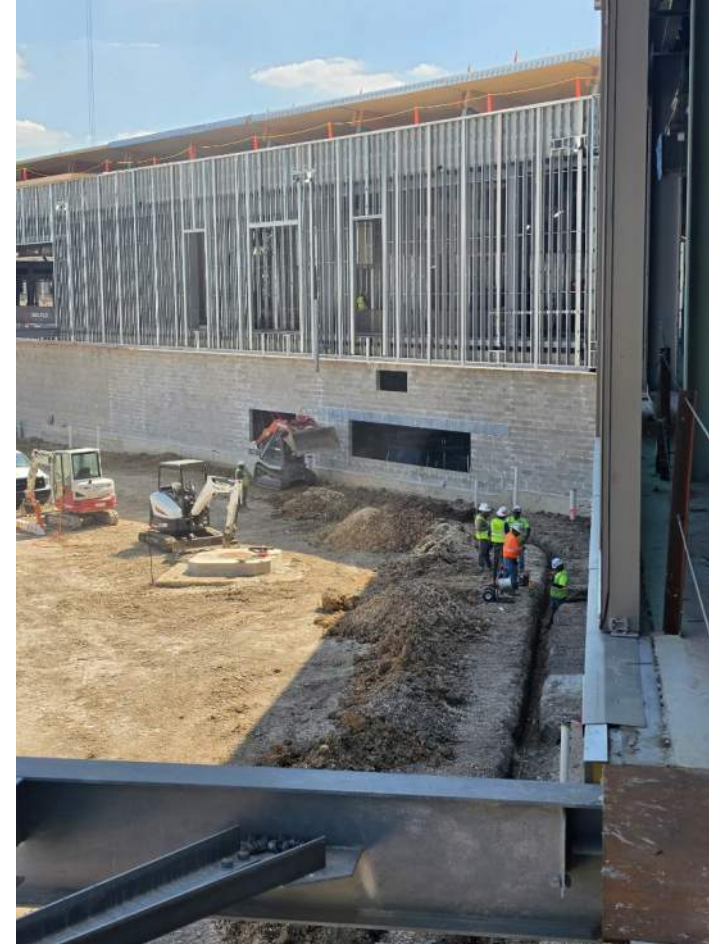

TDP – Work Package #03b – Below Level 1 Utilities/Structure

Weekly Progress

- Continued installing utilities throughout crawlspace
- Installing GSE charger conduit through crawlspace
- Continued backfilling hydronic installation to CUP

Upcoming Work

- Domestic water connection to Terminal C



TDP – Work Package #04 – Structural Steel & Mass Timber



Weekly Progress

- Continued steel erection through Ticket Hall and Connector
- Continued detail activities through Ticket Hall and Connector.
- Continue setting stairs inside Ticket Hall and at Gate Houses
- Completed erection of Zone 12 steel
- Continuing decking in Terminal Connector
- Completed erecting steel at GTC (TOPPING OUT!!!)

TDP – Work Package #04 – Structural Steel & Mass Timber



Upcoming Work

- Continue setting elevator machine beams
- Continue setting interior and exterior stairs
- Finish Glulam and CLT detailing
- Steel pieces erected - 19,555 pieces
- Glulam beams set – 227 beams
- CLT panels placed – 500 panels

TDP – Work Package #05 – Foundations Above Piers & Concrete

Weekly Progress

- Resumed preparing subgrade at SOV 25
- Forming and reinforcing stair stoops on East side of connector
- Placed footings for retaining walls C and D
- Forming and reinforcing walls at Retaining Wall C and D

Upcoming Work

- Place stair stoops east side of Connector
- Place retaining Wall C and D footing




TDP – Work Package #05 – Underground Utilities

Weekly Progress

- Continued forming and reinforcing lid for junction box W05
- RCP and collars to junction box W05 complete
- Continue installation of domestic water line West side of Concourse under the VSR road
- Completed reroute RCP for trench drain A.W01

Upcoming Work

- Begin forming and reinforcing anchor slab trench drain A.W01
- Underdrain Installation at trench drain A.W01
- Place concrete at underdrain cleanouts

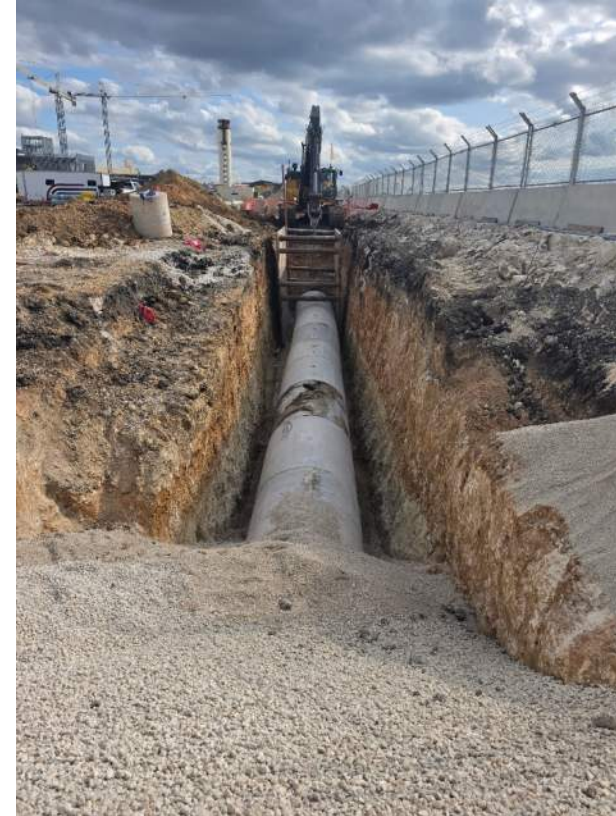

TDP – Work Package #06 – Apron Paving

Weekly Progress

- Continued placing P-501 cement concrete pavement in the East Apron
- Resumed Cement treated base course up to face of building in Sequence 1 & 2
- Installing Compression joint seals throughout Sequence 1

Upcoming Work

- Continue airfield paving and subgrade preparation through 3B
- Continue Installing P-604 and P-605 joints in SEQ 1



TDP – Work Package #06 – Building Exterior Envelope

Weekly Progress

- Concourse (East)
 - Continued IMP Phase 3
 - Continued installation of curtain wall Phase 2
 - Complete Phase 4 Level 1 CMU wall
- Concourse (West)
 - Begin Phase 3 Level 2-3 insulated metal wall panels install
 - Install glazing in Phase 2
 - Begin Phase 4 IMP installation
- Concourse (North)
 - Install IMP on North side of Delta Club
- Concourse (Roof)
 - Installing roof above North and Middle Gate Houses
 - Installing framing modifications



TDP – Work Package #06 – Building Exterior Envelope

Weekly Progress

- Ticket Hall East
 - Completed Phase 2 & 3 Level 1 CMU wall
 - Continue Phase 2 and 3 level 2 IMP install
- Ticket Hall West
 - Continue Phase 3 Level 2 CFMF
 - Continue Phase 3 Level 1 CMU
 - Removed stair tower at middle Gate House
 - Completed installation of exterior CFMF where stair tower
- Ticket Hall Roof
 - Continuing Ticket Hall KEY roofing membrane installation
- Terminal Connector East
 - Installing Phase 1 CMU wall



TDP – Work Package #06 – Building Exterior Envelope

Upcoming Work

- GTC/Ticket Hall South:
 - Phase 1 Level 1 & 2 install CMU/CFMF
- Concourse West:
 - Spray applied water proofing lvl 1 CMU
- Concourse North:
 - IMP install level 2
- Ticket Hall Roof
 - Lighting protection installation
 - Install equipment roof curbs
 - Standing seam installation
- Terminal Connector East:
 - Begin roofing activities



TDP – Work Package #06 – Mechanical, Electrical, Plumbing & Fire Protection Systems & Building Exterior Envelope

Areas of Work

- Back of House
- Outbound Baggage
- Concourse (Levels 2 & 3)
- Checked Baggage Inspection System (CBIS)
- Customs & Border Protection (CBP)
- Loading Dock (Ticket Hall)
- Fire Pump Room
- Domestic Baggage Claim
- Inbound Baggage
- Concessions
- Security Screening Checkpoint (SSCP)
- Ticketing
- Gatehouses (Northern, Middle & Southern)



TDP – Work Package #06 – Mechanical, Electrical, Plumbing & Fire Protection Systems & Building Exterior Envelope

Weekly Progress

➤ Mechanical

- Verifying hydronic piping impacts from Design Bulletin T052
- Continued hanging and installing hydronic piping
- Continued installation of hangers for mechanical piping
- Continued overhead rough-in of mechanical piping
- Continued installation of copper mechanical piping
- Continued installation of HVAC duct
- Continued pre-testing of HVAC duct in Concourse
- Continued HVAC duct testing in Back of House
- Continued insulating of hydronic piping
- Continued insulating HVAC duct
- Continued installation of steel pipe in Fire Pump Room
- Delivery of Air Handling Unit (AHU)



TDP – Work Package #06 – Mechanical, Electrical, Plumbing & Fire Protection Systems & Building Exterior Envelope

Upcoming Work

➤ Mechanical

- Continue insulating HVAC duct in Concourse
- Continue installation of copper mechanical piping
- Continue overhead rough-in of mechanical piping
- Continue hanging and installing hydronic piping
- Continue insulating of hydronic piping
- Continue insulation of HVAC duct
- Continue installation of equipment for High Volume, Low Speed (HVLS) Fans
- Continue installation of HVAC duct equipment
- Complete installation of Fan Coil Units (FCUs) in CBIS
- Complete insulation of hydronic piping in CBIS
- Continue installation of steel pipe in Fire Pump Room
- Continue installation of HVAC duct hanger in Concessions Area



TDP – Work Package #06 – Mechanical, Electrical, Plumbing & Fire Protection Systems & Building Exterior Envelope

Weekly Progress

➤ Plumbing

- Continued installation of hangers
- Continued testing domestic water overhead and in-wall piping in Back of House area
- Continued installation of overhead and in-wall piping

Upcoming Work

➤ Plumbing

- Continue installation of hangers
- Continue installation of overhead and in-wall piping
- Start installation of shower stalls in Locker Rooms



TDP – Work Package #06 – Mechanical, Electrical, Plumbing & Fire Protection Systems

Weekly Progress

➤ Electrical

- Continued in-wall and overhead rough-in
- Continued overhead rough-in of pre-fabricated racks
- Continued overhead tie-in
- Continued pulling of branch wire
- Continued preparations for floor poke through
- Continued wall stub outs
- Continued installation of OHAs in Northern Gatehouse

➤ Low Voltage

- Completed tie-ins to Surge Anticipation Valves (SAVs) in Back of House area
- Continued overhead installation
- Continued overhead hanger support rough-in
- Continued in-wall rough-in
- Continued overhead rough-in for cable tray hangers
- Continued installing hangers in Middle Gatehouse



TDP – Work Package #06 – Mechanical, Electrical, Plumbing & Fire Protection Systems

Upcoming Work

➤ Electrical

- TOPS inspection by Development Services (SS1)
- Start installation of electrical panel interiors
- Continue pulling of branch wire
- Continue installation of buss duct
- Continue in-wall rough-in & overhead tie-in
- Continue overhead rough-in of pre-fabricated racks
- Continue wall stub outs
- Continue installation of OHAs in Northern Gatehouse

➤ Low Voltage

- Continue overhead hanger support rough-in
- Continue in-wall rough-in
- Continue installation of basket trays




TDP – Work Package #06 – Mechanical, Electrical, Plumbing & Fire Protection Systems

Weekly Progress

- Fire Protection
 - Continued installation of sprinkler mains and branch lines
 - Continued priming and painting of sprinkler pipe

Upcoming Work

- Fire Protection
 - Continue installation of sprinkler mains and branch lines
 - Pull, test & terminate fire pump feeders from Fire Pump Room to SW2
 - Continue priming and painting of sprinkler pipe

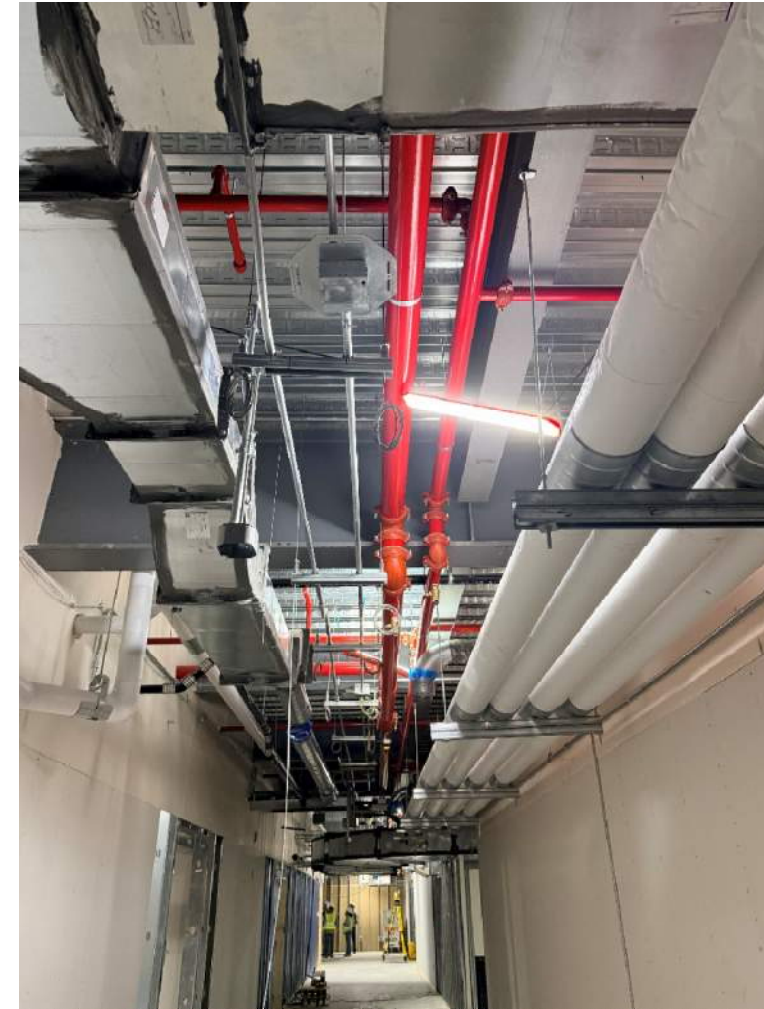

TDP – Work Package #06 – Baggage Handling System

Weekly Progress

- Continued installation of conveyors and steel supports in Outbound Baggage (North & South Sortation)
- Continued layout and installation of steel supports for conveyors in Ticket Hall

Upcoming Work

- Continue installation of conveyors in Outbound Baggage
- Continue installation of steel supports for conveyors in Ticket Hall



TDP – Work Package #06 – Central Utility Plant (CUP) Upgrades

Weekly Progress

- Continue backfilling hydronic lines
- CPSE installing the electrical vault on the West side of the CUP
- Exterior framing of the Water Treatment building

Upcoming Work

- Excavate and install electrical duct bank to future electrical vault South of the CUP



TDP – Work Package #06 – Triturator

Weekly Progress

- Completed installation of CMU
- Installing steel for roof

Upcoming Work

- Metal roof decking



TDP – Work Package #07 – Curbside (Upper Roadway)

Weekly Progress

- Bent cap extension concrete placement
- Final hand chipping on the bridge
- Core drilling to be completed end of week

Upcoming Work

- Continue bent cap extension concrete placements (2 weeks)



Terminal A – Electrical System Expansion

Weekly Progress

- Work continued with two (2) power outages in Terminal A selected areas to cutover feeder circuits from old switchgear MSB over to MSB-1B
- Cutover was for the main IT network (BDF and IDF rooms)
- Notices have been sent to airport operations stakeholders.

Upcoming Work

- Next 5 weeks follows the same pattern with at least 2 outages per week in selected areas to cutover/migrate feeder circuits.
- Notices will be continually sent to airport stakeholders as work progresses



TERMINAL C PARKING GARAGE

Pad A

Pad B

GTC LOBBY

- Pad A excavation in progress with an estimated completion date of **Oct 16, 2026**
- Drill piers at GTC Lobby in progress with an estimated completion date of **Oct 16, 2026**
 - 32 Pier cages installed as of Oct 15
 - 117 CY of concrete into the piers
 - One 165 ft tall crane on-site. Two drill rigs onsite. FAA 7460 approved/NOTAM issued.
- Fill South Half – Estimated Start Date **Oct 19, 2026**

Upcoming ORAT Activities

Technical Site Visits

- **HVAC CUP:** October 21, 2026, at 1:00 PM
- **Building Management System (BMS):** October 21, 2026, at 2:30 PM
- **Electrical Terminal C:** October 22, 2026, at 10:00 AM
- **Building Maintenance Terminal C:** October 22, 2026, at 1:00 PM

