

Contract Update

Week Ending 15.03.26

N0102 LSIBD Pumping Stations



Jackson

Summary

Week Ending 15.03.2026

Monday 9th :

Install precast wall units at Lapperditch and Marshfield, BCS welding plates at Marshfield

Tuesday 10th :

ACE install pipes and pumps at Lapperditch, Backfill and compact behind precast wall units at Marshfield

Wednesday 11th :

ACE install pipes and pumps at Lapperditch, excavate embankment for weed screen and pump base at Marshfield

Thursday 12th :


ACE install pipes and pumps at Lapperditch, excavate embankment for concrete at Lapperditch, complete excavation for north weed screen and pump base

Friday 13th :

Concrete scour protection of embankment Lapperditch, Core drill precast retaining wall units stone and compact weed screen and pump base for blinding, Install birdcage scaffold for grouting

Jackson

GOOD WORKS

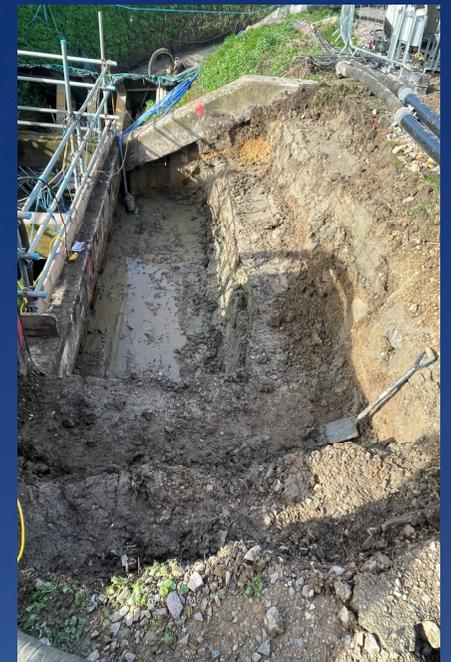

Planned Works

Week Beginning 16/03/2026

Monday:

TSM mobilise for grouting at Marshfield, build rebar cages for pump bases at Marshfield, Vacex embankment at Lapperditch

Tuesday :

TSM grouting at Marshfield, concrete blinding for pump bases and tie rebar cages, Vacex embankment at Lapperditch, ACE start install of pipework in outlet chamber at Marshfield

Wednesday :

Start precast concrete stair install on Lapperdieth outfall, ACE install pipes at Marshfield, remove birdcage scaffold, Build shutters for pump foundations

Thursday :

ACE install pipes and pumps at Marshfield, pour concrete pump foundations, precast stair install at Lapperditch

Friday :

ACE install pipes and pumps at Marshfield, strip shutters and build weed screen rebar cage/shutters, pour concrete for stair infill and eel pass

Jackson

GOOD WORKS
