

Install Checklist

1 First on Site

- Pre-Roof Photos Taken
- Safety Risk Assessment Completed

2 Panels Fitted

- Tidy Cable Management - metal cable-ties used
- Waterproof Gland fitted to Duct
- DC Cable Disconnection Points Labelled & Cable-tied

3 Sol-Flare Fitted

- approx 1.4m above floor
- DC Isolator Wired with cross-over

4 HWC & AC wired


- Thermostat turned to maximum
- New Temp Probe fitted (must be just above the element & underneath the thermostat bracket)

5 Sol-Flare Commissioned

- WiFi Details entered and connected
- AC tested
- PV DC tested




WiFi




AC



PV DC

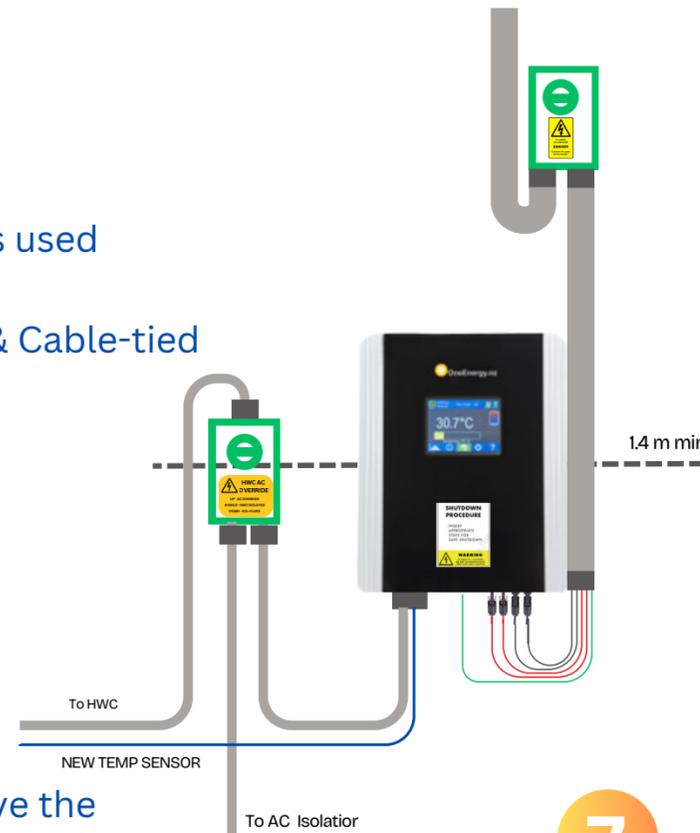

6 Labels Fitted

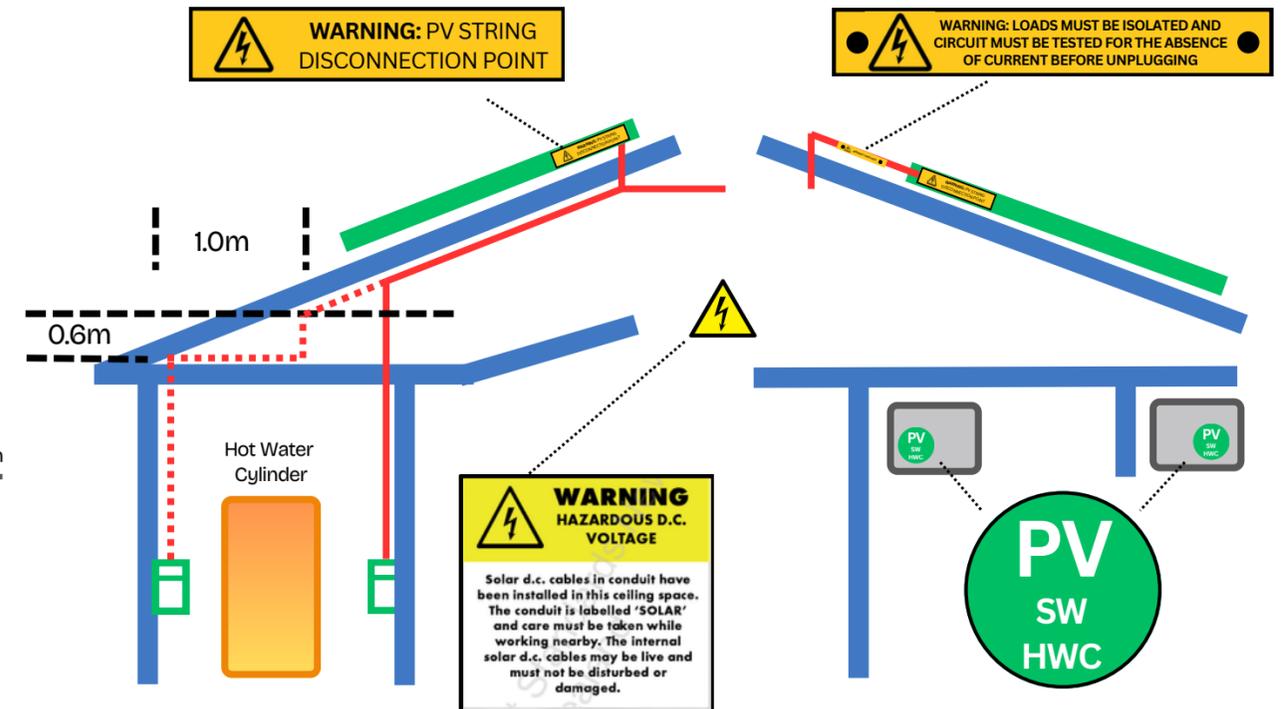

7 Compliance & Photos Uploaded

To www.OneEnergy.nz/installers

- OnSite Roof Photos: Dektite & Finished photos.
- OnSite Sol-Flare Photos: Sol-Flare S/N Label, Installed Sol-Flare; Cylinder Label
- OnSite Commissioning: Sol-Flare S/N & Electrical Commissioning Tests
- CoC: Customer Details & CoC

8 Out of Here
