

Overall Construction Timeline

I-41 Project | Outagamie and Brown Counties, Wisconsin

1 WIS 96 to Lynndale Drive

- » **I-41 Mainline:** early 2025-fall 2026
- » **WIS 96 Interchange:** early 2025-fall 2026
- » **WIS 15 Interchange:** completed in fall 2025
- » **Capitol Drive Overpass:** completed in fall 2024

2 Lynndale Drive to Meade Street

- » **I-41 Mainline:** spring 2026-2028
- » **Gillett Street Underpass:** spring 2026-fall 2027
- » **WIS 47 Interchange:** spring 2026-fall 2026

3 Meade Street to Holland Road and I-41/WIS 441 System Interchange

- » **I-41 Mainline:** fall 2026-2029
- » **Ballard Road Interchange:** completed in fall 2025
- » **French Road Overpass:** early 2026-fall 2026
- » **I-41/WIS 441 System Interchange:** spring 2026-2029

4 Holland Road to County JJ

- » **I-41 Mainline:** 2027-2029
- » **County N Interchange:** completed in fall 2024
- » **WIS 55 Interchange:** 2027-2029
- » **County J Interchange:** completed in summer 2025
- » **Holland Road Overpass:** completed in fall 2025
- » **Vandenbroek Road Overpass:** completed in summer 2025
- » **Buchanan Street Overpass:** early 2026-fall 2026
- » **Rose Hill Road Overpass:** completed in fall 2024

5 County JJ to Miners Way


- » **I-41 Mainline:** spring 2025-fall 2027
- » **County U Interchange:** fall 2025-fall 2027

6 Miners Way to County F

- » **I-41 Mainline:** 2027-2029
- » **Southbridge Road Interchange:** summer 2024-fall 2026
- » **County S Interchange:** 2029

7 Safety and Weight Enforcement Facility (SWEF)

- » Closed for construction fall 2024-summer 2026

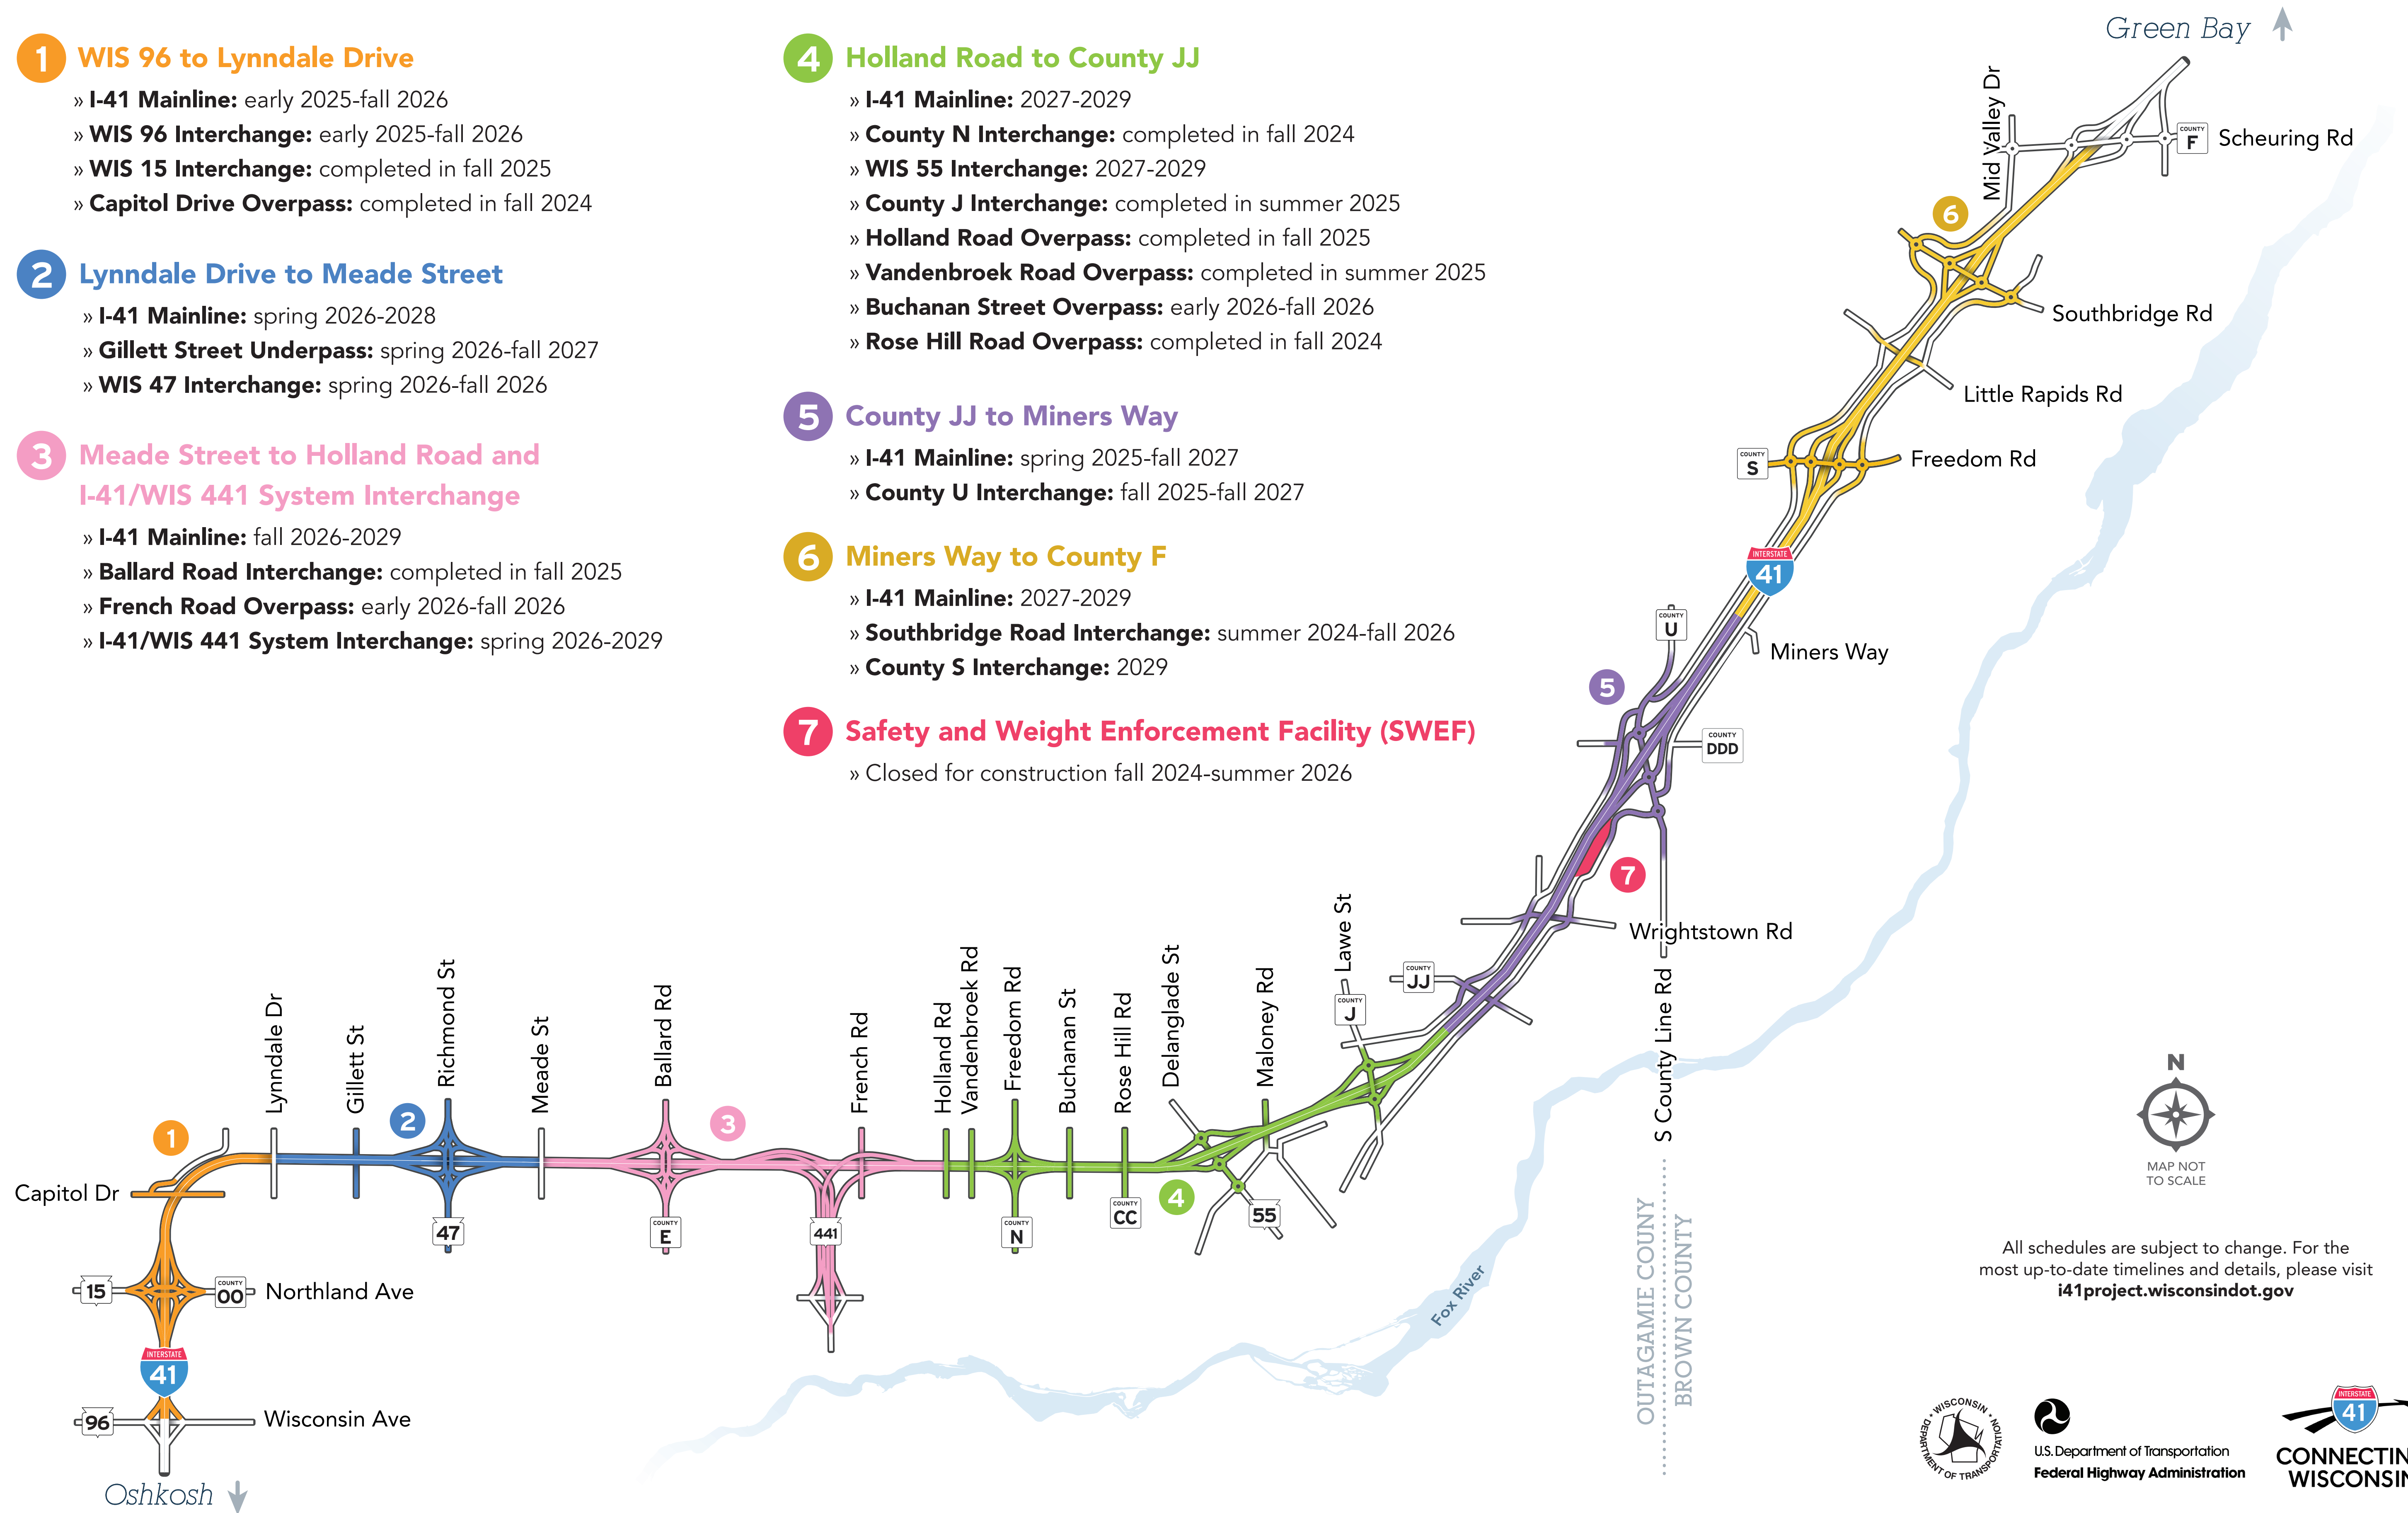

All schedules are subject to change. For the most up-to-date timelines and details, please visit i41project.wisconsin.gov



U.S. Department of Transportation
Federal Highway Administration



2026-01-21
