

Construction Forecast

The Village of Shorewood is reconstructing Oakland Avenue between Capitol Drive and Glendale Avenue. The following work is scheduled as part of this project.

Monday, June 29 through Friday, July 3, 2026:


Crews are scheduled to continue removing pavement from the northbound lanes of Oakland Avenue.

- Short-term crosswalk closures are required as crews remove pavement at intersections
- Short-term driveway closures are expected as crews remove driveway approaches
- Residents are encouraged to remove needed vehicles from driveways and parking lots by 6 a.m.
- Driveway access will be restored by the end of the workday

As the pavement is removed, crews are inspecting and replacing the subgrade as needed.

The **Traffic and Utility Impacts** section of the Oakland Avenue Reconstruction Project website will be updated daily to reflect work areas scheduled for the following day.

Work on Oakland Avenue will pause from noon on Friday, July 3, to 7 a.m. on Monday, July 6 in observance of Independence Day.

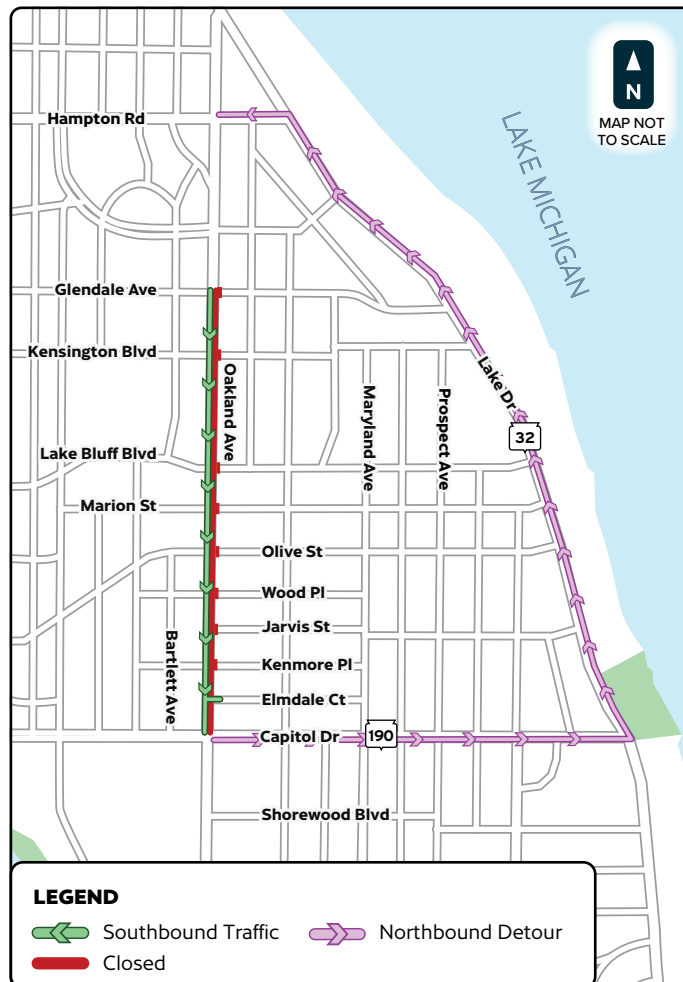

All work is weather dependent and subject to change.

Overnight and Weekend Work:

No overnight or weekend work is scheduled.

Subgrade

The compacted earth serving as a foundation for the base and pavement built on top of it. Poor subgrade materials, such as clay soils, can shorten the lifespan of the finished roadway.

Pavement

Base

Subgrade



Sign Up for Updates

Visit the project website to subscribe for updates.

www.oaklandavereconstruct.com

Project Contact

Public Involvement Team

 (262) 933-0467

 info@oaklandavereconstruct.com

The project team thanks you for your patience and cooperation throughout this project!
