






EquiFlow Wausau Lead-Free Program

Monthly Progress Report

YEAR 2 CONSTRUCTION PROGRESS

(as of June 27, 2025)

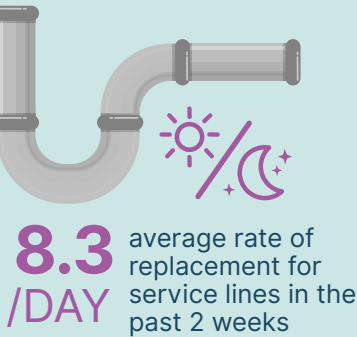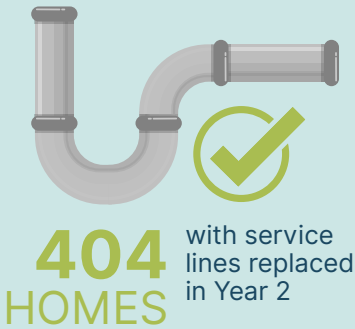


SUMMARY OF LEAD VERIFICATION EFFORTS

(as of June 27, 2025)



SURVEY RESULTS

(as of June 27, 2025)



EquiFlow Wausau Lead-Free Program

Monthly Progress Report

APPRENTICESHIP PROGRAM UPDATE



From June 16–18, EquiFlow hosted a hands-on training for participants in the LSR Apprenticeship Program, in partnership with LIUNA. Trainees gained practical experience in CPR/First Aid, traffic control, and lead service line replacement through both classroom instruction and on-site learning. The session was a key step in preparing them for work in the field.

OUTREACH EVENTS



- **July 11th-12th:** Taste N' Glow Fest
- **July 30th:** CPC Tabling

1,000 LINES REPLACED!

EquiFlow has officially hit 1,000 lead line replacements, marking the halfway point toward our combined Year 1 and Year 2 goal.



JULY CONSTRUCTION

Week of June 30 th	N 7 th Ave, N 10 th Ave
Week of July 7 th	N 8 th Ave, N 6 th Ave, N 9 th Ave
Week of July 14 th	N 8 th Ave, N 6 th Ave, N 1 st Ave
Week of July 21 st	N 8 th Ave, N 9 th Ave
Week of July 28 th	N 9 th Ave
