


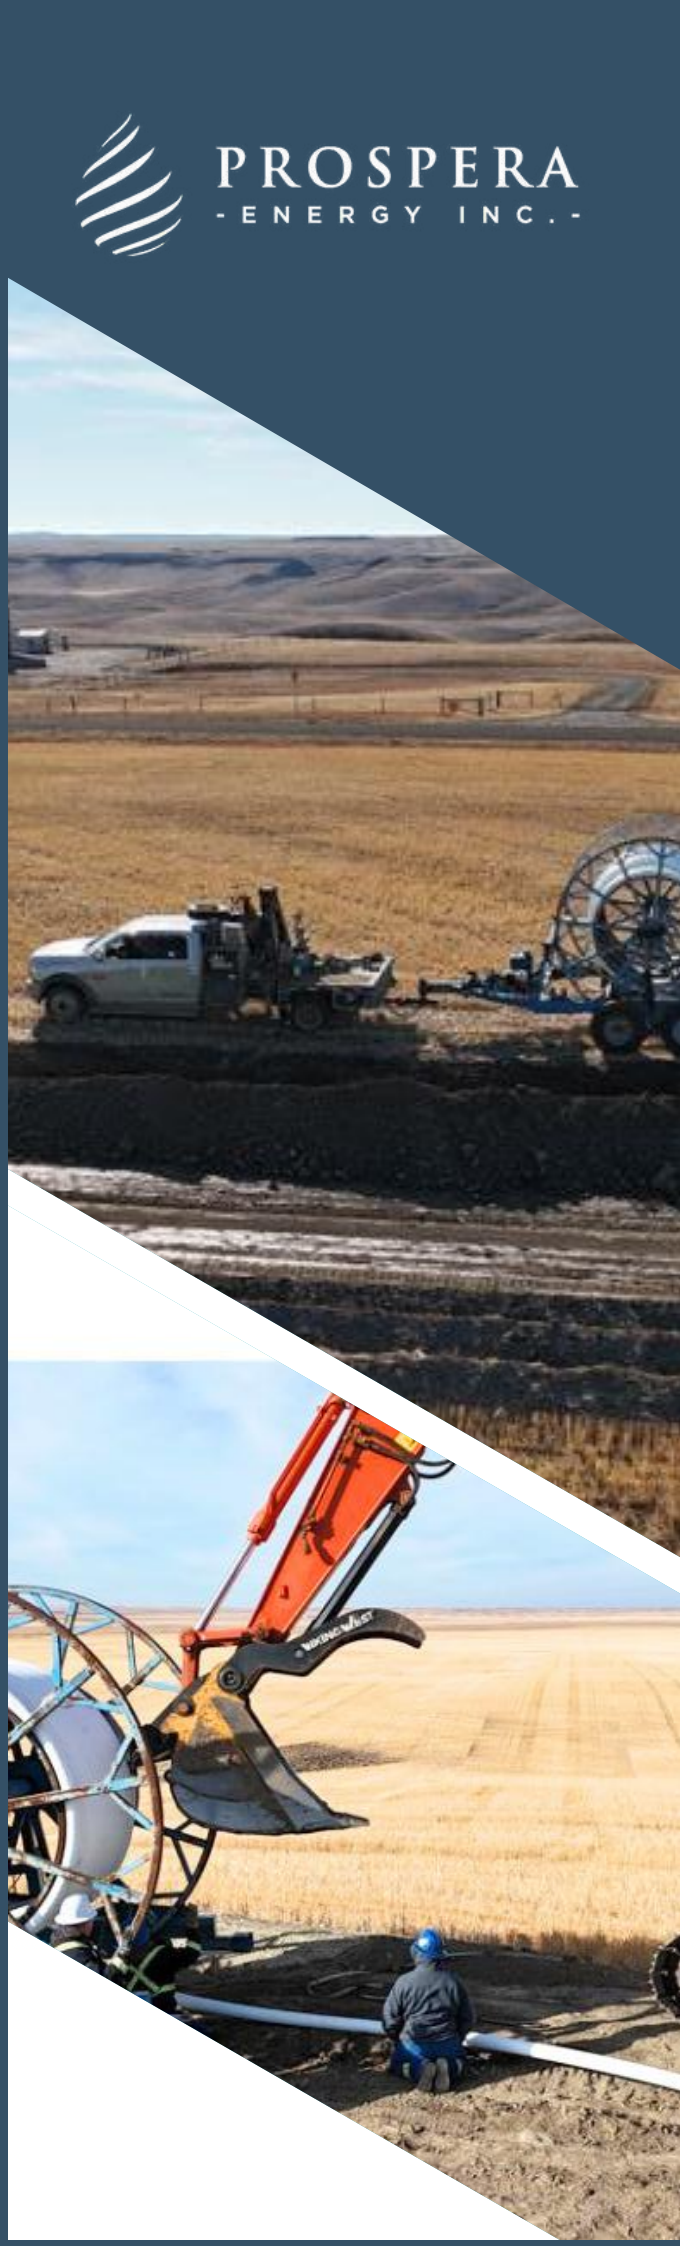

Workover Tracker & Key Wells Report

Legacy Fields.
Modern Solutions.

TSX.V: PEI, OTC: GXRFF

November 2025

Workover Tracker & Key Wells Report

November 2025

	Nov-24	Dec-24	Jan-25	Feb-25	Mar-25	Apr-25	May-25	Jun-25	Jul-25	Aug-25	Sept-2025	Oct-2025
WTI Benchmark Price (\$US/bbl)	69.95	70.12	75.74	71.53	68.24	63.54	62.17	68.17	68.39	64.86	63.96	60.89
WCS Heavy Oil (\$US/bbl)	57.56	57.76	62.86	59.07	54.38	50.83	51.57	58.22	58.31	53.70	51.63	48.62
Sales Revenue (\$)	1,285,795	1,470,665	1,723,046	1,335,500	1,640,941	1,429,757	1,722,240	1,770,689	1,838,798	1,713,265	1,863,619	1,354,078
Production Corporate (boe/d) Oil %	561 95	610 93	644 92	591 92	716 93	730 93	814 93	846 96	859 97	775 97	823 93	780 93
Cuthbert (boe/d) Oil %	322 100	309 100	292 100	329 100	338 100	340 100	333 100	351 100	356 100	295 100	278 100	270 100
Luseland (boe/d) Oil %	54 100	77 100	104 100	67 100	106 100	86 100	161 100	171 100	193 100	217 99	235 98	235 97
Hearts Hill (boe/d) Oil %	142 91	157 90	129 88	111 86	161 88	215 88	230 88	252 89	230 90	202 90	182 88	155 90
Alberta (boe/d) Oil %	44 63	67 70	120 68	84 74	111 77	89 76	89 76	73 69	81 94	61 100	128 77	121 75
Corporate Oil Inventory (bbls)	11,553	12,017	14,418	15,788	16,477	18,696	16,769	16,766	18,766	19,105	19,037	20,036

Luseland Production



Hearts Hill Production



Cuthbert Production





Luseland



10-07 well producing steadily for 140+ days now, currently at 100 RPM with 5 JOF (Joints of Fluid) optimization potential. Casing pressure holding steady at 30 PSI.




10-08 well consistently at 15-20 bbls/d. It has produced steadily for 240 days with solid sand production and numerous RPM increases resulting in higher oil production and drop in water cuts. Monitoring closely and will speed-up again upon further stable performance.




01-17 well with constant production profile in the last 8 months with close monitoring. This well sits against the updip erosional edge of Luseland pool and continues to produce at a very low water cut generating exceptional netbacks.



12-17 well, one of our latest reactivations now with 120 days online with sand slugging action. Recycle pump has been installed and is currently under steadily increasing daily hot oil injection with concurrent well speed-ups.

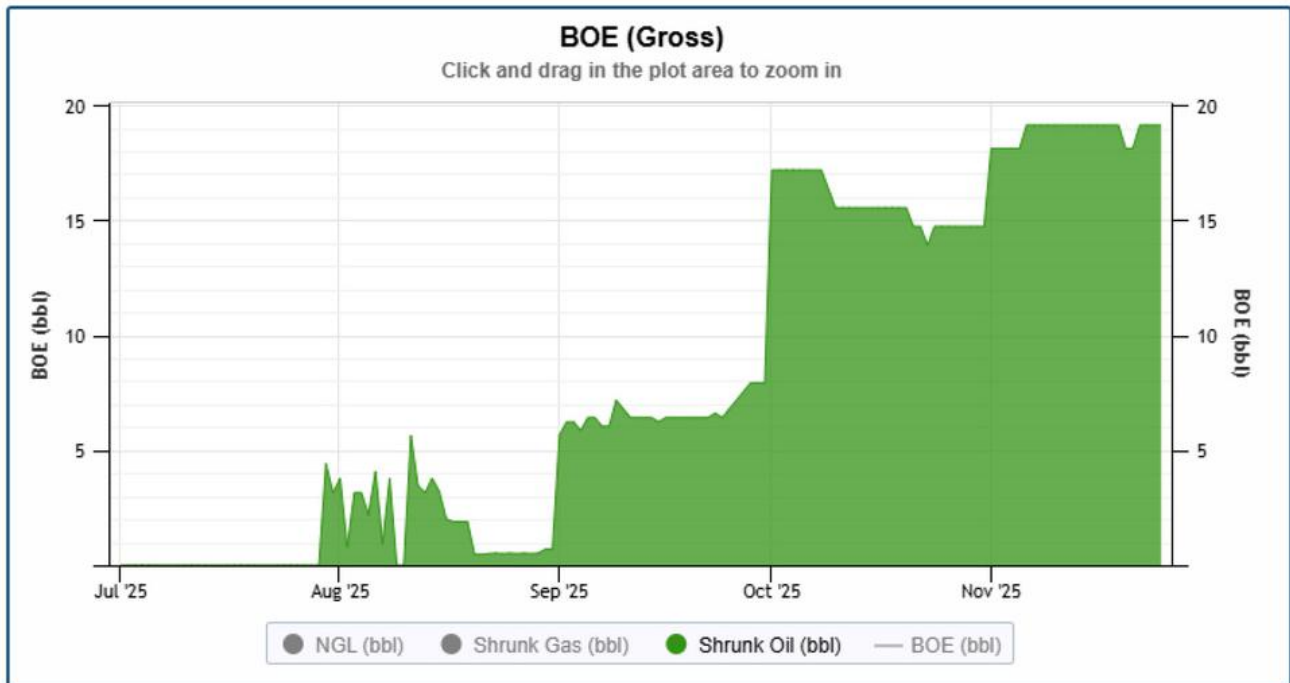


16-07 well, with 8 speed-ups complete and successfully chasing fluid level in order to get to increased reservoir oil. Continues bringing major sand up the wellbore through recycle pump setup and hot oil injection. These production graphs include reservoir oil only, and do not show recycle pump oil injection + production of 5 m3/d which brings sand with it.

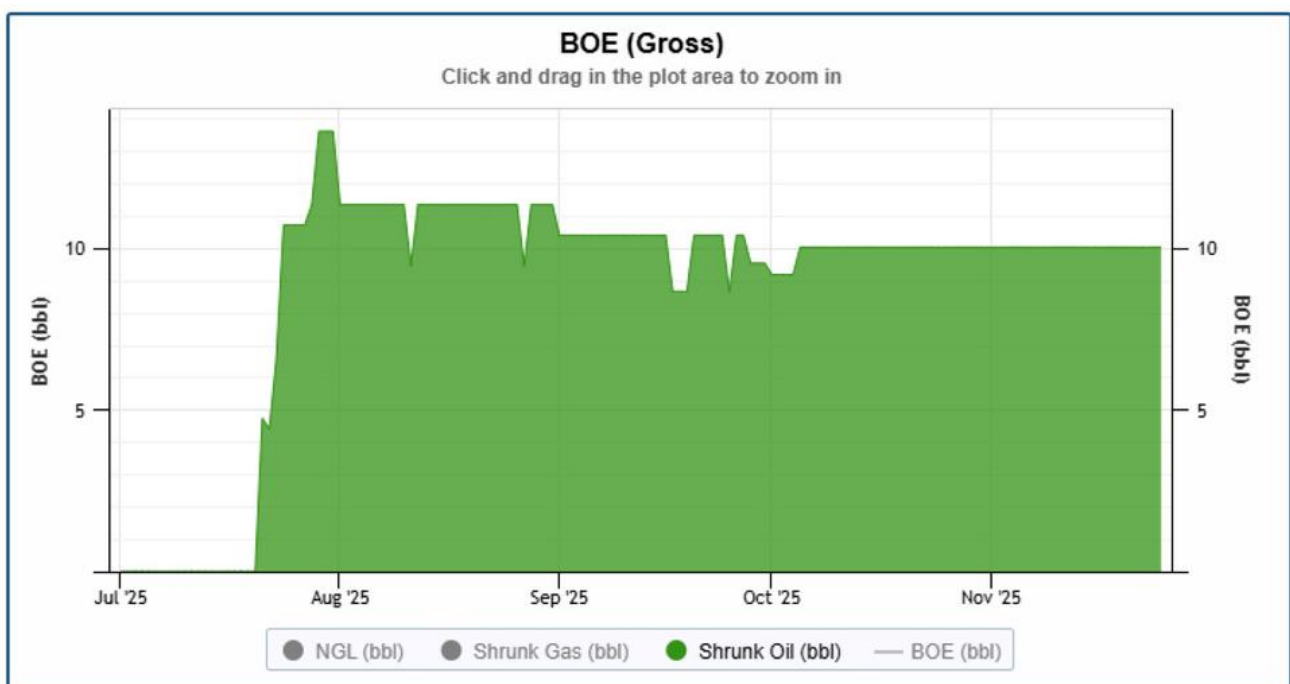




10-18 well, one of our latest reactivations with solid stable production over first 120 days. Section 18 contains numerous high-reliability, high-netback wells.

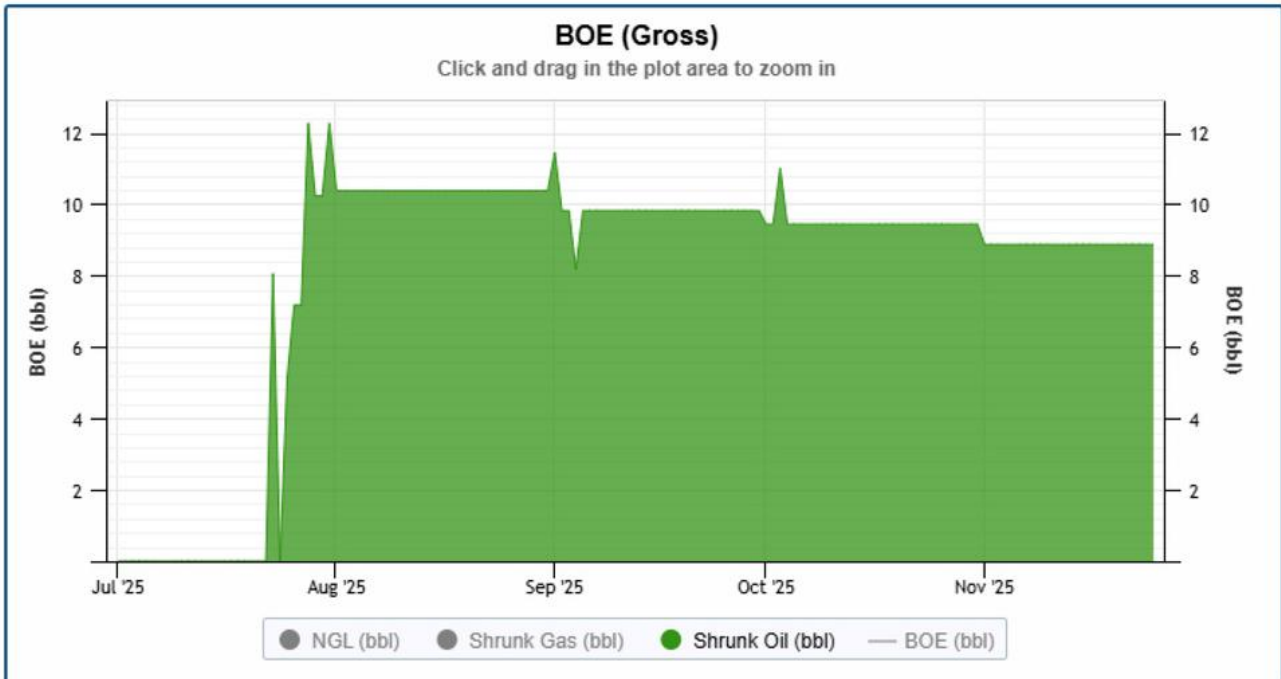


11-18 well, one of our latest reactivations with solid stable production over first 120 days. Section 18 contains numerous high-reliability, high-netback wells.

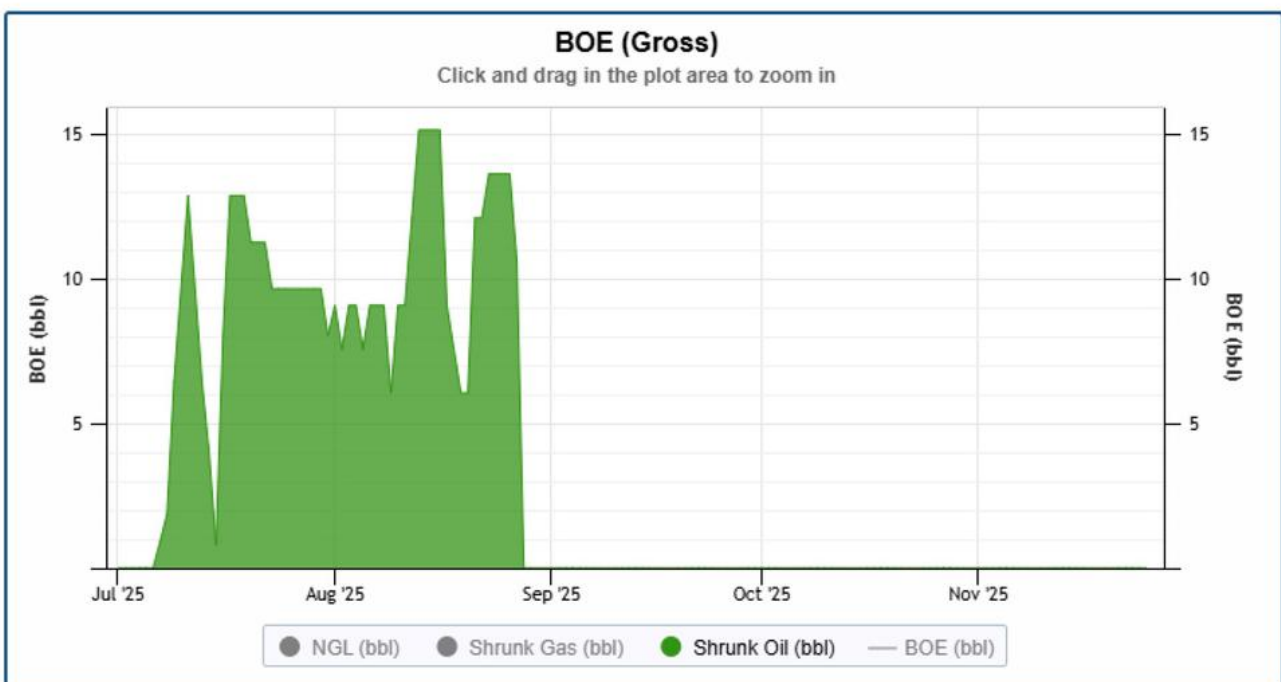


16-05 proof-of-concept well, this area of the reservoir considered to be depleted was brought online after 15 years offline and was producing strongly with consistent 3-15%



sand cuts. Workover completed Nov 25th, some high-impact wells will require multiple workovers for sand cleanout before they will produce in stable profile.

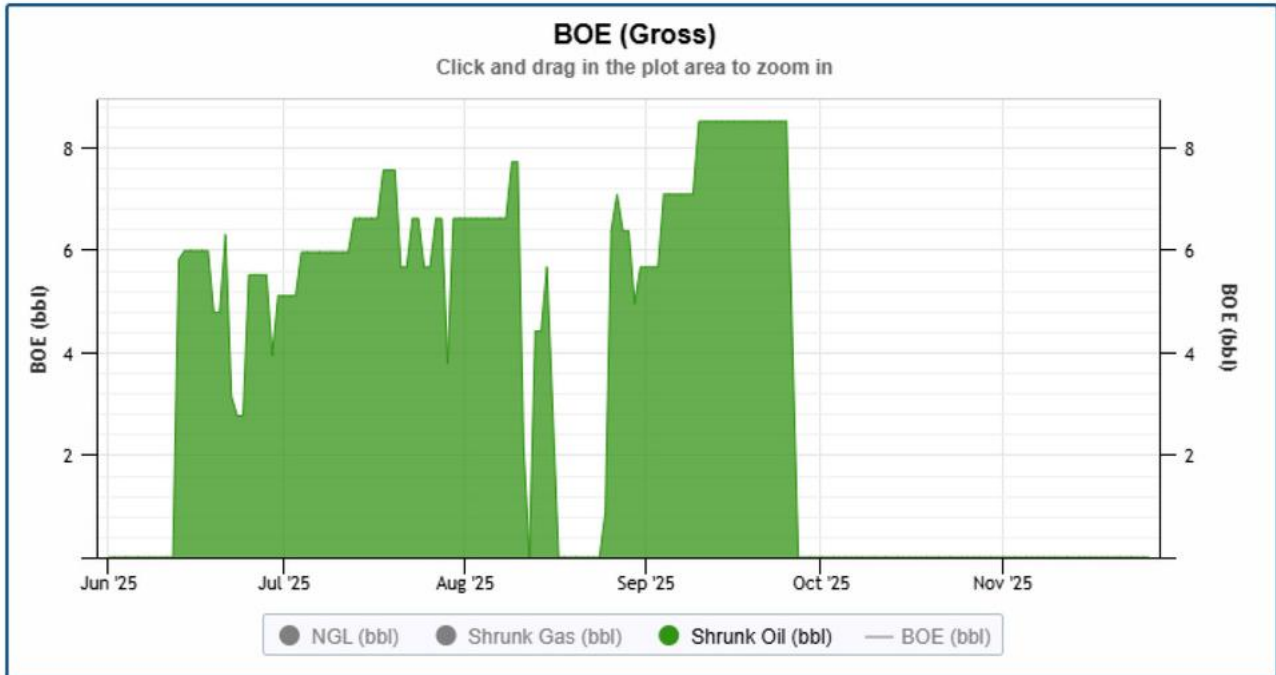

02-33 well, one of our focus wells in Section 33 which is currently at 3% Recovery Factor. Previous attempts to run this well have caused major sand influx, so an enhanced recycle pump and sand suspension chemical setup were installed, service rig on well Nov 27th.

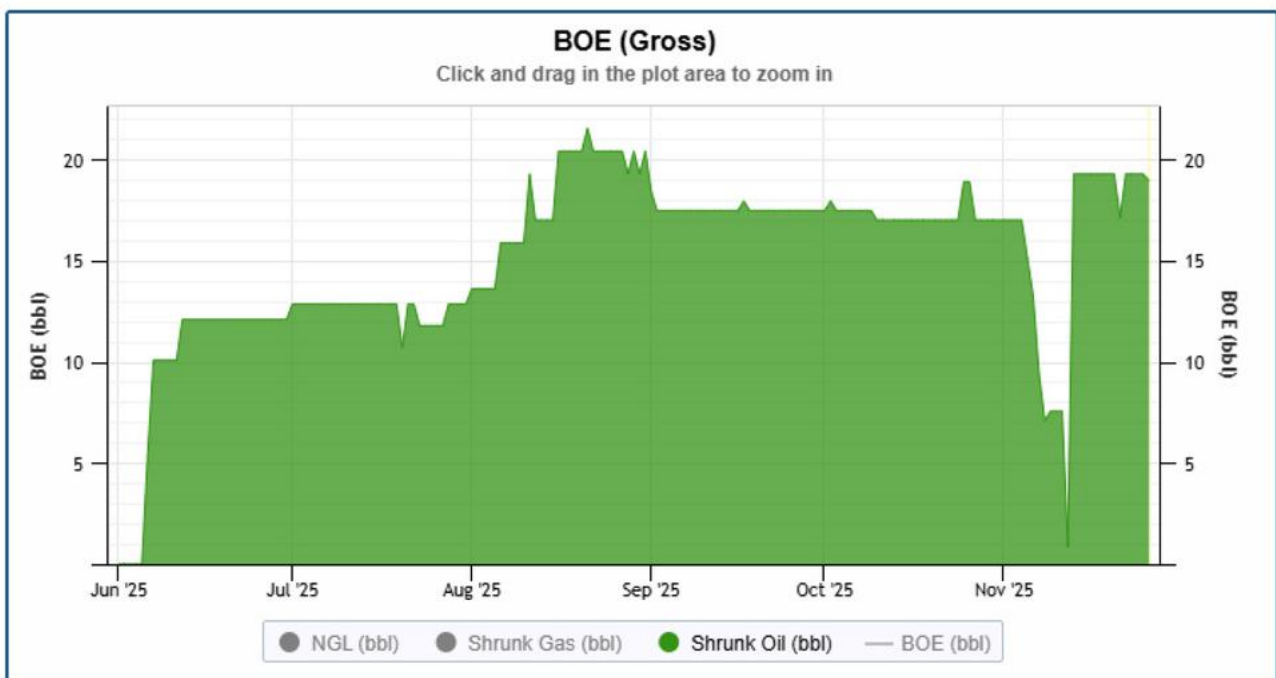





07-33 well, one of our focus wells in Section 33 which is currently at 3% Recovery Factor. Previous attempts to run this well have caused major sand influx, so an enhanced recycle pump and sand suspension chemical setup were installed. Monitoring well at these rates with 5 JOF and 2-3% sand cuts. Successful superflush complete in mid-November.




15-04 well with steady production over first 240+ days since reactivation with major sand slugging and consistent cleanouts.

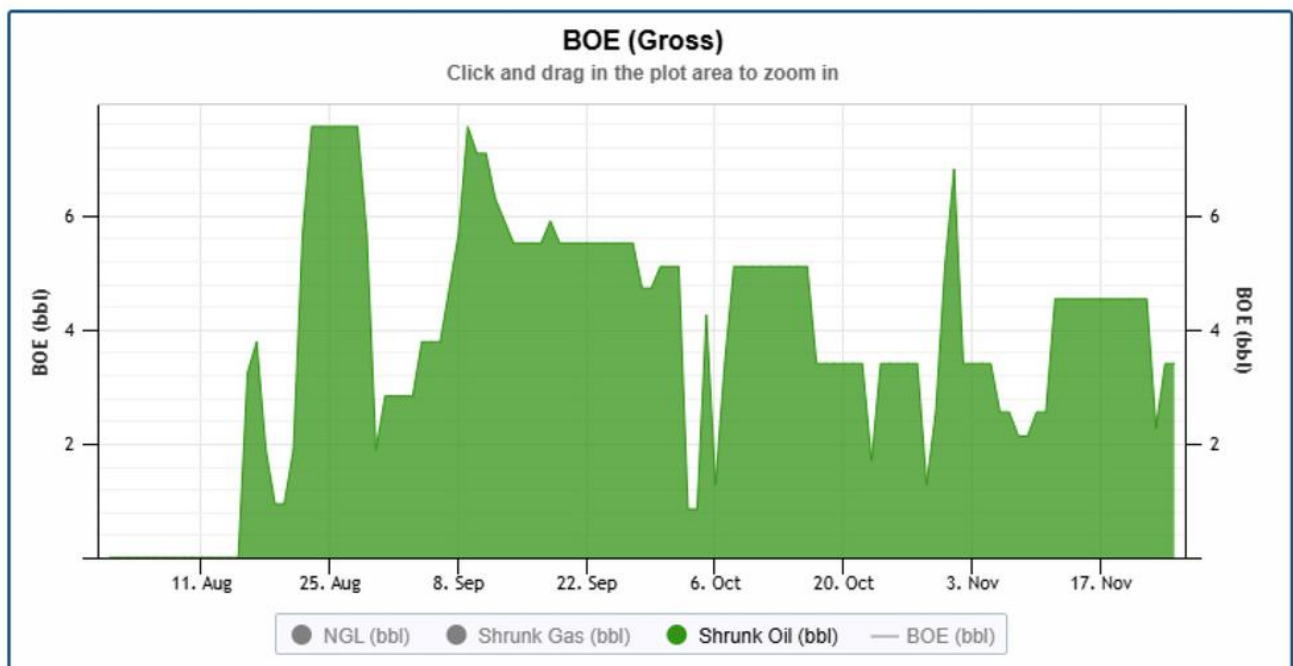

16-08 proof-of-concept well which had not produced more than 2 m3/d total fluid in its last 17 years online. Installed recycle pump to bring sand up wellbore and getting >20% sand cuts at times initiating wormhole development and potential for major EUR increase.

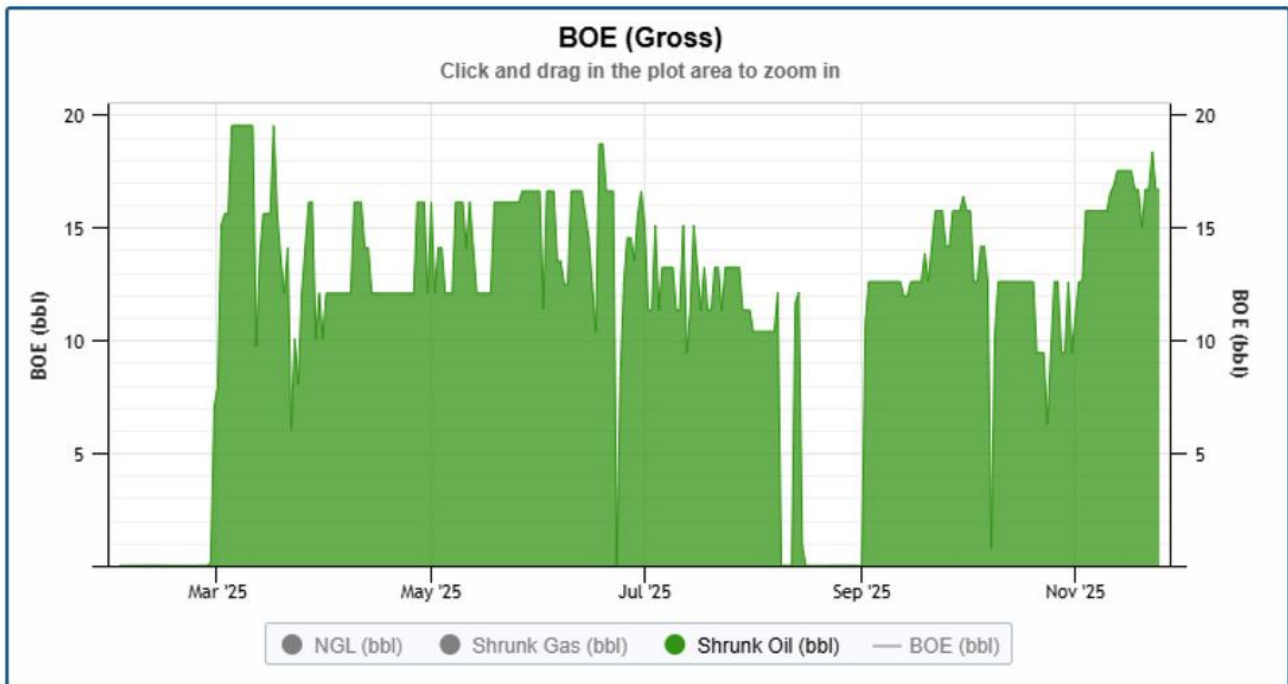


03-09 back online after service rig cleanout job, installed recycle pump and sand suspension chemical. Bigger 8-1500 SN1 CHOPS pump was installed after workover allowing for higher fluid production and showing higher oil production and oil cuts after recent speed-up

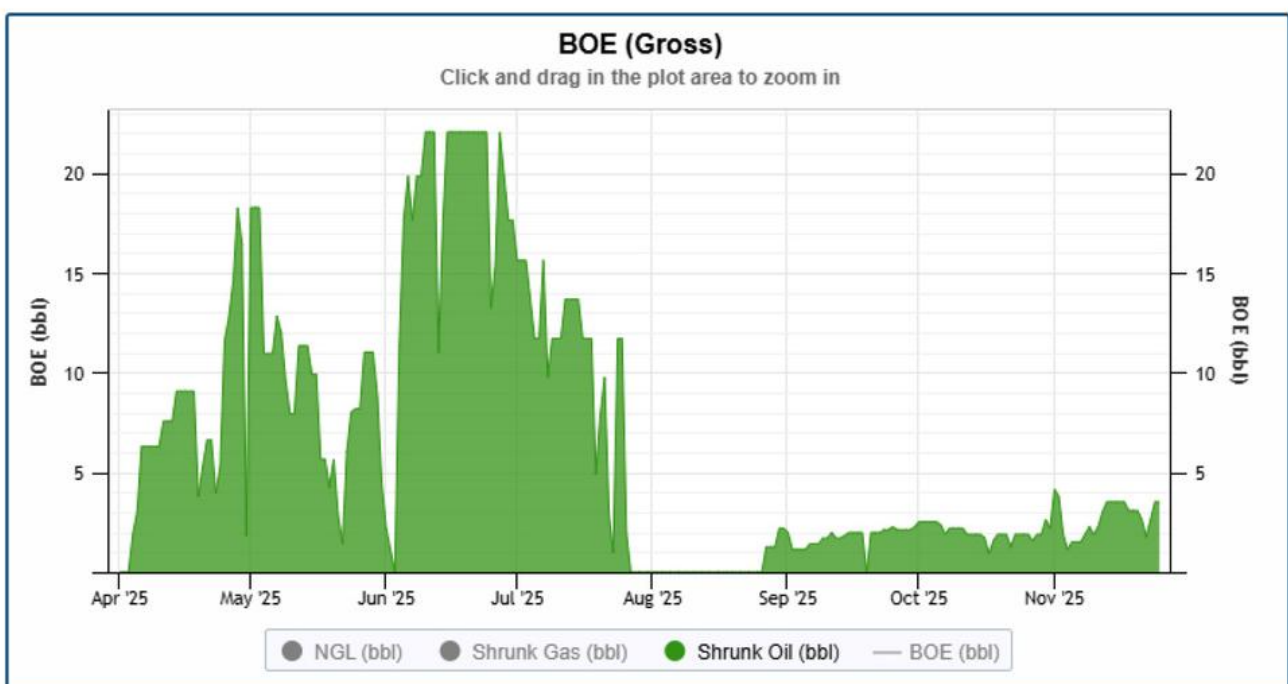


04-33 with installed recycle pump and sand suspension chemical. Bigger 13-1200 SN1 CHOPS pump was installed after workover allowing for higher fluid production with significantly slower ramp-up process to allow sand production. Consistent 3-5% sand production and currently at 10 JOF allowing for significant optimization potential.


Cuthbert

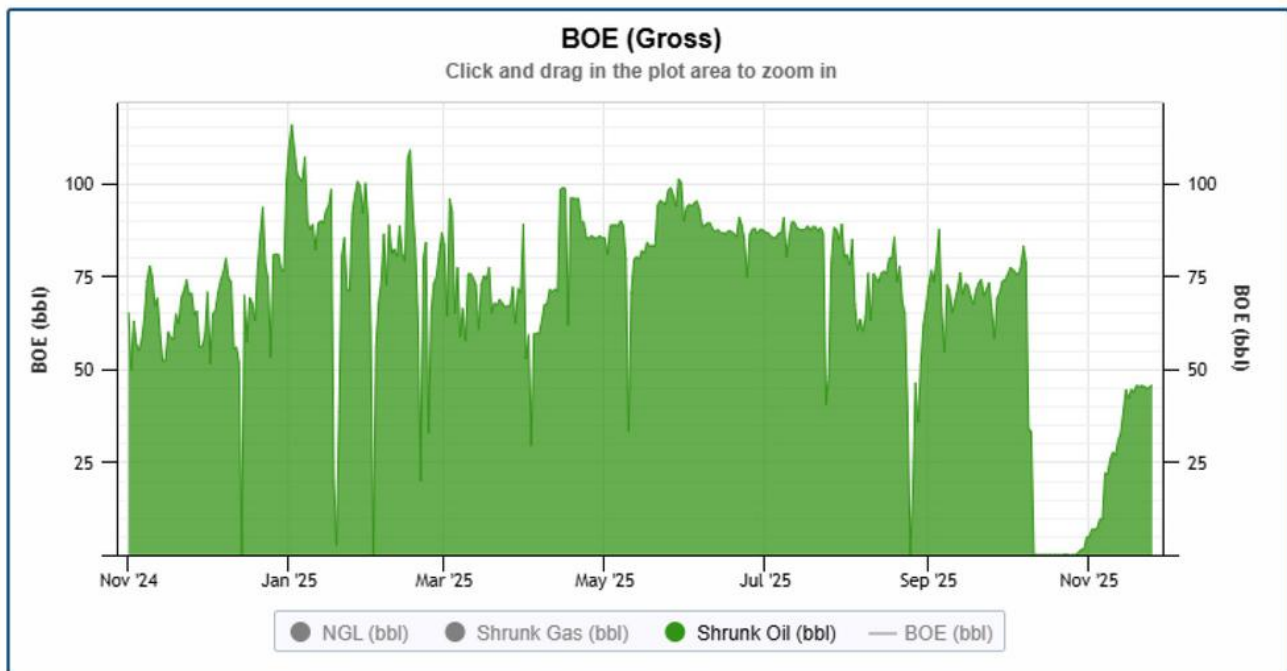


05-27 HZ well optimized through speed-ups, waterflood management, and continuous water-cut monitoring. This well has now paid out 2x in less than 24 months since drilling and enhanced with service rig job in October to completely cleanout sand and debris from horizontal section of well.

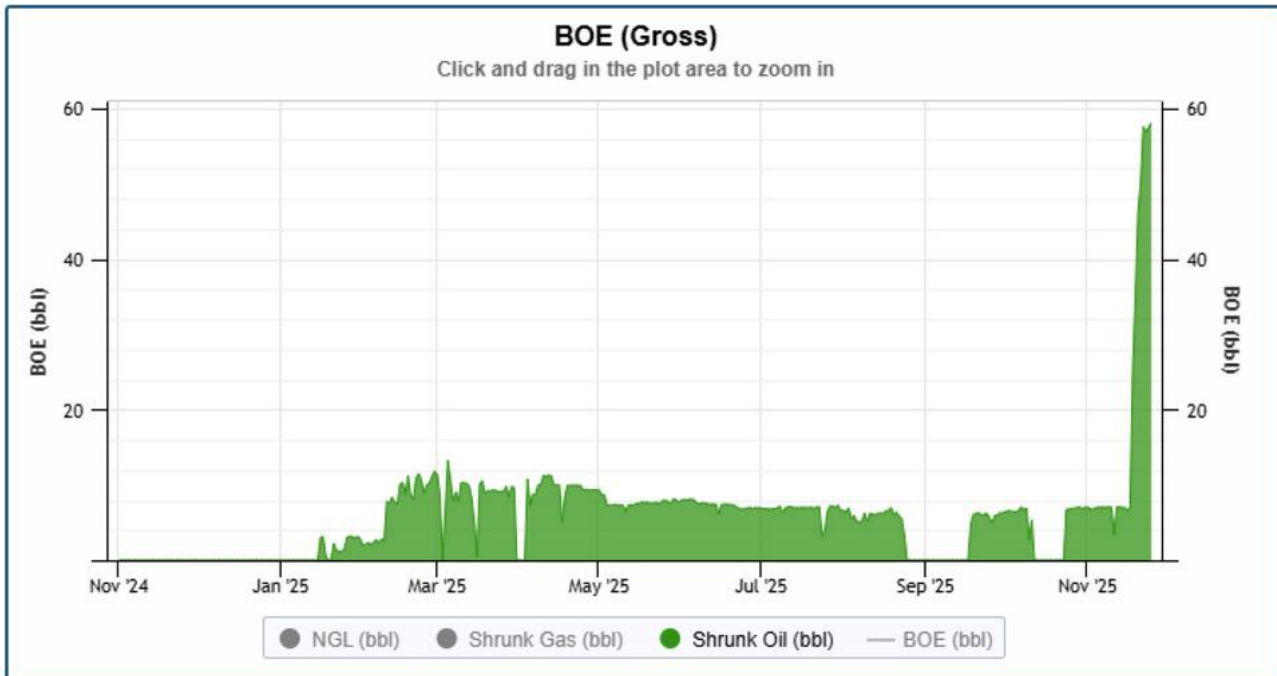


11/08-02 performing strongly with massive increase in oil rate after completion of Cuthbert pipeline replacement project allowing for effective waterflood optimization.

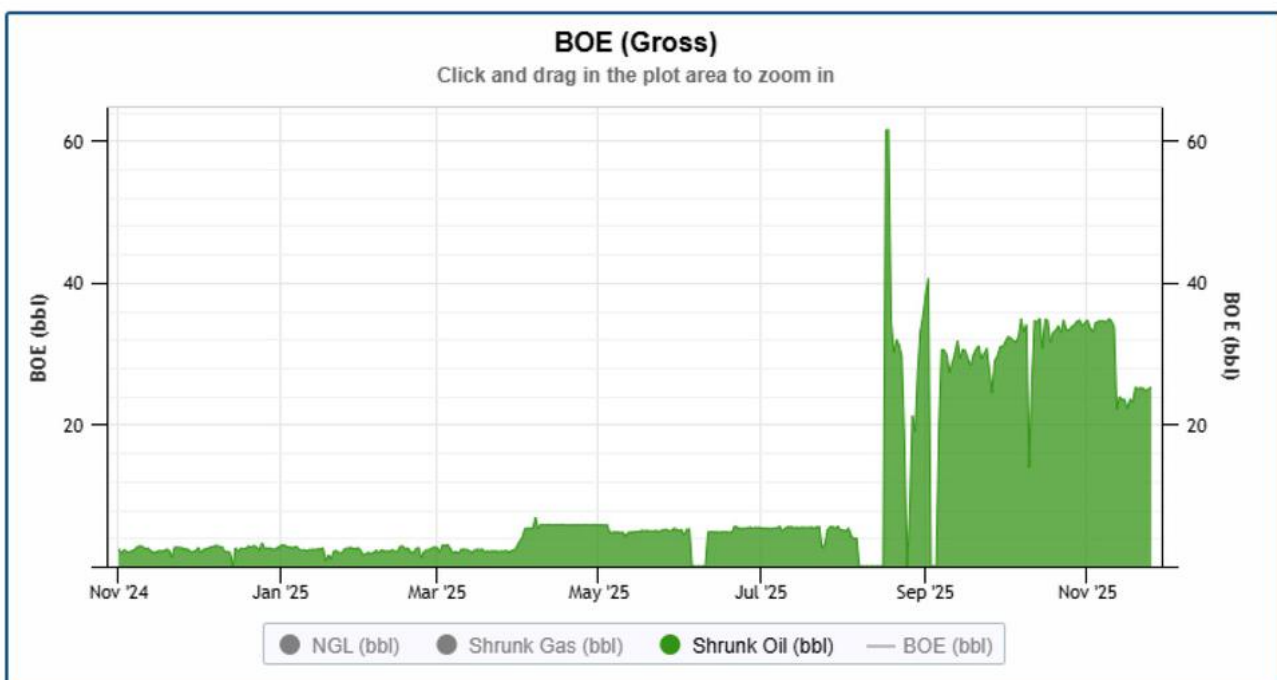


01/08-02 HZ with bridge plug installed to shut-off water and then perforated 35 meters in heel section to access oil reservoir. 40+ JOF of optimization room remains and is incrementally being accessed through speed-ups.

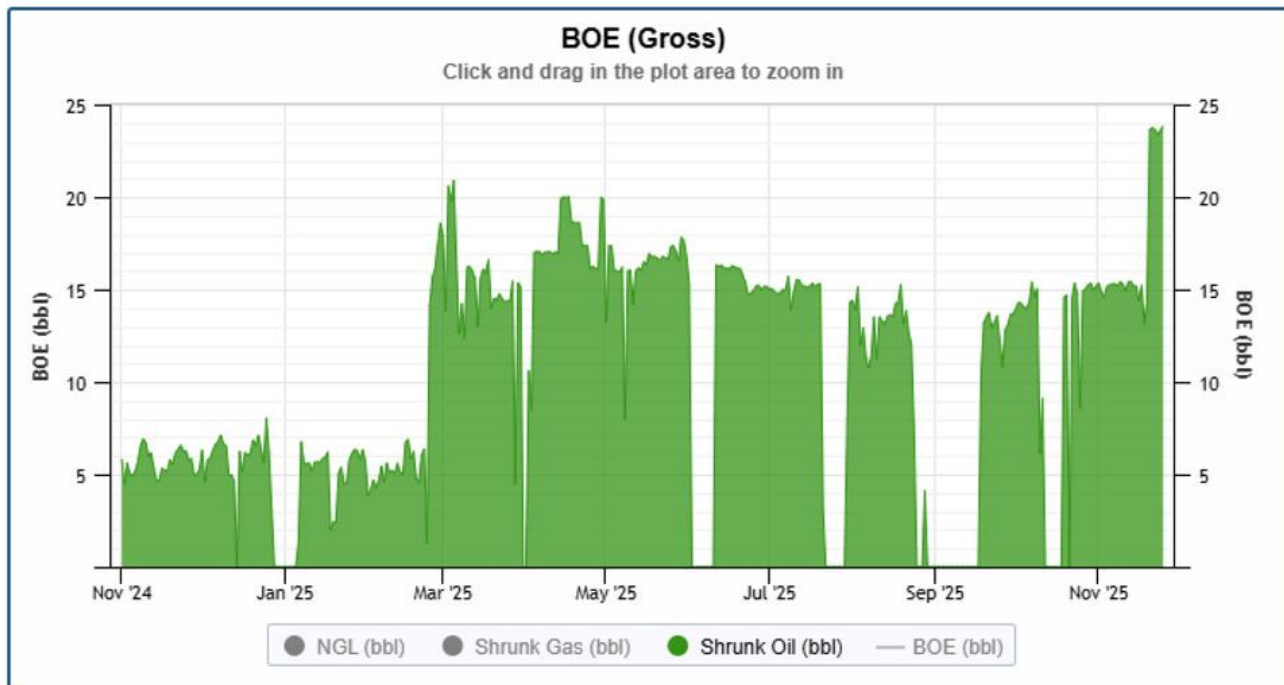

03-02 well with significantly increased production after waterflood pattern change and well speed-up to 3x RPM.

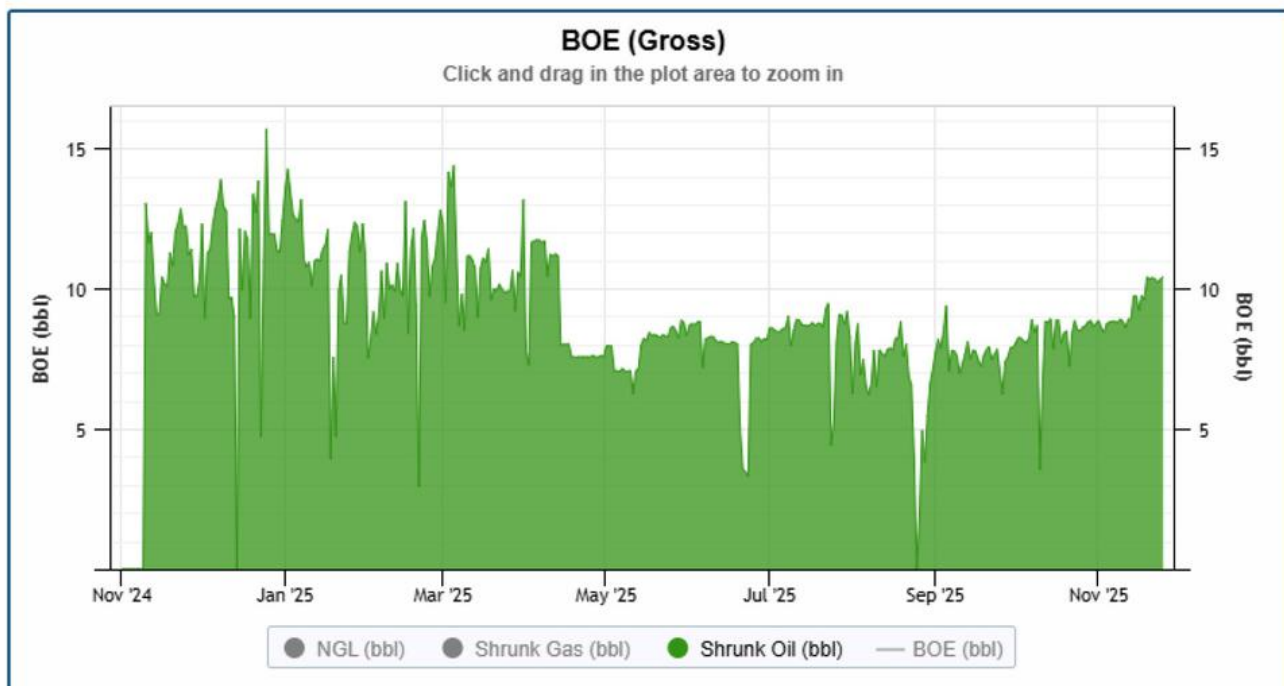


11-28 well with production rising steadily after completion of Cuthbert pipeline replacement project.

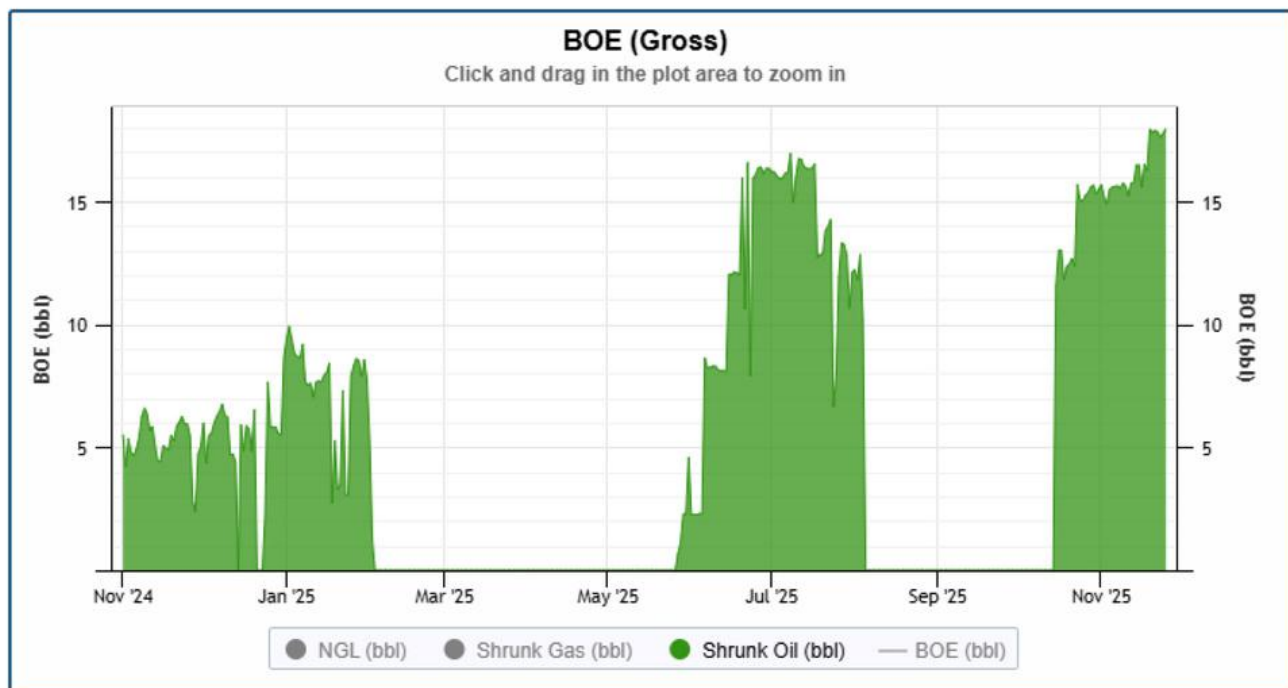

02-28 well with production rising steadily after completion of Cuthbert pipeline replacement project.

Hearts Hill

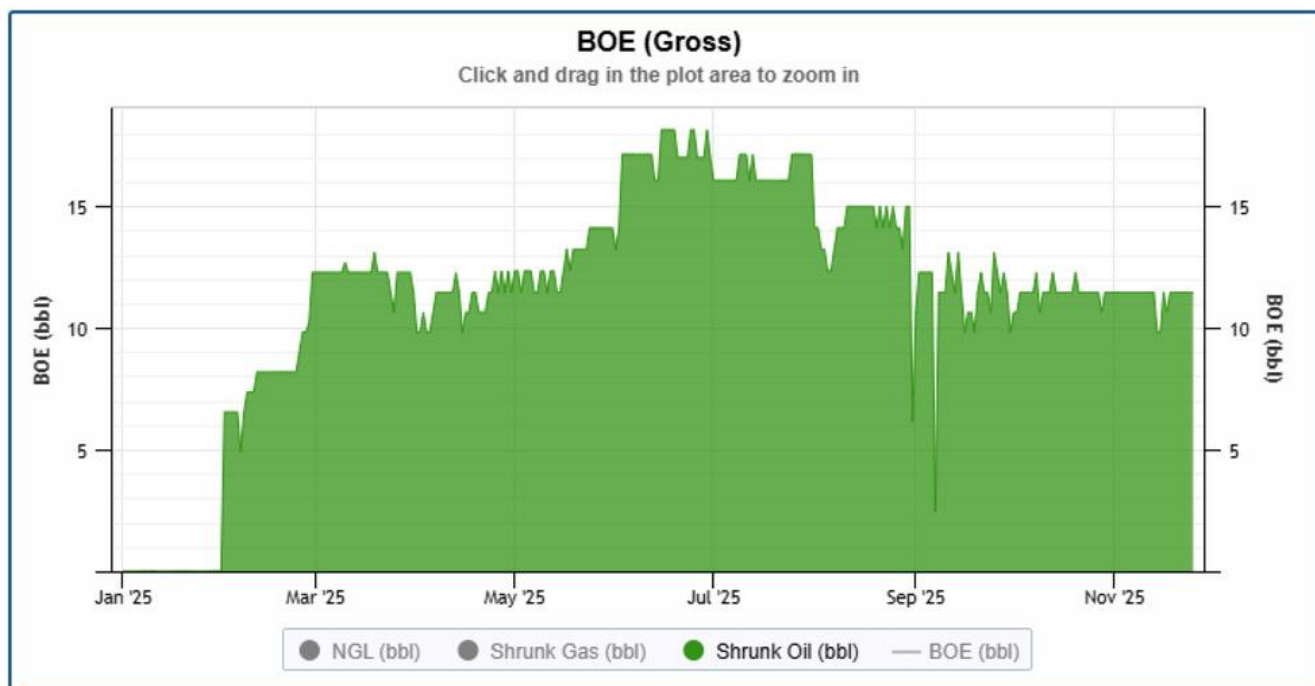


04-34 well reactivated after 4 years offline. Optimizing through speed-ups as production stabilizes and accessing bank oil at reservoir edge.

*Legacy Fields.
Modern Solutions.*



PROSPERA
- E N E R G Y I N C . -

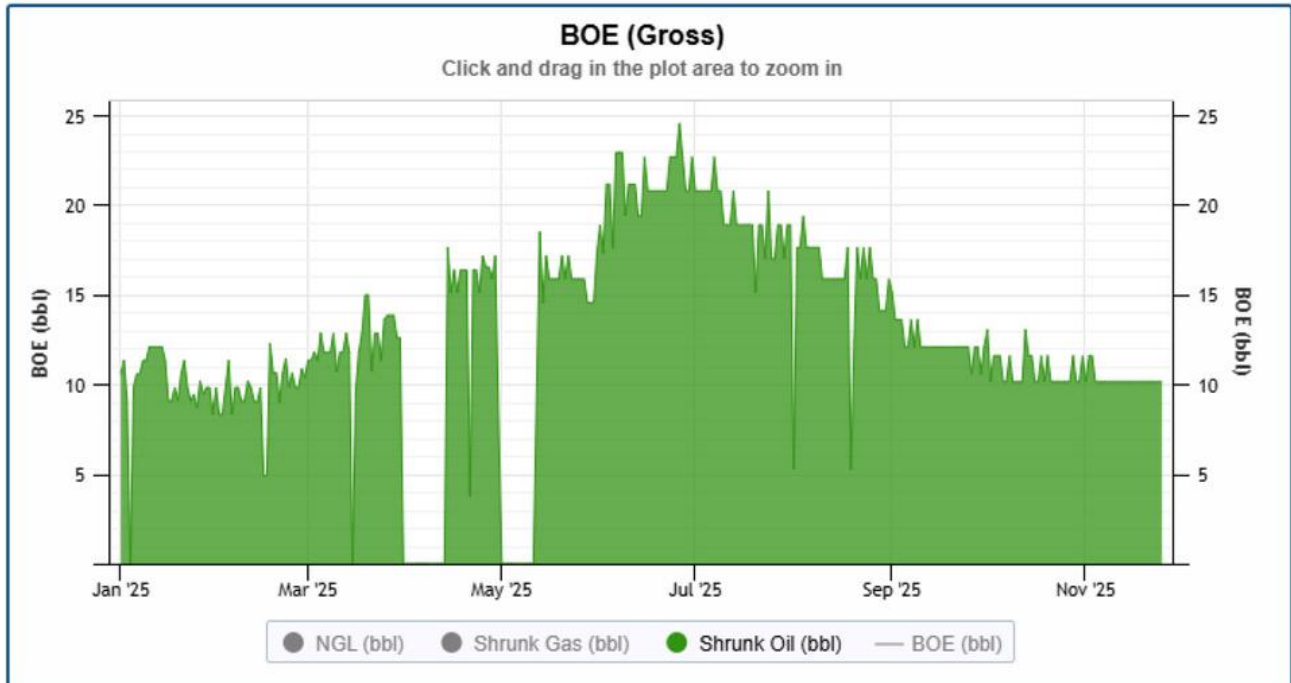

03-30 well, optimized through reduced water injection into nearby wells and slowing down RPM of well thus significantly increasing netbacks.



Legacy Fields Modern Solutions •

Prospera Energy Inc.
Suite 730, 444 - 7th Ave SW
Calgary, AB
T2P 0X8 Canada

prosperaenergy.com



PROSPERA
- ENERGY INC. -
