



**Marine Safety Center Vapor Control System (VCS)  
Plan Review Information Sheet (PRIS)**



Vessel Name		Shipyard	Jeffboat
Official Number		Hull Number	03-2972 & 03-2977

1. This sheet consolidates critical VCS parameters for MSC Staff Engineers and CG Field Inspectors dealing with Vapor Control Systems. CG Inspectors should verify the vessel's VCS design is consistent with the information listed in boxes 2, 6, 7 & 8 prior to updating the vapor control endorsement on the vessel's Certificate of Inspection. For cases where the information in the VCS PRIS does not reflect the vessel's design the CG Inspector should contact the MSC's Cargo Authority branch.

2. Tank Maximum Design Working Pressure	<input type="text" value="3.20"/>	psig	Raised Trunk	<input checked="" type="checkbox"/>
			Flush Deck	<input type="checkbox"/>
3. Authorized Maximum Cargo Transfer Rate	<input type="text" value="4285"/>	bbl/hr		
4. Authorized Maximum Cargo Vapor Density	<input type="text" value="0.247"/>	lbm/ft <sup>3</sup>		

5. Cargoes with the highest vapor density and/or pressure drop:

a. Cargo Name Dodecylbenzene

b. Cargo Name Gasoline

6. Pressure Vacuum Valve:			
Manufacturer	<input type="text" value="Bergen KLPH -6"/>	Settings in psig:	
Size	<input type="text" value="6 Inch"/>	Pressure-side	<input type="text" value="3"/>
CG Approval	<input type="text" value="Yes"/>	Vacuum-side	<input type="text" value="0.5"/>
Required Venting Capacity of Pressure-Side of P/V valve		<input type="text" value="9191"/>	bbl/hr (air)
Required Venting Capacity of Vacuum-Side of P/V valve		<input type="text" value="4285"/>	bbl/hr (air)

7. Tank Overfill Protection System (check appropriate box or boxes)			
a. High Level/Tank Overfill Alarm	<input checked="" type="checkbox"/>	Type	<input type="text" value="0"/>
b. Overfill Control Shutdown	<input checked="" type="checkbox"/>	Type	<input type="text" value="0"/>
c. Spill Valve	<input type="checkbox"/>	Type	<input type="text" value="0"/>
d. Rupture Disk	<input type="checkbox"/>	Type	<input type="text" value="0"/>
			Setting in psig <input type="text" value="N/A"/>
			Meets ASTM F1271

8. Closed Gauging Verify the vessel has closed gauging that satisfies 46 CFR 39.20-3 and 151.15-10(c).

9. Instructions/Guidelines for the OCMI:

9a. The following is the Marine Safety Center's recommended COI endorsement

"Only those cargoes named in the vessel's Cargo Authority Attachment, Serial #C1-0304452, dated 25Mar03, may be carried and then only in the tanks indicated. In accordance with 46 CFR Part 39, excluding part 39.40, this vessel's vapor control system has been inspected to the plans approved by Marine Safety Center letters Serial # C2-0203101 dated 12Sep02 and C1-0304452 dated 25Mar03, and found acceptable for collection of bulk liquid cargo vapors annotated with "Yes" in the CAA's VCS column."

9b. The Marine Safety Center approval letter/s must be available at the OCMI's request.


9c. Verify isolation valve at the vapor connection flange is manually operable and designed in a way it is "clearly" open or closed.

9d. Previous applicable VCS approval letters:

VCS Approval Letter  MSC Plan Reviewer

CBC 90 thru CBC 99  
03-2972 to 03-2977 and 03-2990 to 03-2993  
CBC 124 thru CBC 131  
01-2746 TO 01-2751, 02-2965, 02-2966  
4,285 BBL/HR MAX TRANSFER RATE

### PRESSURE DROP IN VCS PIPING

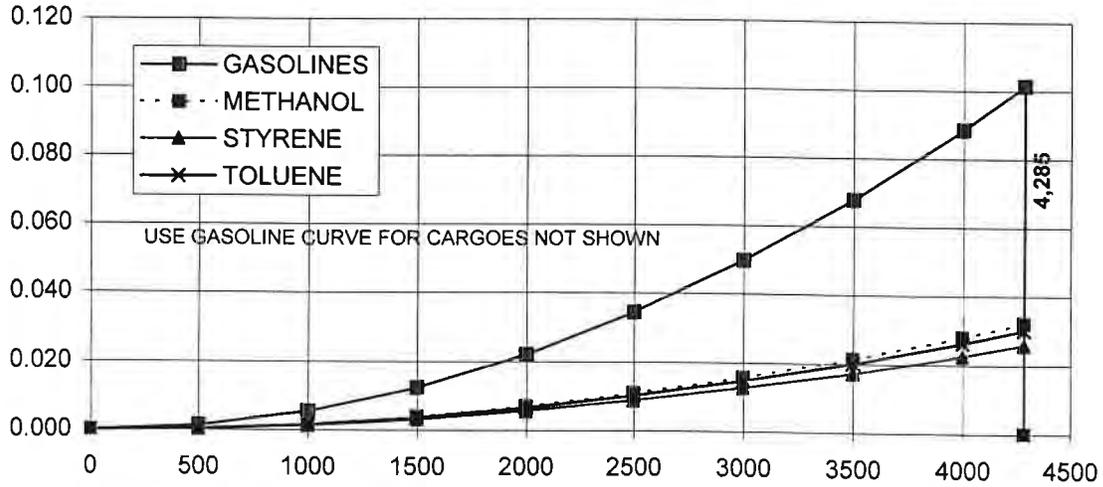

### LIQUID TRANSFER RATE VS FACILITY VAPOR CONNECTION PRESSURE

