

**VESSEL
REPAIR
CONSTRUCTION**

5848 Proctor Street
Port Arthur, TX 77642
409.962.1302

PIPELINE TEST REPORT

The following vessel's pipeline has been tested and stenciled in accordance with U.S.C.G. regulation 33 CFR 156.170 on the dates indicated:

Vessel Name: CBC-385

Vessel Owner: Canal Barge Company

Date of Test: 7/24/26

Test Pressure: 188 psi.

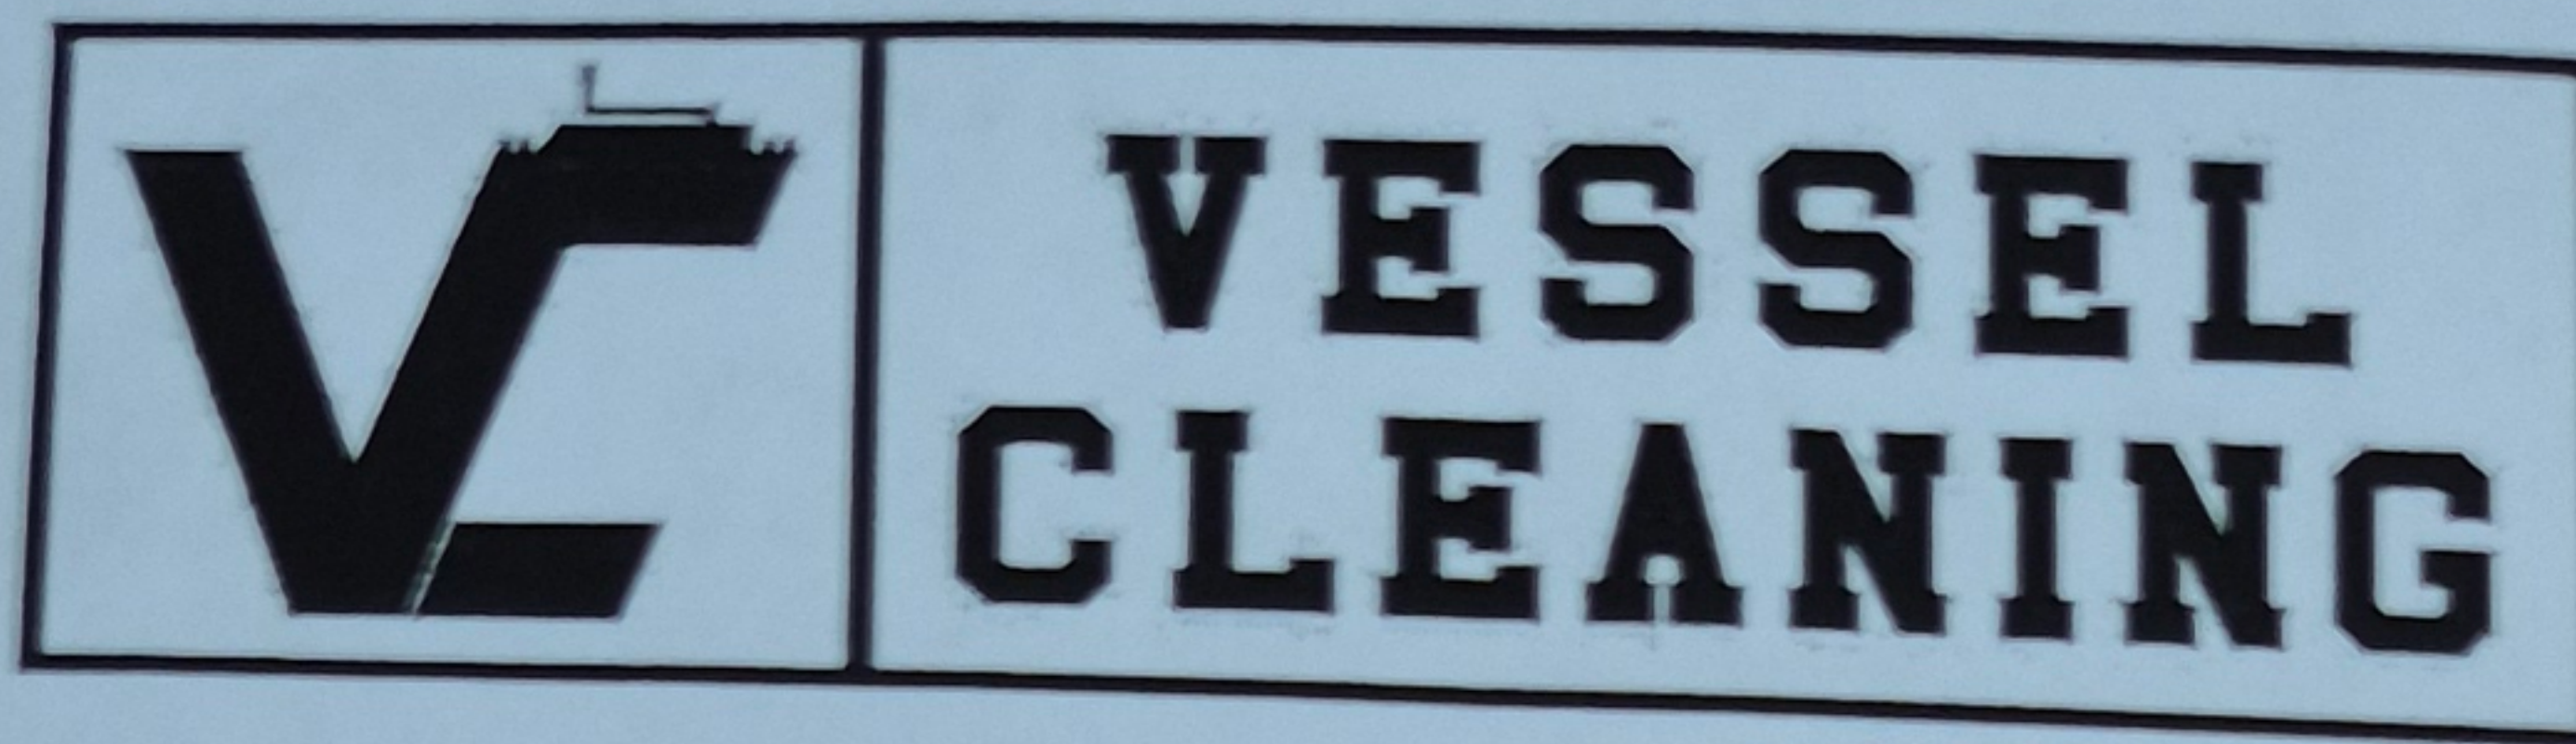
Name of Tester: Kurt Moerbe

Tester Signature:

Name of Witness:

Wes Broussard

Witness Signature:



5848B Proctor Street
Port Arthur, TX 77642
409.962.1302

HYDROSTATIC PIPELINE TEST REPORT

The following vessel's pipeline has been tested and stenciled in accordance with U.S.C.G. regulation 33 CFR 156.170 on the dates indicated:

Vessel Name: CBC 385
Vessel Owner: Canal Barge Co
Date of Test: 2/3/20
Test Pressure: 188 psi M.A.W.P 125 psi
Name of Tester: Jesus Trejo
Tester Signature: Jesus Trejo
Name of Witness: Cassie White
Witness Signature: Cassie White

TEST RESULTS

This barge has been tested in accordance with section 156.170 and is considered to be vapor-tight.

Pump Psi Relief Tested: _____

Cargo Dummy Line Tested: _____

Starting Pressure: 28"

Test Time: 1500

Ending Pressure: 28"



Cargo Piping Test Letter

Note: Test results are valid for (1) year from date of test!

Date:	<u>4/8/2025</u>	M.A.W.P.	<u>125</u>
Vessel:	<u>CBC 385</u>	Method of Test:	<u>Hydro</u>
Owner:	<u>Canal Barge Company</u>	Testing Location:	<u>VLS Marine Services Inc.</u>
Address:	<u>1801 Engineers Rd</u>	Physical Address:	<u>8700 Old Yacht Club Rd</u>
	<u>Belle Chase, LA 70037</u>		<u>Port Arthur, TX 77642</u>

TRANSFER SYSTEM TESTING DATA



**** Fill out completely. Write N/A on any non-applicable line. ****

Date:	Barge Piping:	Results	Note:
<u>4/8/2025</u>	<u>Cargo Pipeline</u>	<u>187.5</u> p.s.i	
<u>4/8/2025</u>	<u>Cargo pressure gauges</u>	<u>98</u> % accurate	
<u>N/A</u>	<u>Steam System</u>	<u>125</u> p.s.i	

Note: Test each pressure gauges annually, accurate within 10 percent. Test each remote controlled operating or indicating equipment such as remotely operated valve, tank alarm, or emergency shutdown device. 33 CFR 156.170(c)(2) & 46 CFR 35.35-70(b)

SIGNATURES

I credit that the tests contained herein were conducted in compliance with 33 CFR 156.170, 46 CFR 35.35-70.

Tester name: Charles Johnson
Tester signature: 
Witnessing inspector name: Tosha Mckusker
Witnessing inspector signature: 
Witnessing inspector affiliation: VLS



Move with confidence

Cargo Pipeline Test and/or Vapor Tightness Test Certificate

Barge Name: CBC 385

Test Date: 5/17/24

Testing Location: IMT Lemont Shipyard

Barge Vapor Tightness Test

Test Results

This barge has been tested in accordance to section 40 CFR 61.304(f), and section 63.565(c)(1) and is considered to be vapor tight.

Signature of Tester: [Signature]

Test Time Started: 0900

Test Time Completed: 1000

Beginning Pressure: 1 psi

Ending Pressure: 1 psi

Operational Cargo Pipeline Test

The following test(s) have been performed in compliance with U.S. Coast Guard regulations 33 CFR 156.170 and 46 CFR 35.35-70 and USCG Marine Safety Manual, Vol. II, Section B, Page B6-30.

Transfer System Piping	Test Pressure	125 psi
Cargo Pump Relief Valve	Test Pressure	125 psi
Cargo Pump Pressure Gauge(s)	Test Pressure	125 psi

IMT Lemont Shipyard 5/17/24

(If only one test performed, line through Test Not Performed)

Signature/Tester name: [Signature]

Print name/Tester Name: Jeff Westbrooke

CBC Authorized Representative

Signature/Witness name: [Signature]

Print name/Witness name: Jake Stevenson

Affiliation of Witness (Company): IMT



SOUTHWEST SHIPYARD, L.P.

18310 Market Street, Channelview, Texas 77530 Phone: 281-860-3200 Fax: 281-860-3215
8502 Cypress Street, Houston, Texas 77012 Phone: 713-967-6300 Fax: 713-967-6301
1002 Texas Clipper Rd., Galveston, Texas 77554 Phone: 409-740-3755 Fax: 409-740-3451

F-7.5.1(C/R).6 - A

BARGE PIPING TEST LETTER

Note: Test Results are valid for One (1) Year from Date of Test !

INSTRUCTIONS: FILL OUT COMPLETELY. WRITE "N/A" ON ANY NON-APPLICABLE LINE.

BARGE NAME/NUMBER: C.B.P. 385 CANAL BARGE LENO

LETTER EXPIRATION DATE (One Year from Test): 05-27-2024

1. Cargo Piping and Valves (Date of Test): 05-27-2023

Test Pressure (psi): 188 Psi

2. Cargo Pressure Gauge (Date of Test): 05-27-2023


Percent Accuracy (%): 98 %

3. Steam Piping and Valves (Date of Test): 05-27-2023

Test Pressure (psi): 125

SWSLP Signature: [Signature] Date: 05/27/23

DISTRIBUTION: Place original as last page of "USCG Papers Folder" located in Barge document mailbox.



VLS

MARINE SERVICES

Cargo Piping Test Letter

Note: Test results are valid for (1) year from date of test!

Date:	5/16/2022	M.A.W.P.	125
Vessel:	CBC 385	Method of Test:	Hydro
Owner:	Canal Barge Company	Testing Location:	VLS Marine Services Inc.
Address:	1801 Engineers Rd Belle Chase, LA 70037	Physical Address:	8700 Old Yacht Club Rd Port Arthur, TX 77642

TRANSFER SYSTEM TESTING DATA



**** Fill out completely. Write N/A on any non-applicable line. ****

Date:	Barge Piping:	Results	Note:
5/16/2022	Cargo piping & valves	187.5 p.s.i	
5/16/2022	Cargo pressure gauges	98 % accurate	
N/A	Steam System	125 p.s.i	

Note: Test each pressure gauges annually, accurate within 10 percent. Test each remote controlled operating or indicating equipment such as remotely operated valve, tank alarm, or emergency shutdown device. 33 CFR 156.170(c)(2) & 46 CFR 35.35-70(b)

SIGNATURES

I credit that the tests contained herein were conducted in compliance with 33 CFR 156.170, 46 CFR 35.35-70.

Tester name: Charles Johnson
Tester signature: 
Witnessing inspector name: Beverly Guidry
Witnessing inspector signature: 
Witnessing inspector affiliation: VLS Gas Free PM
