

Vicksburg Shipyard, LLC.
404 Port Terminal Circle
Vicksburg, MS 39183
(601) 973-7413

PIPELINE TEST LETTER

Date: 8/4/2026

To Whom It May Concern:

The cargo pipeline on tank barge CBC 1367 was tested to 187.5psi one and a half times its working pressure MAWP125psi and proved operable in accordance with 33CFR156.170 and 46CFR35.35-70.

The cargo pipeline relief valve was tested to 125psi and certified. The cargo pipeline pressure gauge is working within 10 percent of shown pressure.

The steam system and relief valve did function as required by 46 CFR61.15-15

Vicksburg Shipyard TESTER

(PRINT) Jan Aguilar

(SIGN) [Signature] DATE: 08/04/2026

WITNESSING INSPECTOR

(PRINT) Terry DeFrance

(SIGN) Terry DeFrance DATE: 8/4/26

(PRINT) Oscar Sanchez

(SIGN) Oscar Sanchez DATE: 8/4/26

T.T. 237, LLC

Specializing in Gas Freeing, Cleaning and Repairs
5190 North River Road, Port Allen, Louisiana 70767
Phone: (225) 473-8222 Fax: (225) 473-2199

Pipeline Test Letter

Date: 9/8/25

To Whom It May Concern:

The cargo pipeline and relief valve as required by 33CRH156.170, on tank barge

CBC 1367 located at T.T. 237, was tested on 9/8/25 at 188psi.

- Pressure gauge was found to be operating.
- The relief valve functioned as required.
- The steam piping system was tested at N/A psi.
- The steam system relief valve functioned as required.

Signature of Tester: Joey Jones

Witness: [Signature]



Cargo Piping Test Letter

Note: Test results are valid for (1) year from date of test!

Date:	10/28/2024	M.A.W.P.	125 PSI
Vessel:	CBC 1367	Method of Test:	Air
Owner:	Canal Barge Company	Testing Location:	VLS Marine Services-Plaquemine
Address:	1801 Engineers Rd	Physical Address:	1070 River Road
	Belle Chase, LA 70037		Sunshine, La 70780

TRANSFER SYSTEM TESTING DATA


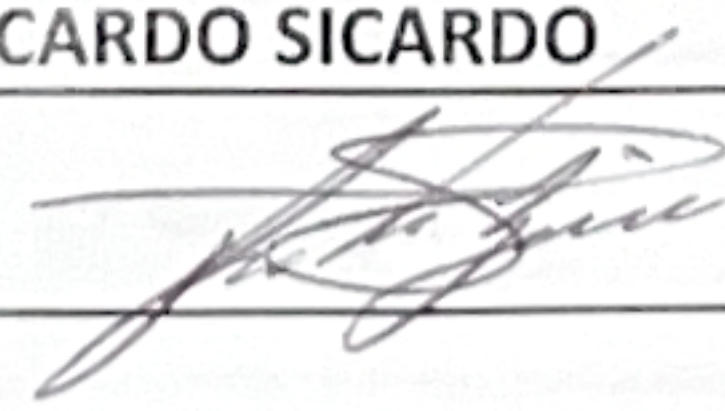
**** Fill out completely. Write N/A on any non-applicable line. ****

Date:	Barge Piping:	Results
10/8/2024	Cargo piping & valves	187.5 p.s.i
10/28/2024	Cargo pressure gauges	98% accurate
10/28/2024	Steam System	125 p.s.i

Note: Test each pressure gauges annually, accurate within 10 percent. Test each remote controlled operating or indicating equipment such as remotely operated valve, tank alarm, or emergency shutdown device. 33 CFR 156.170(c)(2) & 46 CFR 35.35-70(b)

SIGNATURES

I credit that the tests contained herein were conducted in compliance with 33 CFR 156.170, 46 CFR 35.35-70.

Tester name:	NICHOLAS JULIEN
Tester signature:	
Witnessing inspector name:	RICARDO SICARDO
Witnessing inspector signature:	
Witnessing inspector affiliation:	Project Manager



SOUTHWEST SHIPYARD, L.P.

F-7.5.1(C/R).6 - A

18310 Market Street, Channelview, Texas 77530 Phone: 281-860-3200 Fax: 281-860-3215
8502 Cypress Street, Houston, Texas 77012 Phone: 713-967-6300 Fax: 713-967-6301
1002 Texas Clipper Rd., Galveston, Texas 77554 Phone: 409-740-3755 Fax: 409-740-3451

BARGE PIPING TEST LETTER

Note: Test Results are valid for One (1) Year from Date of Test !

INSTRUCTIONS: FILL OUT COMPLETELY. WRITE "N/A" ON ANY NON-APPLICABLE LINE.

BARGE NAME/NUMBER: C.B.C 1367 CANAL BARGE LINE

LETTER EXPIRATION DATE (One Year from Test): 11-12-2024

1. Cargo Piping and Valves (Date of Test): 11-12-2023

Test Pressure (psi): 188 PSI

2. Cargo Pressure Gauge (Date of Test): 11-12-20-23

Percent Accuracy (%): 98%

3. Steam Piping and Valves (Date of Test): 11-12-2023

Test Pressure (psi): 125 PSI

SWSLP Signature: [Signature] Date: 11-12-23

DISTRIBUTION: Place original as last page of "USCG Papers Folder" located in Barge document mailbox.



Campbell Transportation Company, Inc.
2567 Congo Arroyo Road
Newell, WV 26050-1317

Tel. (304) 387-3860
Fax (304) 387-3885

TANK BARGE PIPING PRESSURE TEST FORM

The following vessel equipment has
been tested in accordance with
46 CFR 35.35-70 and 33 CFR 156.170
on the date indicated.

Date: 9-1-22

Vessel Name: CBC 1367

Cargo Pipeline: 188 PSI

Cargo Relief Valve: 125 PSI

Cargo Pressure Gauge: Operable

Cargo Transfer Hose: N/A

Tested By: [Signature]

Witnessed By: Bill Att
