


CANAL



BARGE

Move with confidence

Cargo Pipeline Test and/or Vapor Tightness Test Certificate

Barge Name: CBC 388

Test Date: 08-25-2026

Testing Location: CHannahon

Barge Vapor Tightness Test

Test Results

This barge has been tested in accordance to section 40 CFR 61.304(f), and section 63.565(c)(1) and is considered to be vapor tight.

Signature of Tester: Ray England

Test Time Started: 0900

Test Time Completed: 0930

Beginning Pressure: 1psi

Ending Pressure: 1psi

Operational Cargo Pipeline Test

The following test(s) have been performed in compliance with U.S. Coast Guard regulations 33 CFR 156.170 and 46 CFR 35.35-70 and USCG Marine Safety Manual, Vol. II, Section B, Page B6-30.

Transfer System Piping	Test Pressure	125 psi 08-25-2026
Cargo Pump Relief Valve	Test Pressure	125 psi 08-25-2026
Cargo Pump Pressure Gauge(s)	Test Pressure	125 psi 08-25-2026

(If only one test performed, line through Test Not Performed)

Signature/Tester name:

Ray England

Name/Tester Name:

RAY ENGLAND

CBC Authorized Representative

Signature/Witness name:

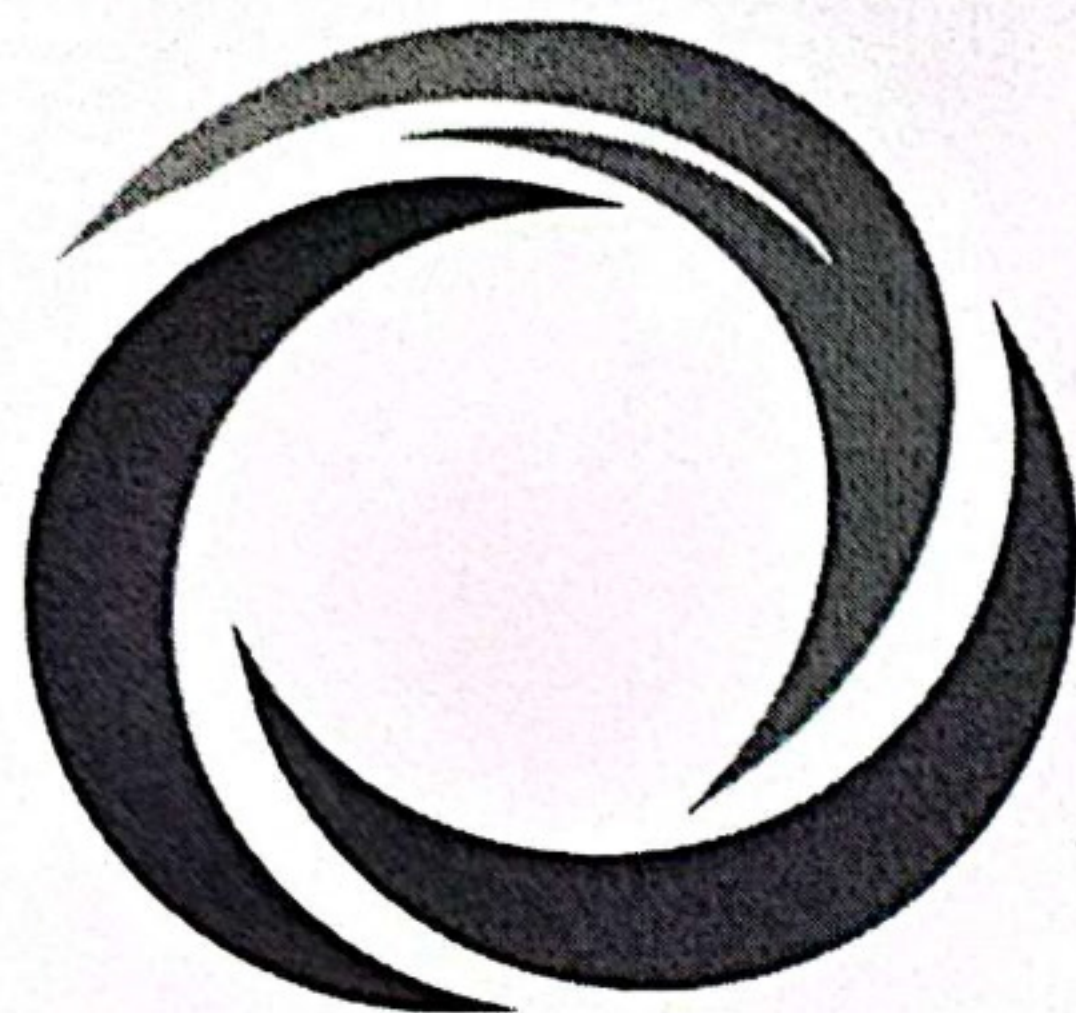
Francisco Ramos

Print name/Witness name:

Francisco Ramos

Affiliation of Witness (Company):

IMT



VLS

GAS FREE SERVICES

Cargo Piping Test Letter

Note: Test results are valid for (1) year from date of test!

Date:	10/30/2025	M.A.W.P.	125
Vessel:	CBC 388	Method of Test:	Hydro
Owner:	Canal Barge Company	Testing Location:	VLS Gas Free Services, LLC
Address:	1801 Engineers Rd Belle Chase, LA 70037	Physical Address:	8700 Old Yacht Club Rd Port Arthur, TX 77642

TRANSFER SYSTEM TESTING DATA



**** Fill out completely. Write N/A on any non-applicable line. ****

Date:	Barge Piping:	Results	Note:
10/30/2025	Cargo piping & valves	187.5 p.s.i	
10/30/2025	Cargo pressure gauges	98 % accurate	
na	Steam System	125 p.s.i	

Note: Test each pressure gauges annually, accurate within 10 percent. Test each remote controlled operating or indicating equipment such as remotely operated valve, tank alarm, or emergency shutdown device. 33 CFR 156.170(c)(2) & 46 CFR 35.35-70(b)

SIGNATURES

I credit that the tests contained herein were conducted in compliance with 33 CFR 156.170, 46 CFR 35.35-70.

Tester name:	Francisco E Moreno
Tester signature:	
Witnessing inspector name:	Jose Nava
Witnessing inspector signature:	
Witnessing inspector affiliation:	VLS Gas Free Services, LLC



Cargo Piping Test Letter

Note: Test results are valid for (1) year from date of test!

Date:	<u>7/11/2025</u>	M.A.W.P.	<u>125</u>
Vessel:	<u>CBC 388</u>	Method of Test:	<u>Hydro</u>
Owner:	<u>Canal Barge Company</u>	Testing Location:	<u>VLS Marine Services Inc.</u>
Address:	<u>1801 Engineers Rd</u> <u>Belle Chase, LA 70037</u>	Physical Address:	<u>8700 Old Yacht Club Rd</u> <u>Port Arthur, TX 77642</u>

TRANSFER SYSTEM TESTING DATA



**** Fill out completely. Write N/A on any non-applicable line. ****

Date:	Barge Piping:	Results	Note:
<u>7/11/2025</u>	<u>Cargo Pipeline</u>	<u>187.5</u> p.s.i	
<u>7/11/2025</u>	<u>Cargo pressure gauges</u>	<u>98</u> % accurate	
<u>N/A</u>	<u>Steam System</u>	<u>125</u> p.s.i	

Note: Test each pressure gauges annually, accurate within 10 percent. Test each remote controlled operating or indicating equipment such as remotely operated valve, tank alarm, or emergency shutdown device. 33 CFR 156.170(c)(2) & 46 CFR 35.35-70(b)

SIGNATURES

I credit that the tests contained herein were conducted in compliance with 33 CFR 156.170, 46 CFR 35.35-70.

Tester name: Charles Johnson
Tester signature: 
Witnessing inspector name: Tosha McKusker
Witnessing inspector signature: 
Witnessing inspector affiliation: VLS



Cargo Piping Test Letter

Note: Test results are valid for (1) year from date of test!

Date:	<u>7/16/2024</u>	M.A.W.P.	<u>125</u>
Vessel:	<u>CBC 388</u>	Method of Test:	<u>Hydro</u>
Owner:	<u>Canal Barge Company</u>	Testing Location:	<u>VLS Marine Services Inc.</u>
Address:	<u>1801 Engineers Rd</u> <u>Belle Chase, LA 70037</u>	Physical Address:	<u>8700 Old Yacht Club Rd</u> <u>Port Arthur, TX 77642</u>

TRANSFER SYSTEM TESTING DATA

**** Fill out completely. Write N/A on any non-applicable line. ****

Date:	Barge Piping:	Results	Note:
<u>7/16/2024</u>	<u>Cargo piping</u>	<u>187.5</u> p.s.i	
<u>7/16/2024</u>	<u>Cargo pressure gauges</u>	<u>98</u> % accurate	
<u>N/A</u>	<u>Steam System</u>	<u>125</u> p.s.i	


Note: Test each pressure gauges annually, accurate within 10 percent. Test each remote controlled operating or indicating equipment such as remotely operated valve, tank alarm, or emergency shutdown device. 33 CFR 156.170(c)(2) & 46 CFR 35.35-70(b)

SIGNATURES

I credit that the tests contained herein were conducted in compliance with 33 CFR 156.170, 46 CFR 35.35-70.

Tester name:	<u>Charles Johnson</u>
Tester signature:	<u>[Signature]</u>
Witnessing inspector name:	<u>Tosha McKusker</u>
Witnessing inspector signature:	<u>[Signature]</u>
Witnessing inspector affiliation:	<u>VLS PM</u>

CANAL



BARGE

Move with confidence

Cargo Pipeline Test and/or Vapor Tightness Test Certificate

Barge Name: CO-388

Test Date: 8-11-23

Testing Location: Channahon Fleet

Barge Vapor Tightness Test

Test Results

This barge has been tested in accordance with section 40 CFR 61.304(f), and section 63.565(c)(1) and is considered to be vapor tight.

Signature of Tester: [Signature]

Test Time Started: 0800

Test Time Completed: 0900

Beginning Pressure: 185

Ending Pressure: 185

Operational Cargo Pipeline Test

The following test(s) have been performed in compliance with U.S. Coast Guard regulations 33 CFR 156.170 and 46 CFR 35.35-70 and USCG Marine Safety Manual, Vol. II, Section B, Page B6-30.

Transfer System Piping Test Pressure 125 psi ✓

Cargo Pump Relief Valve Test Pressure 125 psi ✓

Cargo Pump Pressure Gauge(s) Test Pressure 125 psi ✓

(If only one test performed, line through Test Not Performed)

Signature/Tester name: [Signature]

Name/Tester Name: Jose Stevenson

U.S. Authorized Representative.

Signature/Witness name: [Signature]

Print name/Witness name: RAY ENGLAND

Affiliation of Witness (Company): IMT



SOUTHWEST SHIPYARD, L.P.

F-7.5.1(R).6-D

18310 Market Street, Channelview, Texas 77530 Phone: 281-860-3200 Fax: 281-860-3215
8502 Cypress Street, Houston, Texas 77012 Phone: 713-967-6300 Fax: 713-967-6301
1002 Texas Clipper Rd., Galveston, Texas 77554 Phone: 409-740-3755 Fax: 409-740-3451

BARGE PIPING TEST LETTER

Note: Test Results are valid for One (1) Year from Date of Test !

INSTRUCTIONS: FILL OUT COMPLETELY. WRITE "N/A" ON ANY NON-APPLICABLE LINE.

BARGE NAME / NUMBER: C.B.C. 388

BARGE OWNER: CANAL BARGE LINE

OWNER ADDRESS: _____

TESTING
LOCATION:

SOUTHWEST SHIPYARD, L.P.
18310 MARKET STREET
CHANNELVIEW, TX 77530

SOUTHWEST SHIPYARD, L.P.
8502 CYPRESS
HOUSTON, TX 77012

SOUTHWEST SHIPYARD, L.P.
1002 TEXAS CLIPPER RD.
GALVESTON, TX 77554

Identify Location by Checking Box



LETTER EXPIRATION DATE (One Year from Test): 08 - 10 - 2023

1. Cargo Piping and Valves (Date of Test): 08 - 10 - 2022

Test Pressure (psi): 188 PSI

2. Cargo Pressure Gauge (Date of Test): 08 - 10 - 2022

Percent Accuracy (%): 98 %

3. Steam Piping and Valves (Date of Test): N/A

Test Pressure (psi): N/A

4. Cargo Tank Relief Valves (Date of Test): N/A

Test Pressure (psi): N/A

SWSLP Tester/Position: Alamy D. L. Date: 08-10-22

SWSLP Inspector/Position: J. A. Date: 08-10-22

DISTRIBUTION: Place original as last page of "USCG Papers Folder" located in Barge document mailbox.
