

ODC Daily Coaling Plan

06/09/2025

Geologist Contact: 0473 223 132




Coal Locations

Location	Coal Type	Destination	Comments
T03	C_VU1_VU3	SP_N	
	C_LL1	SP_B	Thin seam – take care when mining Tip Stockpile South to North
	C_LL2T_LL2B		
	C_LL3B	SP_M	Thin seam – take care when mining.
T04	C_LL1	SP_B (west)	Thin seam – take care when mining
	C_LL2T_LL2B	SP_P	
	C_LL3B	SP_Q	
	C_VU1_VU3	SP_O	
T05	C_LL1	SP_B (east)	Thin seam – take care when mining
	C_LL2T_LL2B	SP_D/SP-N	SP-D for ramp de-stack and SP-N for T05 dig
	C_LL3B	SP-R	Thin seam – take care when mining
	C_VU1_VU3	SP_A	



NON-
Trial
VL1 to
VL_PAD

Location	Coal Type	Destination	Comments
T03/04 – VL Trial	C_VL11_VL12	VL_Pad	North-Eastern Section (Separate from other VL)
	C_VL13	SP_T	Southern End
	C_VL15	SP_T2	Northern End

Ideal Roof and Floor Conditions

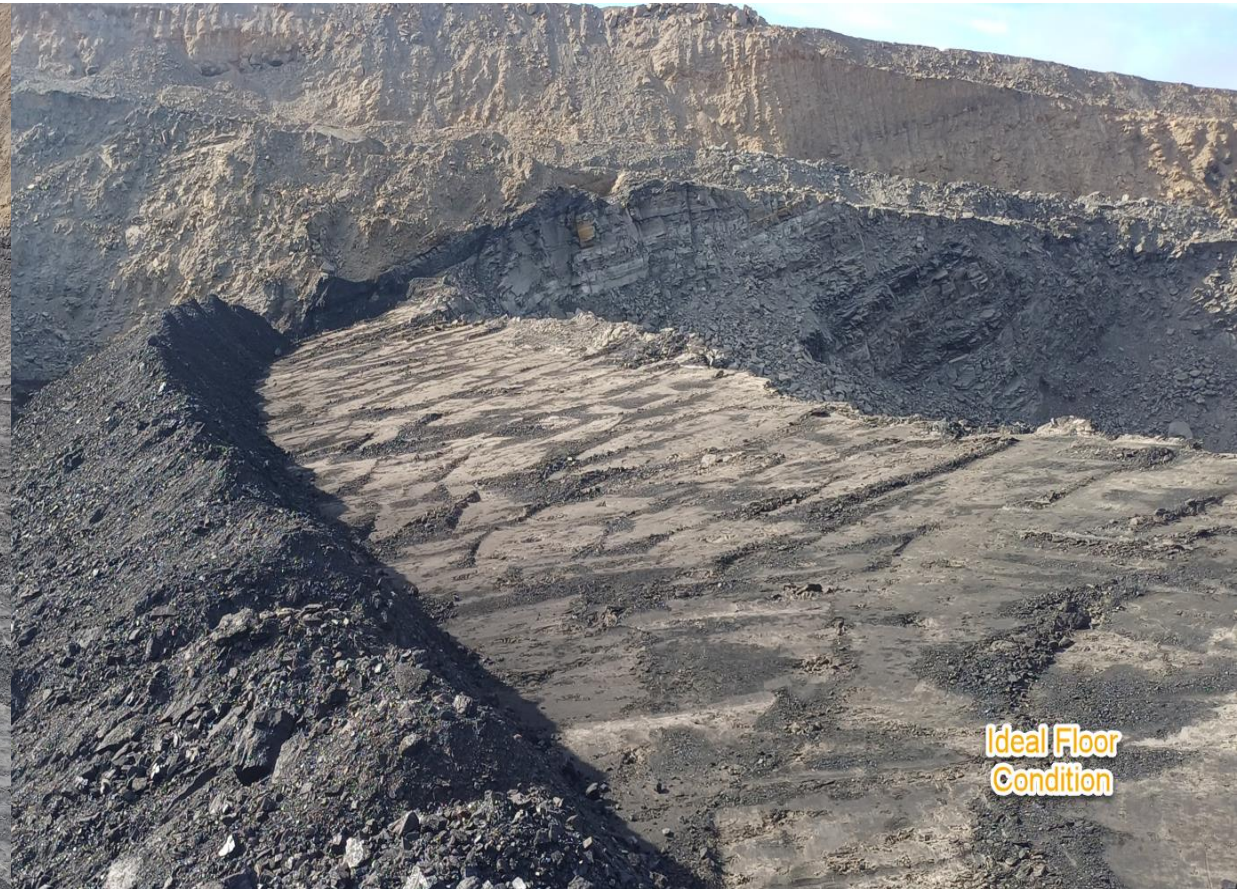

T03/S01 (VL Trial)

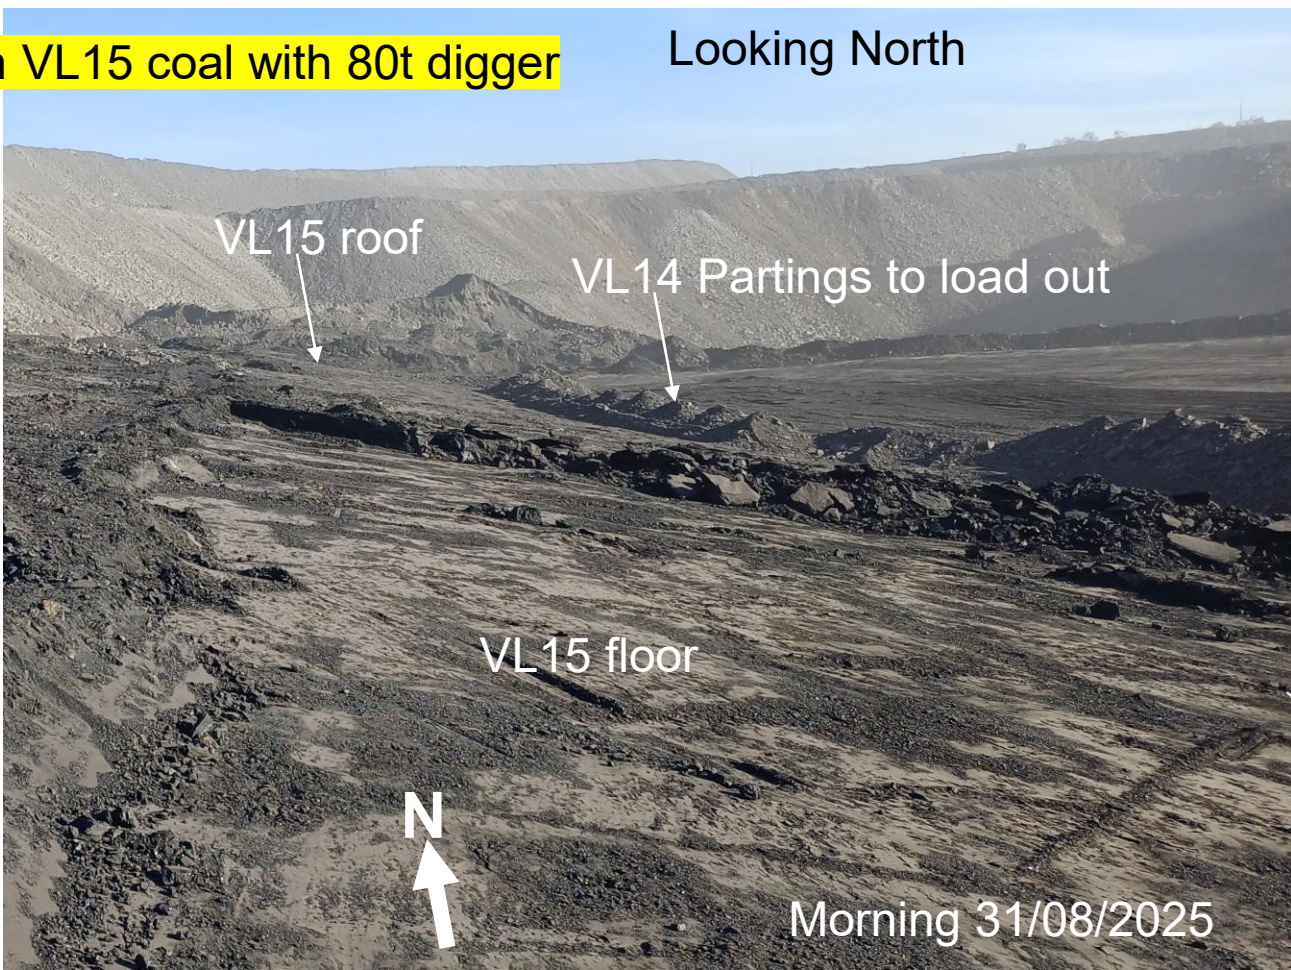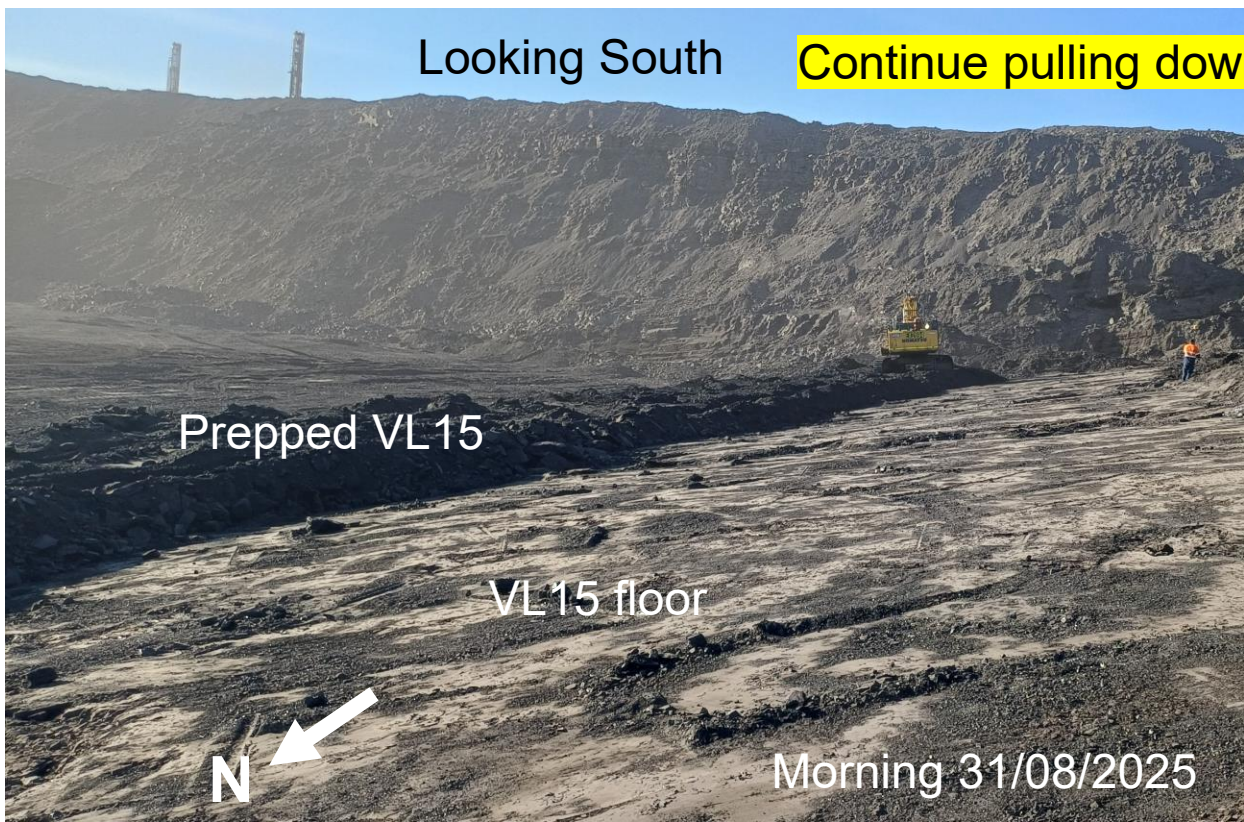

Have received good feedback so far from client on the coal prep of VL15, thanks for your efforts.

Location	Coal Type	Destination	Comments
T03 – VL Trial	C_VL11_VL12	VL_Pad	North-Eastern Section (Separate from other VL)
	C_VL13	SP_T	Southern End
	C_VL15	SP_T2	Northern End

COAL CODE	STOCKPILE	COMMENTS
C_LL1	SP_B	Thin seam – take care when mining
C_LL2B_LL2T		
C_LL3B	SP_M	
C_VU1_VU3	SP_G	SP_N overflow

T03/S01 (VL Trial)

Continue pulling down VL15 coal with 80t digger

Have received good feedback so far from client on the coal prep of VL15, thanks for your efforts.



Afternoon 31/08/2025

T05/S02




COAL CODE	STOCKPILE	COMMENTS
C_LL1	SP_B (east)	Thin seam – take care when mining
C_LL2T_LL2B	SP_N	Stockpile on SP-N
C_LL3B	SP_R	Eastern Side
C_VU1_VU3	SP_A	




T05/S01

Coal everywhere, and not always outcropping!!

COAL CODE	STOCKPILE	COMMENTS
C_LL1	SP_B (east)	Thin seam – take care when mining
C_LL2T_LL2B	SP_N	Stockpile on SP-N
C_LL3B	SP_R	Eastern Side
C_VU1_VU3	SP_A	

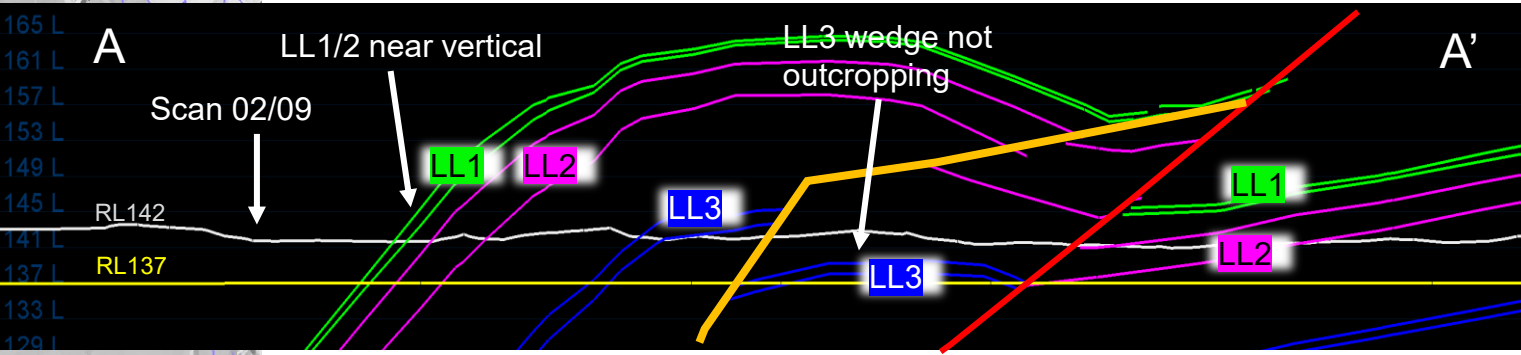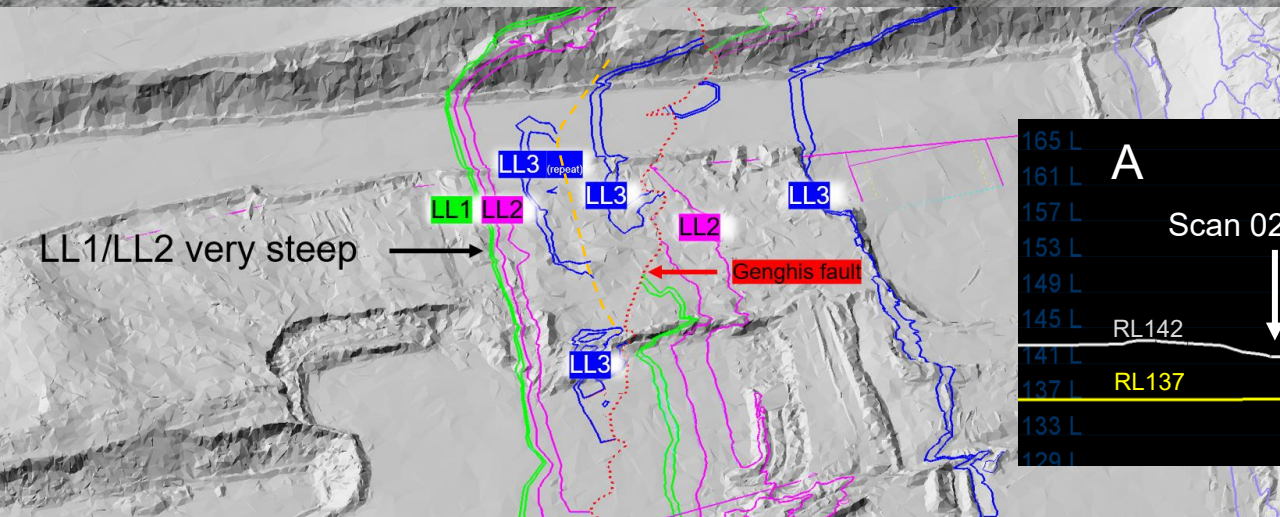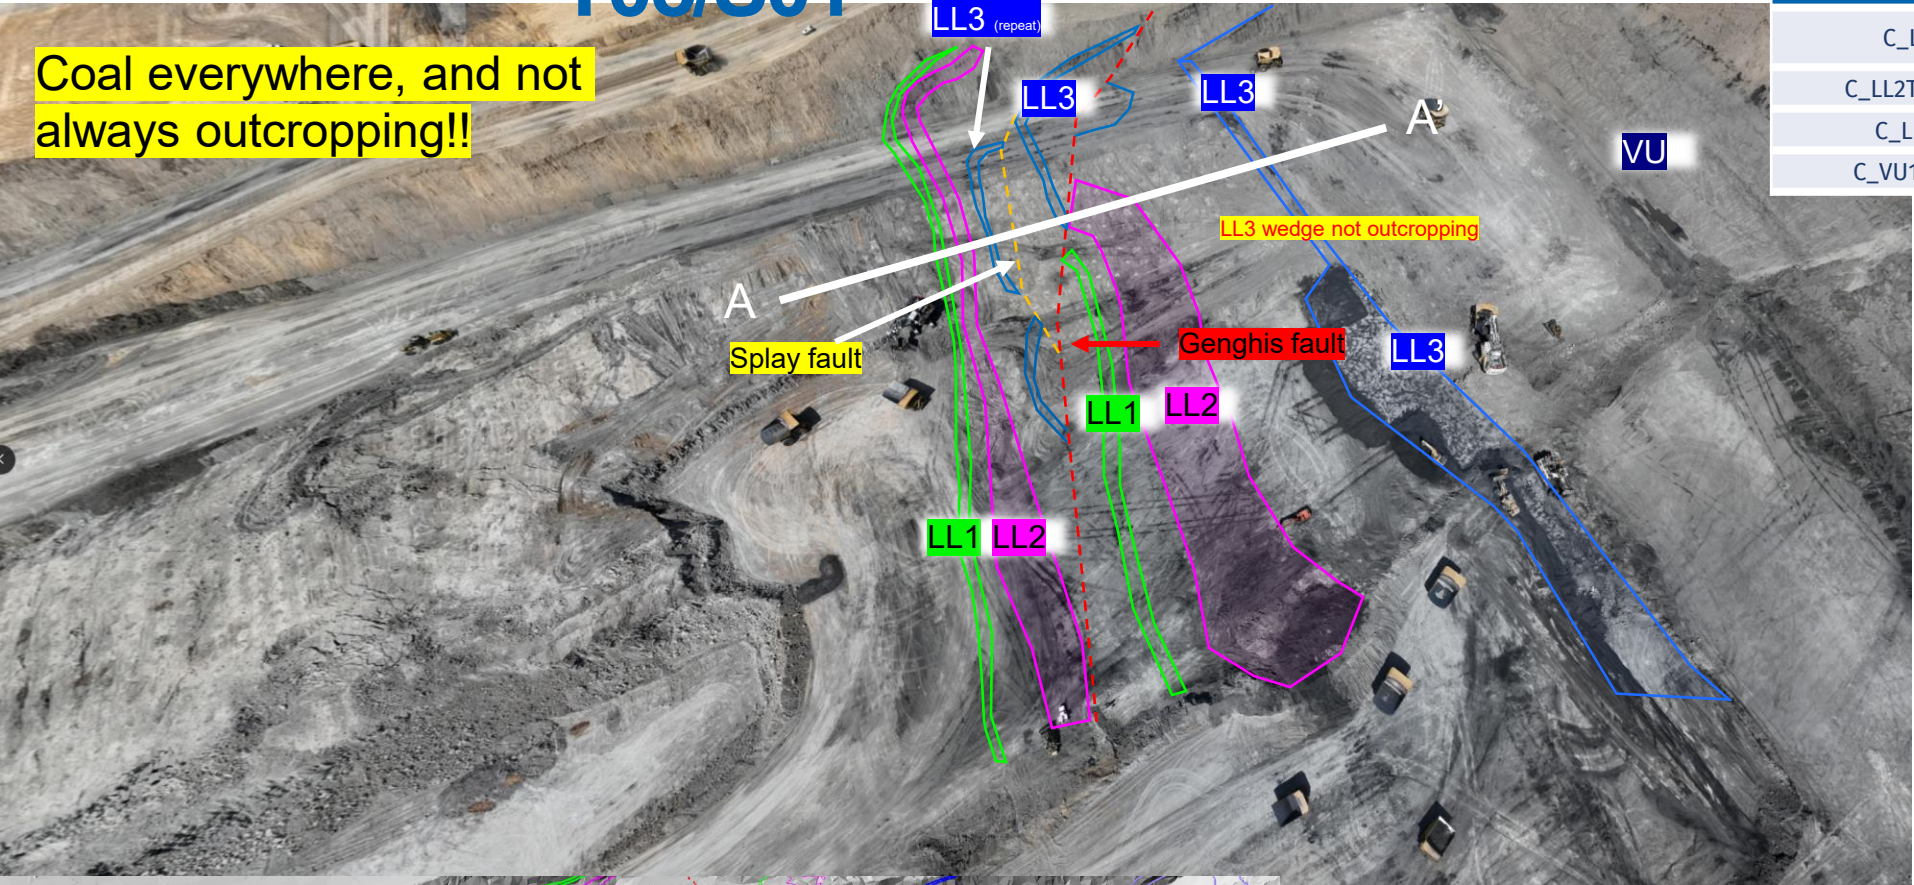

ROM

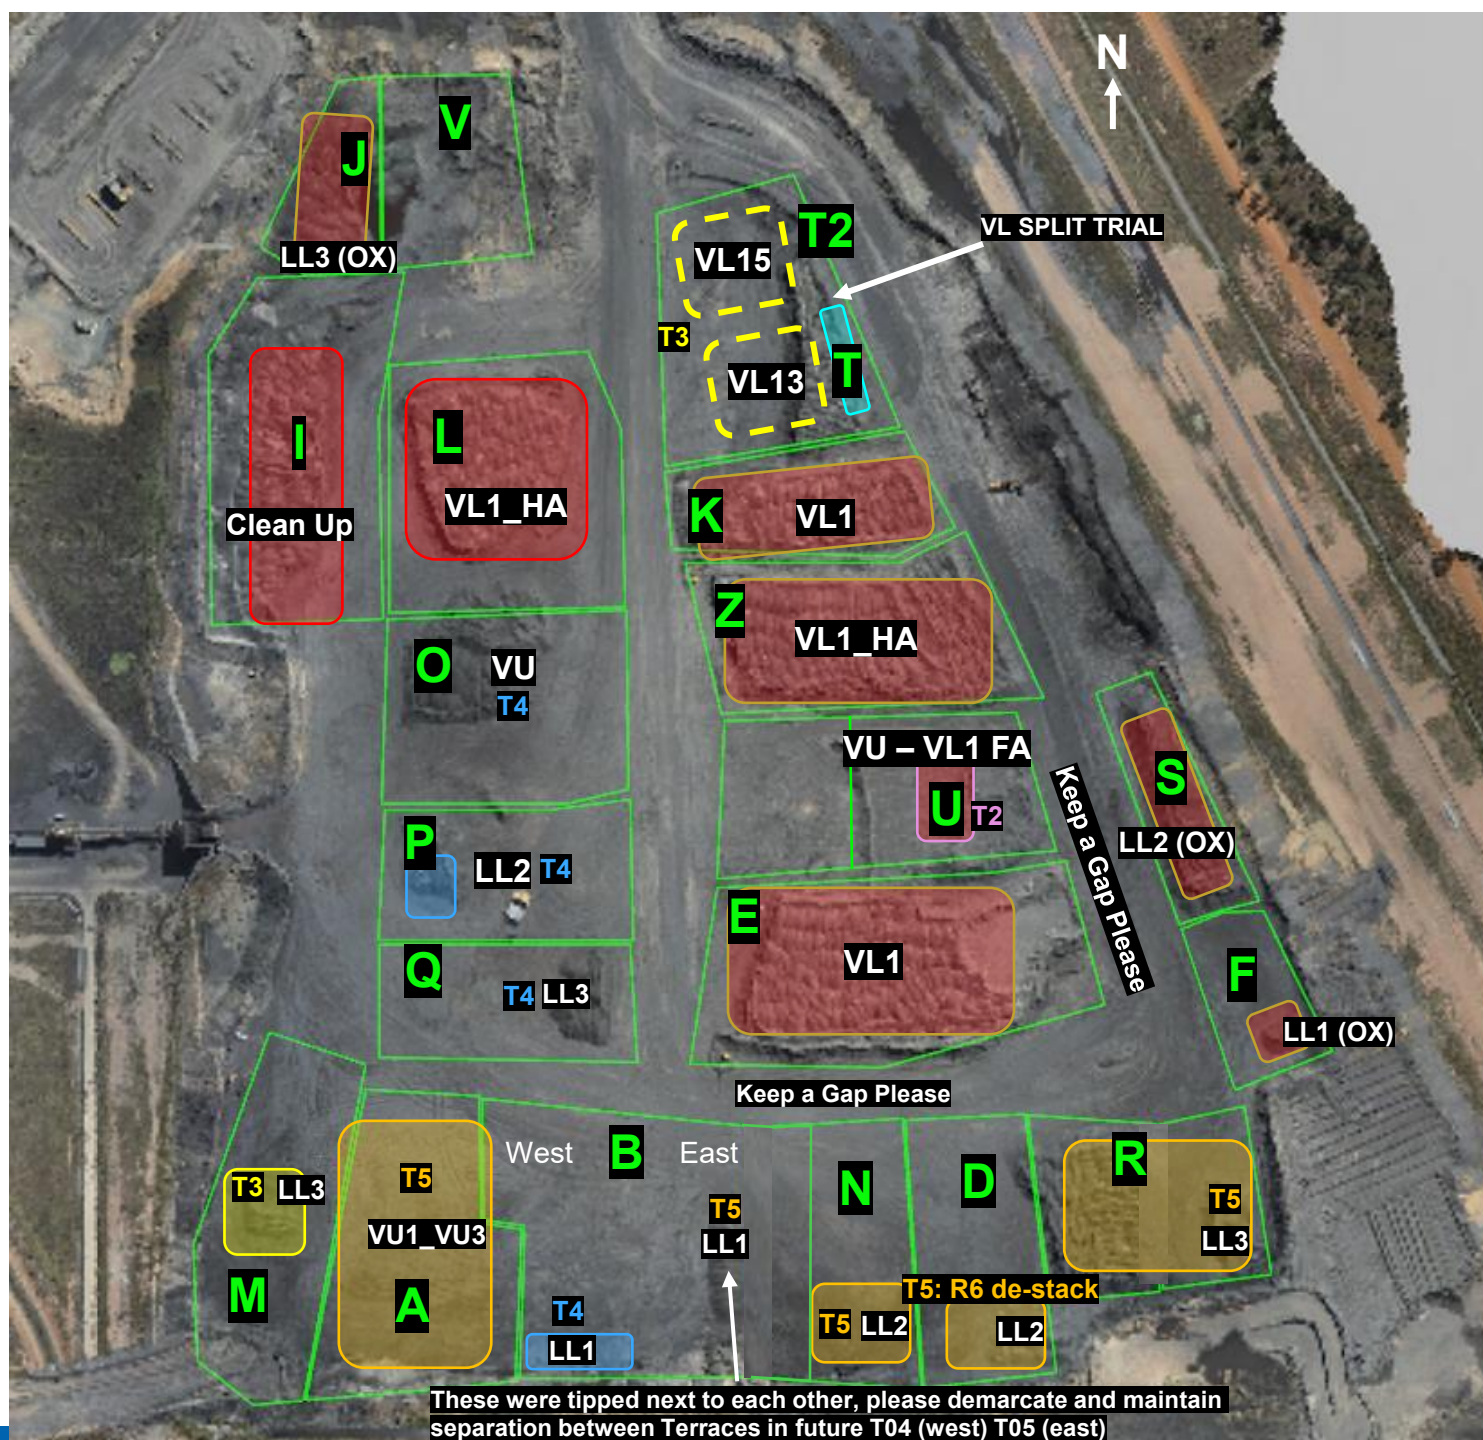**THIESS**

Tip Stockpiles South to North

ROM

VL1 ROM Pad

VL11_VL12 – VL Trial – keep separate and maintain access



31/08/25

Comments

Once Stockpile U is exhausted change to Blend 6
Once Stockpile M is exhausted change to Blend 2

Stockpile M may contain GET, ROM loader be aware.

Communicate any direct

feed start and finish time to

CHPP control.

Blends

	Feed 1	Feed 2	Feed 3	Ratio	ROM Loaders	ROM Trucks	Direct Feed	Comments	active
VL TRIAL	SP-T			Straight			Yes	VL Trial Blend (VL13 and VL15)	
Blend 2	SP-A	SP-R		1:1				1 x VU (T05S01) : 1 x LL3 (T03S02)	
Blend 3									
Blend 4									
Blend 5	SP-A	SP-U		2:1	1	2	No	2 x VU (T05S01) : 1 x VU (FA)	x
Blend 6	SP-A	SP-M		1:1				1 x VU (T05S01) : 1 x LL3 (T03S02)	
Wet weather									

[illegible]

