



Assembly Book

Revised January 22, 2026



Backyard Basecamp

Building Size
12'x12' or 12'x16'

Manufactured by RBS Holdings, LLC

205 Arlington Drive

Greenville, PA 16125

This manual is copyrighted. Under the copyright laws, this manual may not be copied, in whole or in part, without consent from

RBS Holdings, LLC © Copyright 2022

IMPORTANT INFORMATION ABOUT YOUR KIT

Thank you for purchasing our kit. Please read the following information before beginning construction. Always check with your local HOA or building code office for any requirements or restrictions.

Floor: Wood flooring is sold optionally. You may choose to build your own or pour a cement pad.

Always wear safety glasses when cutting or nailing!

Tools Required: Hand or Circular Saw
Cordless Drill
Hammer
Pencil

Level
Measuring Tape
6'-8' Ladder(s)

Safety Glasses
Dust Mask
Phillips Screwdriver
Framing Square

Additional Materials - **Not included in kit:**

Windows are purchased separately

Required: Shingles or metal roofing, Drip Edge, Roofing Nails or Screws, Paint

Optional: Caulk, Ridge Vent

Terminology:

Square - Confirm corners are at 90 degrees

Plumb - Confirm walls and trusses are straight vertically

Wall Plate - Top and bottom 2x4s used to frame walls


Tie Plate - 2x4s connecting wall sections together

Header - Spans top of door opening

OSB - Oriented Strand Board

LAP - Edge of siding that overlaps

Tongue - Edge of siding that is overlapped

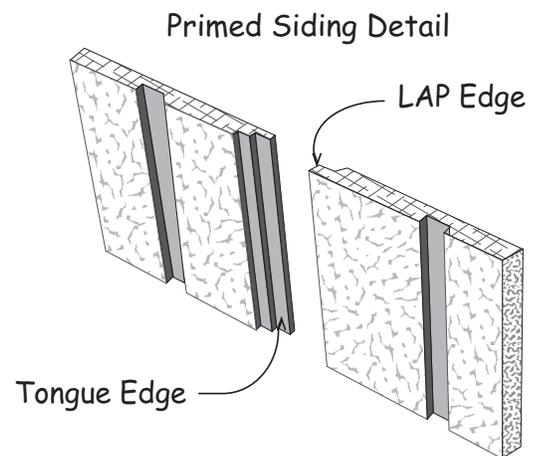

Organize:

Unpack all items & organize according to size and type. This will make items easier to find when instructed.

Review the parts list on the back page. Should there be missing items or sub-par material contact Best Barns Customer Service.

DO NOT discard any material including the pallet until your project is complete.

Assembly:

Review all instructions before you begin. Please follow steps carefully and in sequence for successful results.

If you have any questions we are happy to assist you. Please contact us at:

800-245-1577 - Mon - Fri 8AM - 5PM EST


724-866-4357 - After hours and weekends

Email - questions@barnkits.com


Constructing Details for Deluxe Floor System

Check local building codes in your area, the construction may have to change. For a concrete slab, install sill sealer as a moisture barrier between the concrete and the wall plates. Foam sill sealer can be purchased at home centers in rolls 3-1/2" or wider.

- For a 16' building, butt the 4x4-8' timbers together to make 16' runners. Secure the 4x4s together with 2' long 2x4 blocks cut from (2) two 8' boards using 16d galvanized nails.
- Cut (2) two 2x4 joist headers to length. Cut 2x4s to 12'-0" for a 12' long building, 16'-0" for a 16' long building. Layout for 16" on center joist spacing. 'X' marks where floor joist will be placed.




- Cut 2x4-12' floor joist to 11'-9". *Treated lumber may be thicker than 1-1/2". Take this into account when cutting the length of floor joists. Shorten joist measurements if necessary to obtain 12'-0" building width.*

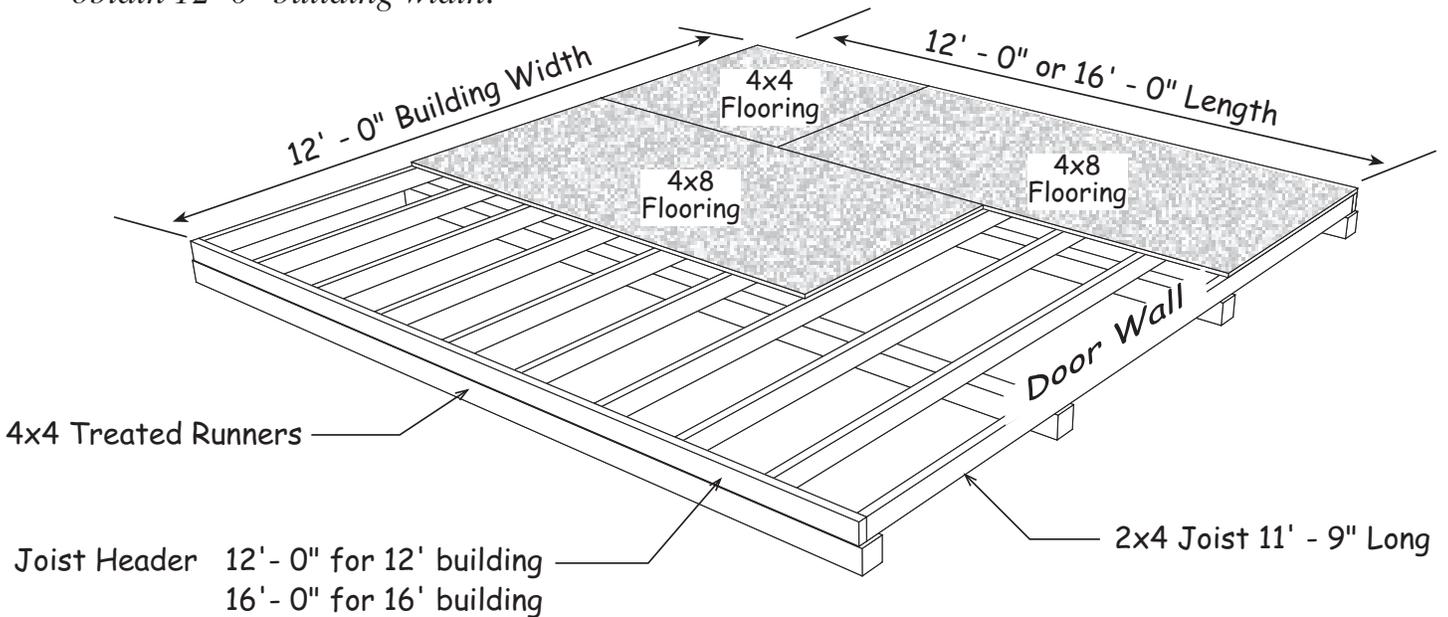

It is important that the floor be level and square. Square the floor as follows: before nailing the flooring, measure the floor diagonally (corner to corner), then measure the opposite corners; these measurements will be the same when the floor is square.

Material Description	12' x 12' shed	12' x 16' shed
2x4 Treated Blocking		2 pcs. 8'
2x4 PT Joist Headers	2 pcs. 12'	2 pcs. 16'
2x4 PT Floor Joist	10 pcs. 12'	13 pcs. 12'
4x4 Treated Runners	4 pcs. 12'	8 pcs. 8'
Flooring 5/8" or 3/4"	5 pcs. 4x8	6 pcs. 4x8
Spiral Floor Nails	2 lbs. 8d	3 lbs. 8d
Galv. Deck Nails	1 lb. 16d	3 lbs. 16d


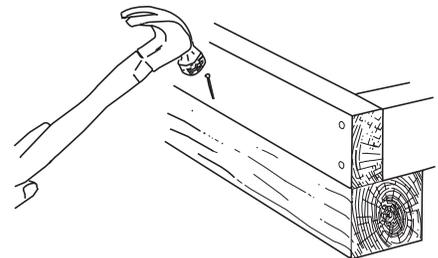


To keep 2x4 frame from moving, toe nail to 4x4.


 Do not discard any material until construction is complete. Including short blocks of 2x4s.

Step 1 Assemble 12' Long Sidewalls

1. Gather (4) four 2x4-72" boards and position together then indicate with 'X' mark where the wall studs will be located. Mark the ends that will butt together with 'the letters A' and 'B'.

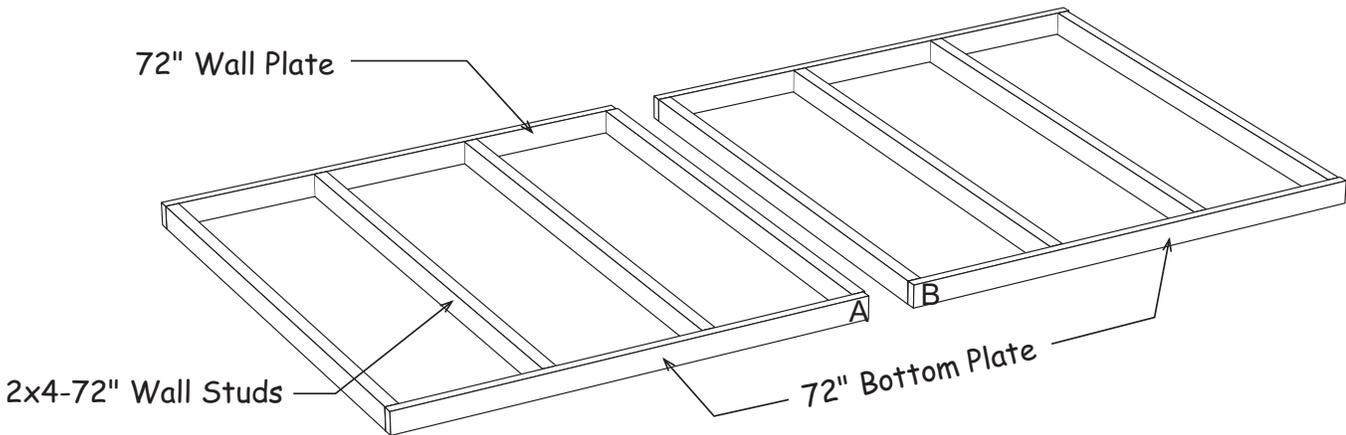

2. Install (8) eight 72" wall studs between the top and bottom plates. Use 10d sinkers, (2) two nails at each stud end. Nail both wall frames together with 10d sinkers.
3. Square wall frame. *Measure diagonally (corner to corner). The measurements will be the same when the wall is square.*
4. Install the first siding panel with the 'LAP edge' flush the end of the wall and extending 3/4" below the bottom plate. Use 6d galv. nails spaced 8" apart.
5. Install (2) two more siding panels.

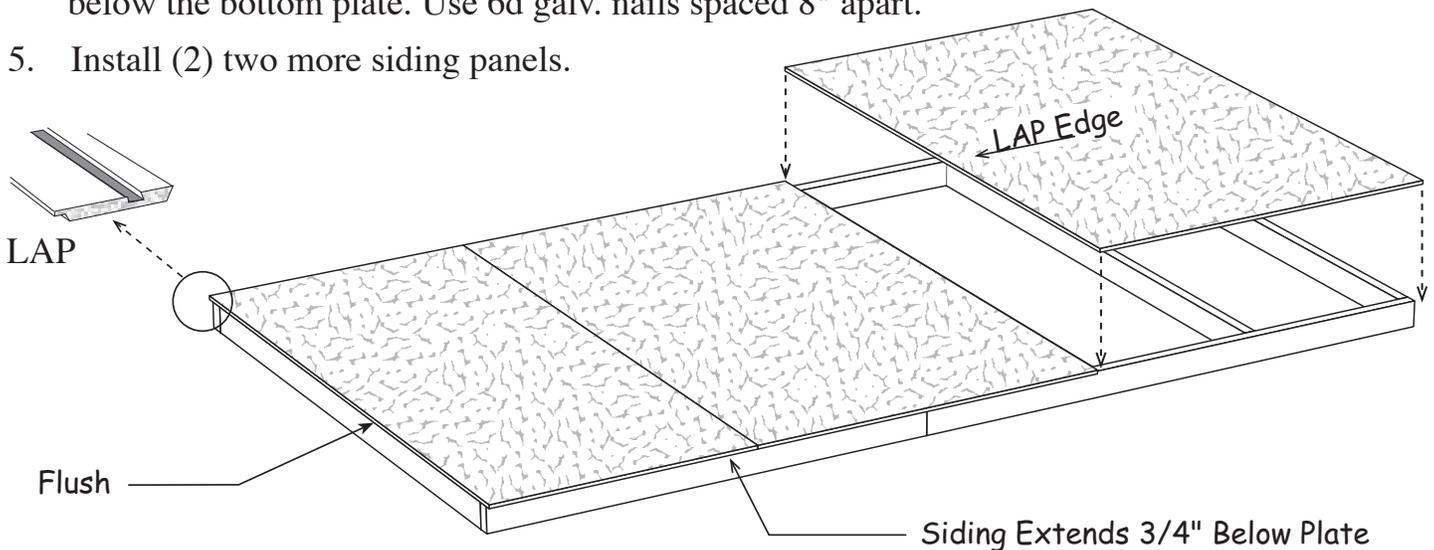


6. Repeat to assemble another sidewall.

 If you are constructing a 12' x 12' building, go to Step 3.


Step 2 Assemble Sidewalls for 16' Building Length

 If you are constructing a 12' x 12' building, go to Step 3.

1. Locate (2) two 48" long 2x4s and (3) three 2x4-72" wall studs.
2. Install (2) two 2x4-72" wall studs between wall plates at each end. Install (1) one stud in the center of the wall frame.
3. Repeat to assemble another 48" wall section.

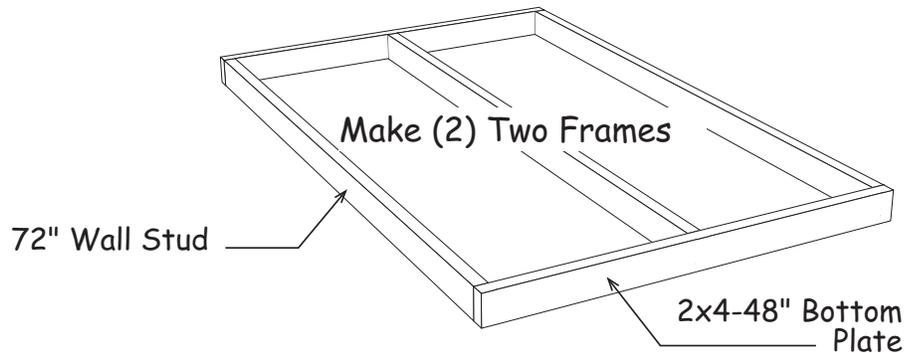


4. Select one of the 12' sidewalls assembled in **Step 1**. Butt the 48" wall frame against the wall with siding. **DO NOT** nail these frames together so they can be separated later.
5. Install a siding panel on the 48" frame. Cut panel flush with the end of the wall frame. **DO NOT** nail along the long edge of siding that overlaps the 12' wall frame. You can nail this edge after the wall panels are installed. Two separate walls are easier to handle when erecting kit.

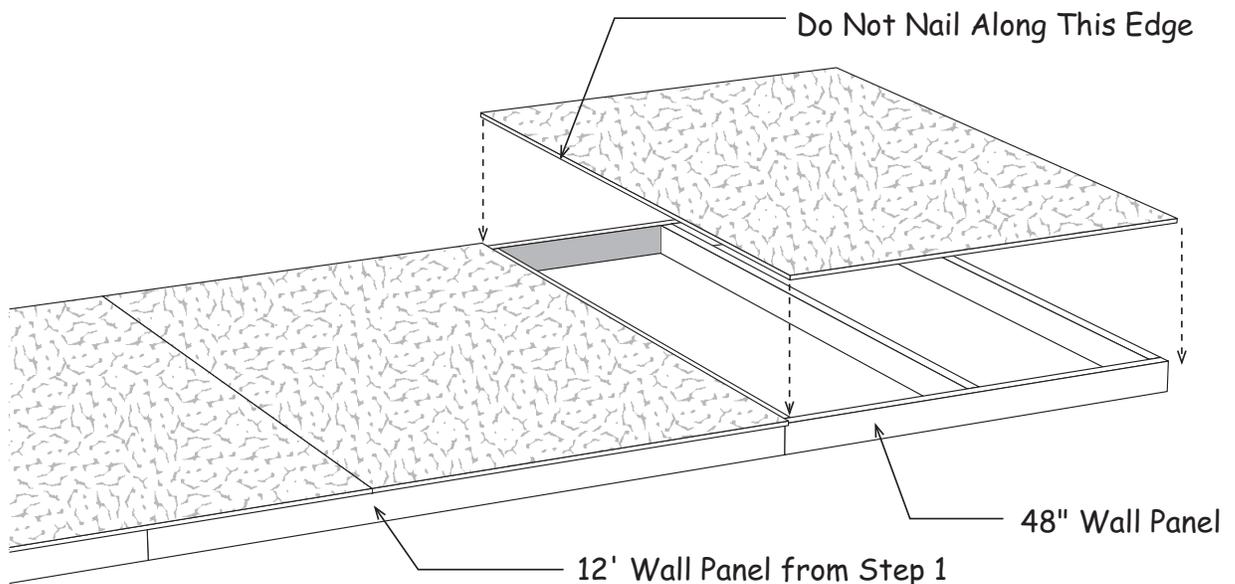


6. Repeat to apply siding to the other 48" wall frame.

Step 3 Assemble Door Wall - Offset Doors

 To position the door opening in the center of the wall, go to Step 4. To position the door opening on the right side of the front wall, flip the walls and apply siding to the opposite side of the wall frames.

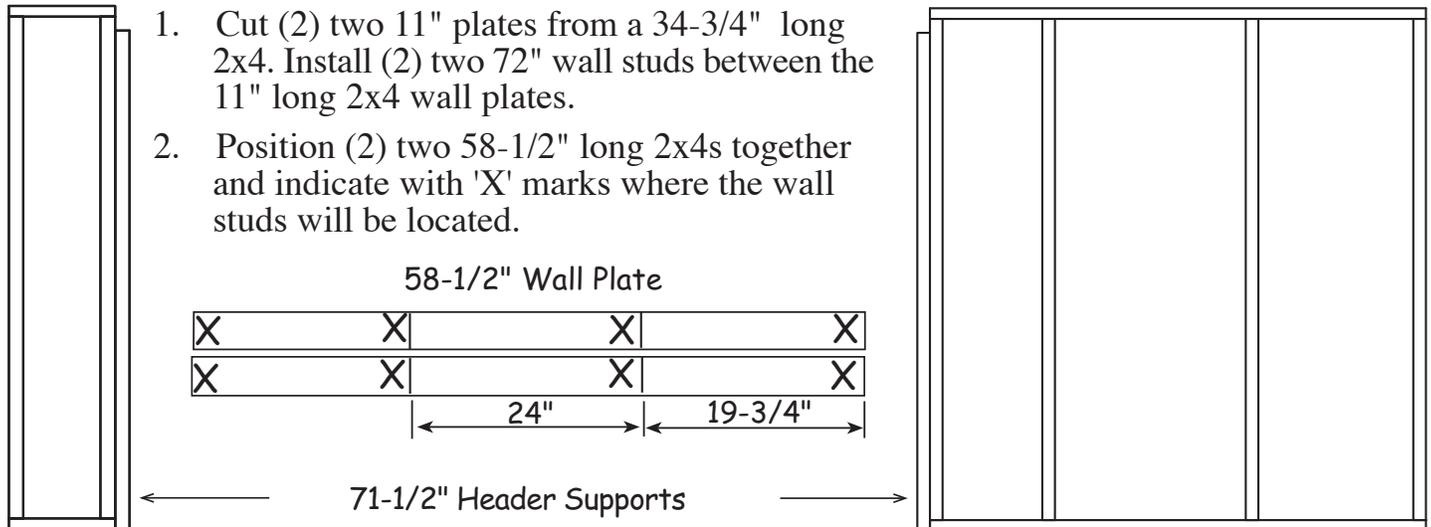


3. Install (4) four 72" wall studs between (2) two 58-1/2" long 2x4 wall plates
4. Gather (2) two 2x4-72" 2x4s. Cut each board to 71-1/2" and install as a header support on each wall frame flush with bottom plate. Use 10d sinkers.

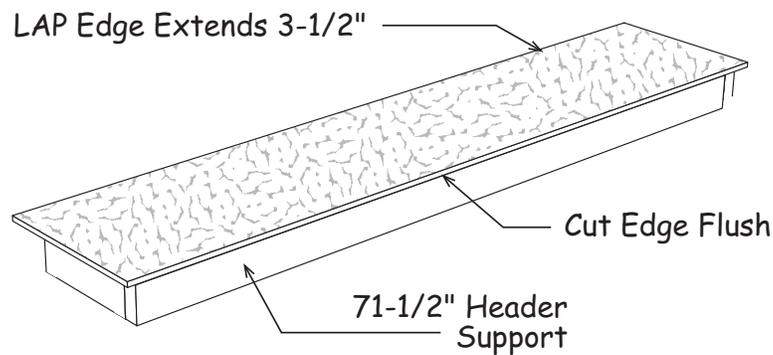

5. Select a 16" wide siding panel with a 'LAP' edge. Install cut edge flush with header support. The 'LAP' edge will extend 3-1/2" beyond the wall frame. Bottom edge will be 3/4" below the bottom plate.


 If installing the optional window you can cut the opening in the siding. Instructions are packed in window box.

6. Install a 16" siding panel with a tongue edge. Cut edge will be flush with the header support.

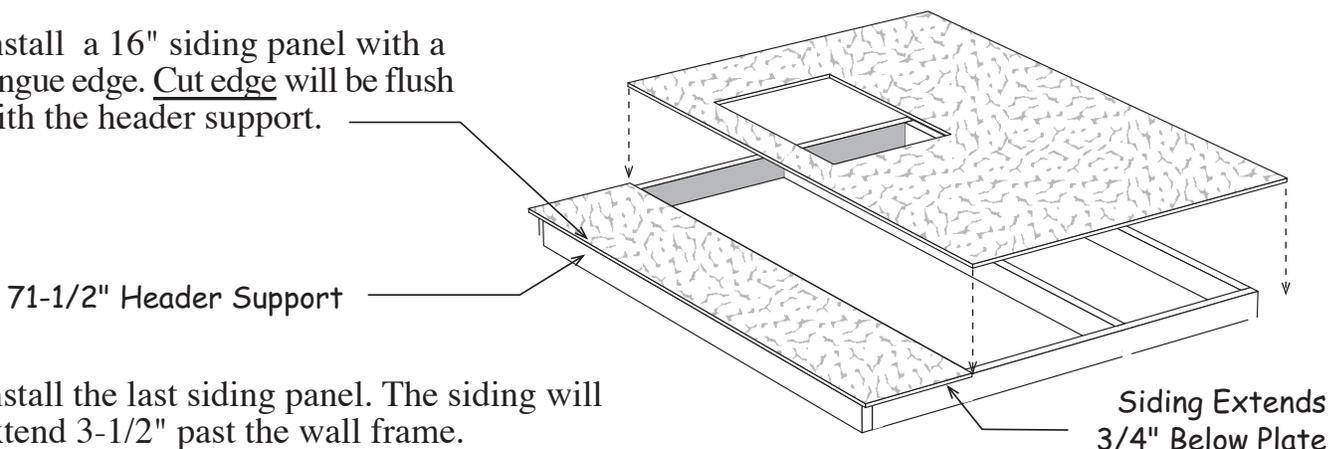


7. Install the last siding panel. The siding will extend 3-1/2" past the wall frame.

Step 4 Assemble Door Wall - Doors Centered

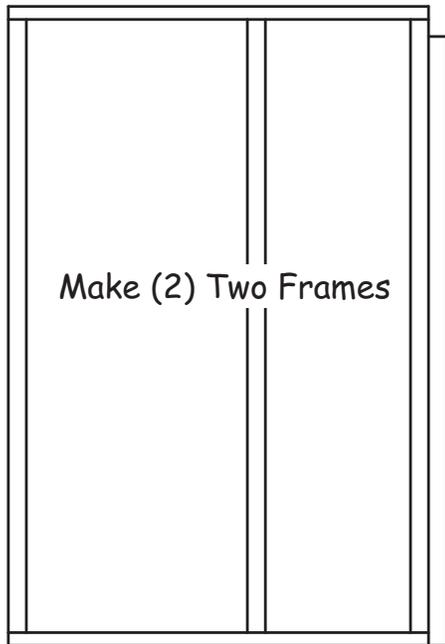


1. Locate (2) two 34-3/4" long 2x4s and position them together. Indicate with 'X' marks where studs will be located..



2. Install (3) three 72" wall studs between the 34-3/4" wall plates.
3. Locate (1) one 2x4-72" and cut to 71-1/2". Install as a header support on right side as shown and flush with bottom plate. Use 10d sinkers.
4. Locate (2) two 58-1/2" 2x4s and cut (1) one 34-3/4" plates from each. Repeat steps 2 and 3 to assemble another wall frame.

← 71-1/2" Header Support



5. Select one frame and position so header support is on right.
6. Locate a 16" wide siding panel with a 'LAP' edge. Install this panel with the cut edge flush with the 2x4 header support. Bottom edge should be 3/4" below bottom plate. Only nail along cut edge until next panel is installed.
7. Cut a 48-3/4" wide siding panel in half lengthways.
8. Select cut panel with the 'Tongue' edge. Install this panel so cut edge extends 3-1/2" beyond the end of the frame and tongue edge under the 16" panel. The siding should extend 3/4" below the bottom plate. Nail both siding panels to frame.

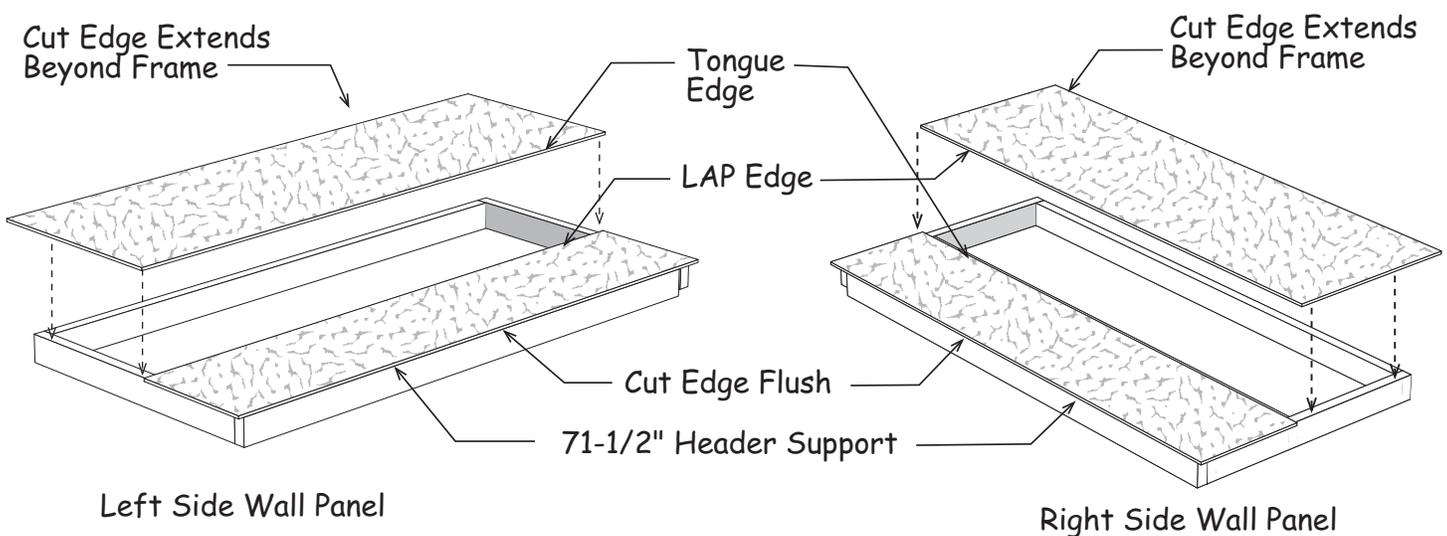


7. Locate a 16" wide siding panel with a 'Tongue' edge and the remaining 24" wide cut panel. Install these on remaining frame. **Make sure header support is oriented to the left.**

Step 5 Assemble 12' Back Wall

- Gather (4) four 2x4-68-1/2" boards an position together then indicate with 'X' marks, where the wall studs will be located. Mark the ends that will butt together with the letters 'A' and 'B'.

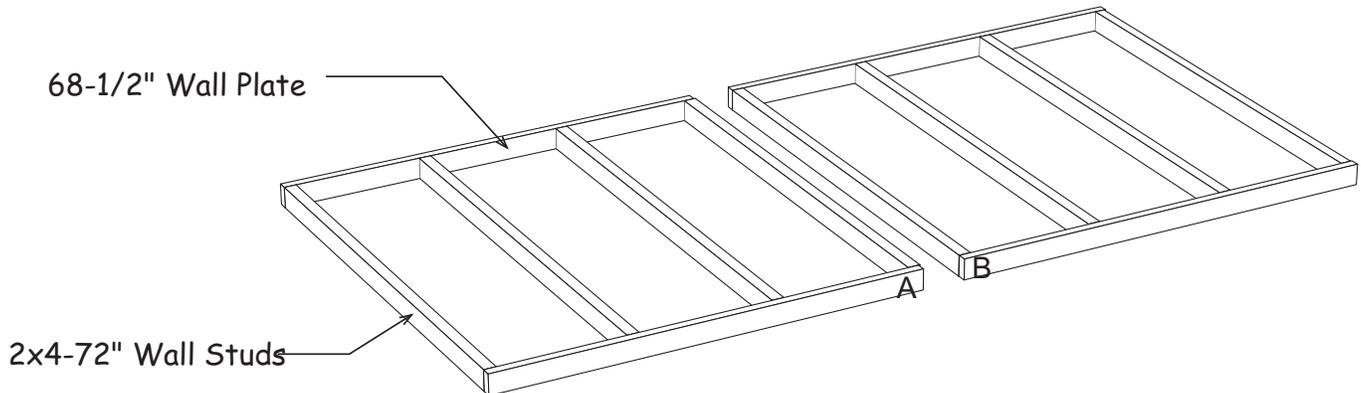


- Install (8) eight 72" wall studs between the top and bottom plates. Assemble wall frames with 10d sinkers, (2) two nails at each stud end. Nail both wall frames together with 10d sinkers.
- Square wall frame.
- Install the 1st siding panel with the 'LAP' edge extending 3-1/2" past the wall frame. The bottom will extend 3/4" below the bottom plate.
- Install (2) two more siding panels. Cut the last panel to extend 3-1/2" beyond the wall frame.

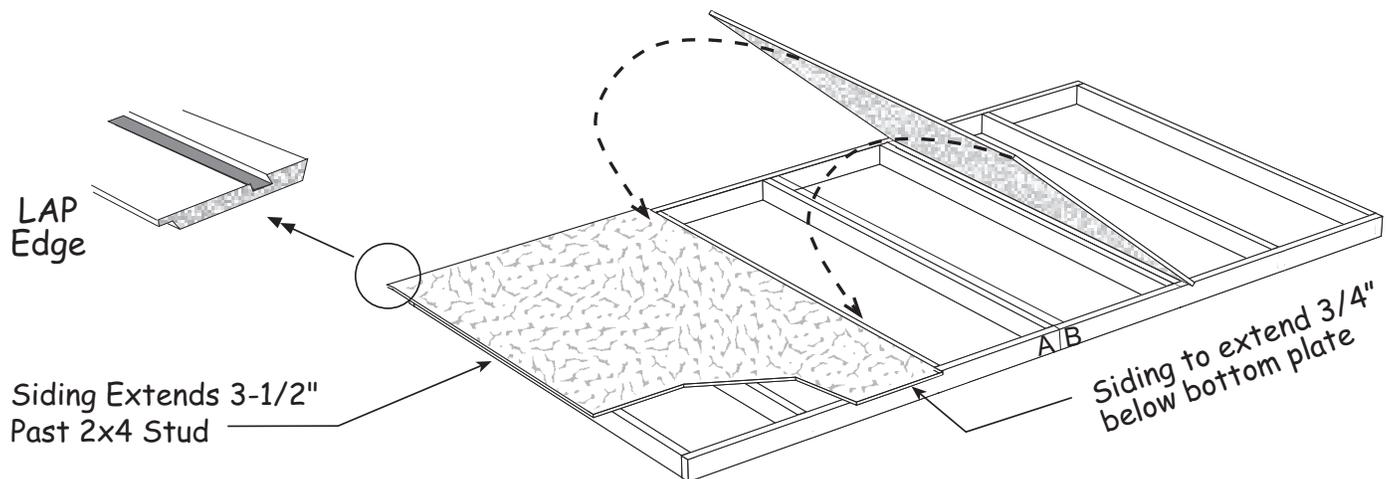


Step 6 Assemble Roof Gables

1. Butt (2) two 72" long 2x4s together and secure them with a 3-1/2" x 31-3/4" long OSB gusset across the top where they butt together. Use (12) twelve 6d common nails. This will be used as the bottom plate on the roof gables.
2. Repeat to assemble another 12' long bottom plate.

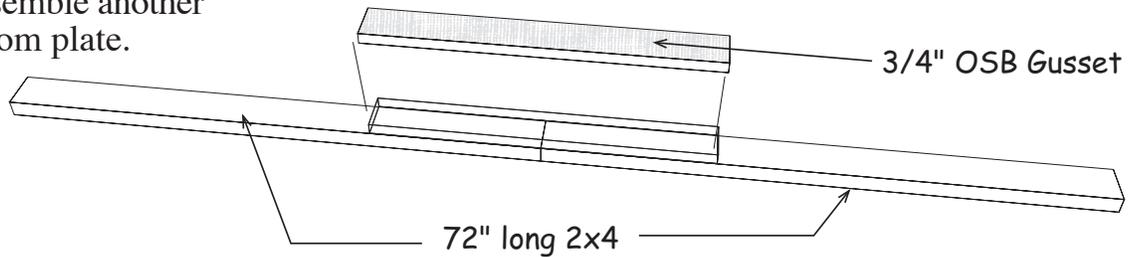


3. Place the bottom gable plate on the floor along with (2) two 80-1/2" long 2x4 truss rafters as shown below. Bottom plate will be on edge. There are short 2x4s, that may have an angle on one end, supplied in the kit. Use these to hold the truss rafter and bottom gable plate together by temporarily screwing the blocks to the floor using 2-1/2" screws. This will ensure that the gable frames and the trusses, assembled next, are identical.
4. Secure the top of the truss rafters together with a 1"x4" barbed metal drive-on plate.
5. Install (2) two 23-1/2" gable studs with angle cut at one end. Nail through the bottom plate with 10d sinkers and secure the top with barbed metal drive-on plates.

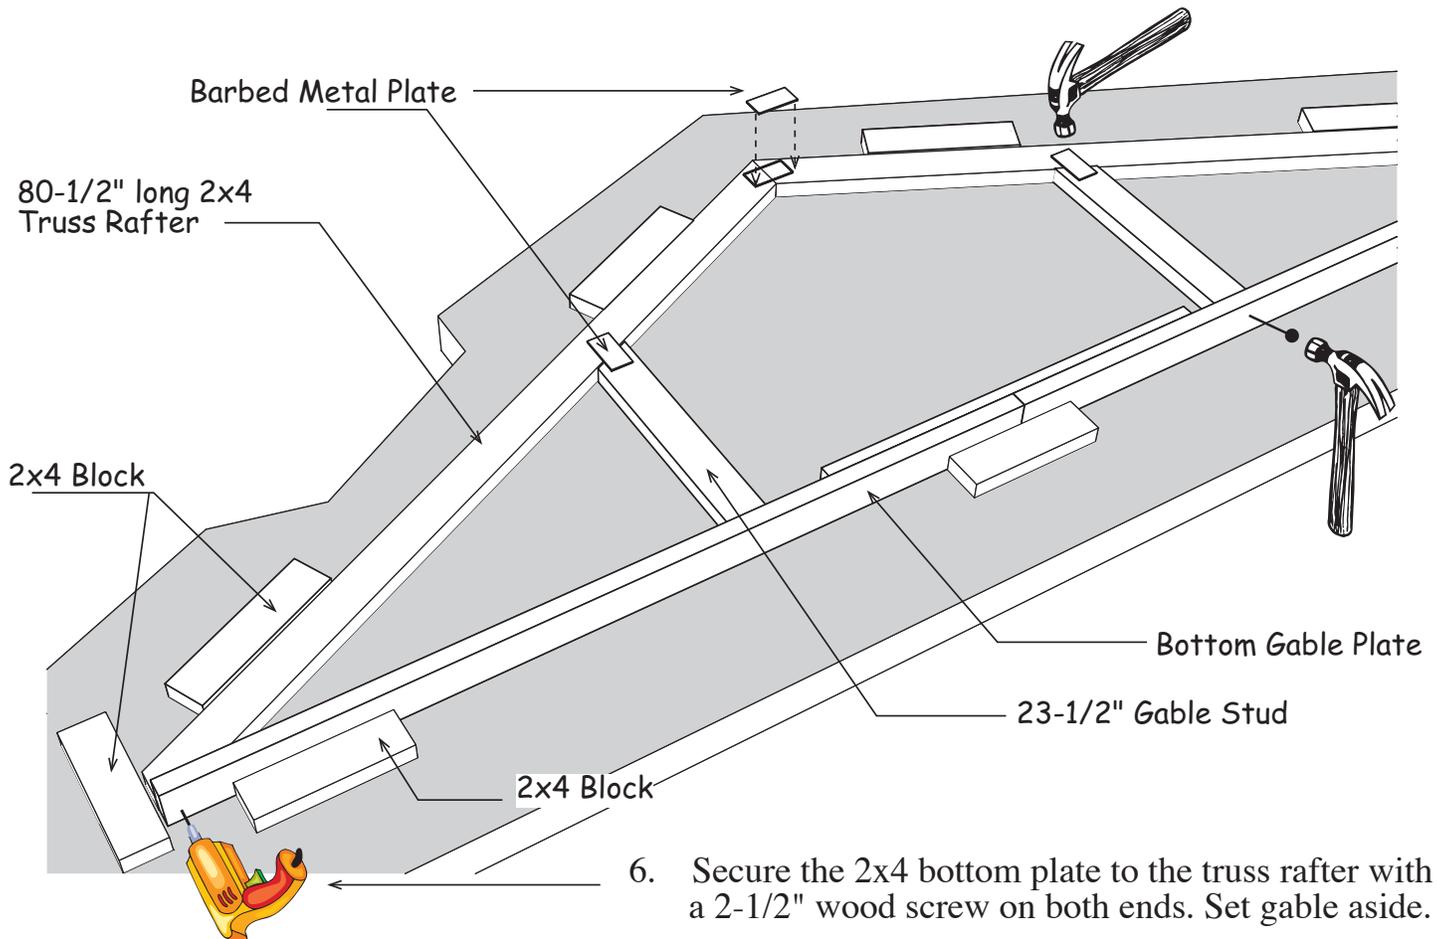


6. Secure the 2x4 bottom plate to the truss rafter with a 2-1/2" wood screw on both ends. Set gable aside.
7. Repeat steps 3-6 to assemble another gable.

Step 7 Assemble Roof Trusses

1. Place (2) two 80-1/2" long 2x4 truss rafters and a 82" long collar tie together as shown below. The collar tie has an angle cut on both ends. Reposition the lower 2x4 blocks to hold the truss rafters in place. See 'Detail B'.
2. Secure the 2x4 truss rafters at the top with a 8" x 16" wood gusset. Nail the gusset to the 2x4s with (14) fourteen 6d common nails,
3. Secure the 2x4 collar tie with (4) four 2-1/2" long wood screws at each end. Tip: Pre-drill holes with an 1/8" bit to prevent wood splitting at ends.
4. Turn this truss over and apply a wood gusset to the opposite side at the ridge.
5. Repeat to assemble (4) four more trusses if you are building a 12' long building. Assemble (6) six more trusses if you are building a 16' long building.

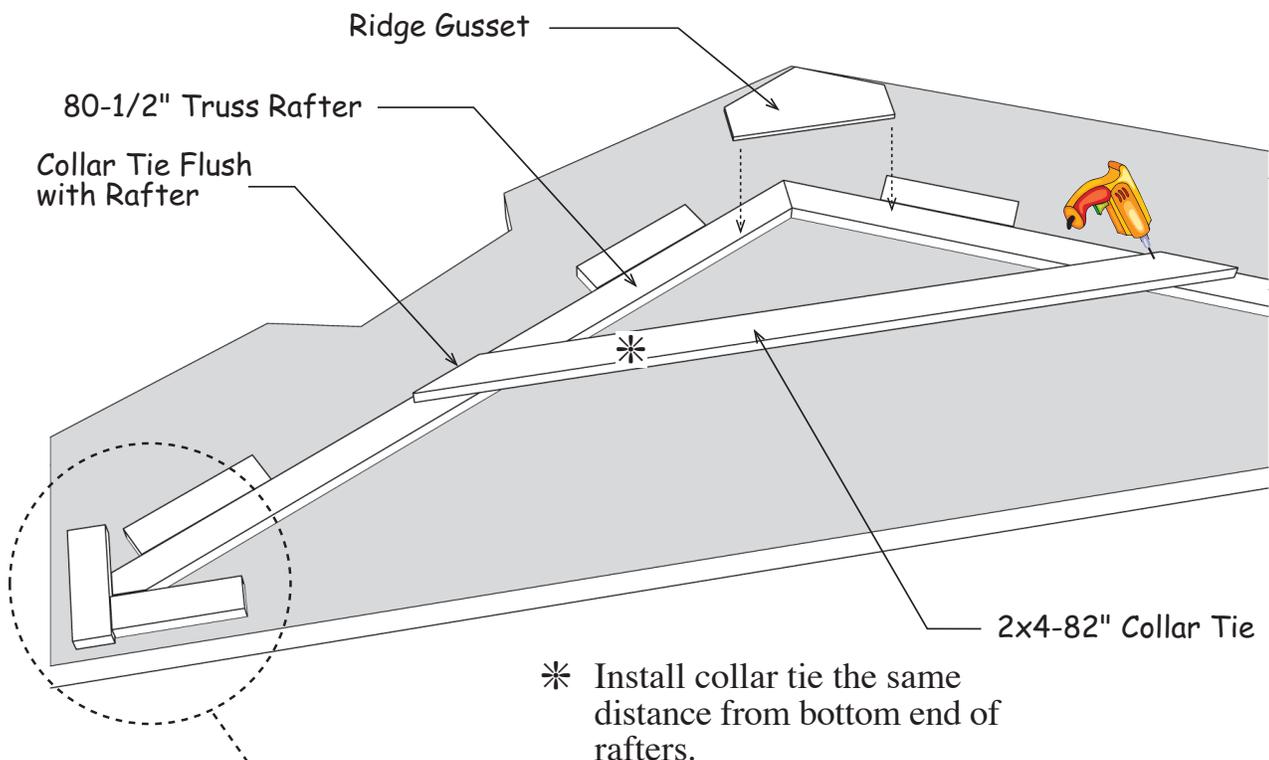


Detail 'B'

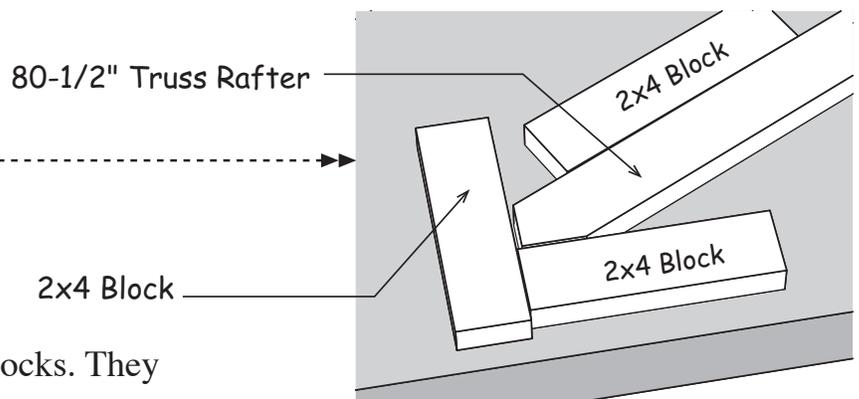


6. Remove and save the short 2x4 blocks. They will be used in a later step.

Step 8A Set Walls For 12' x 12' Building

 If you are constructing a 12' x 16' building, go to **Step 8B**.

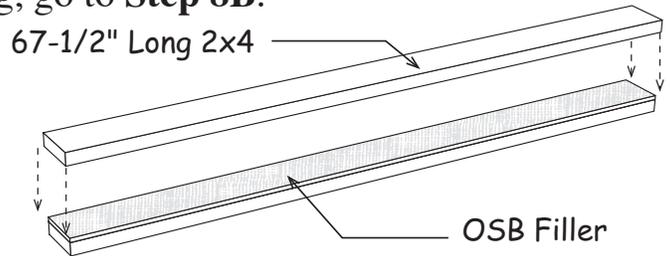

1. Gather (2) two 67-1/2" long 2x4 boards and a 3-1/4" x 67-1/4" OSB filler panel. Nail header together from both sides with 10d sinkers staggered 6" apart.
2. Erect wall panels. **IMPORTANT make sure walls are plumb and square.** Secure together at the corners using (4) four 10d sinkers per corner.
3. Nail along siding edge where it overlaps front and back walls at corners.
4. Install the 2x4 door header between the front wall panels. Nail through the wall stud into the ends of the header. Toenail into the top wall plates.
5. Temporarily install (2) two 2x4-72" boards at both sides of the door opening to hold the wall straight. These boards will be used later for tie plates.
6. Nail all wall panels to the floor through the bottom plate. Space 10d sinkers 24" apart.

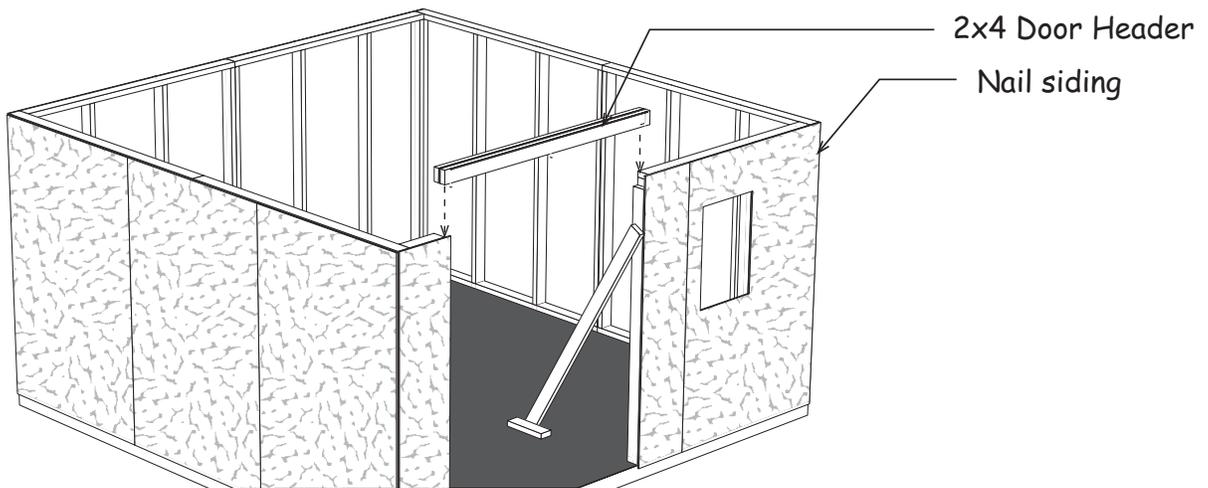


Drawing shows a building with the doors offset.

7. Install (2) two 4-1/4" siding panels over the door header. The siding should extend 3/4" below the door header. Cut length to fit. Wall trim, installed later, will hide where the siding butts the front wall siding.

Cut 4-1/4" x 48" Siding Panels to Fit


3/4" Below Bottom of Header

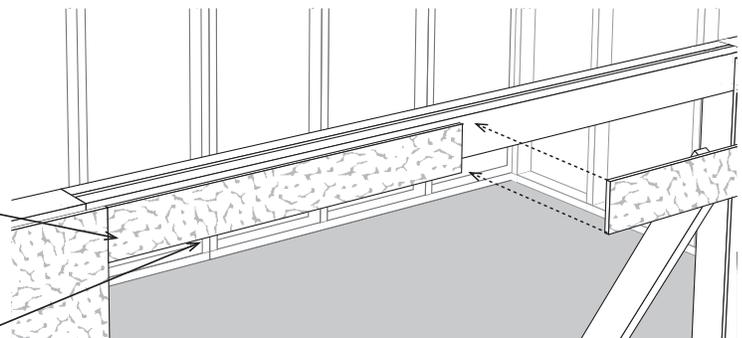

Step 8B Set Walls For 12' x 16' Building


1. Assemble door header using (2) two 67-1/2" long 2x4 boards and 3-1/4" x 67-1/4" OSB filler panel. Nail header together with (8) eight 10d sinkers on each side.

67-1/2" Long 2x4

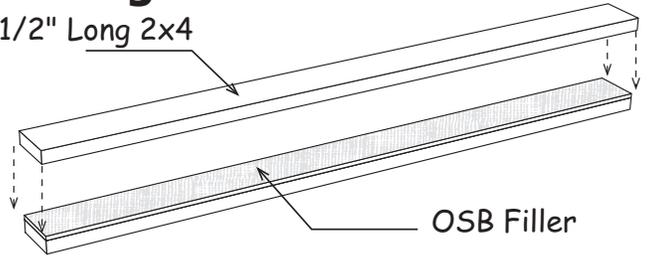

OSB Filler


2. Erect wall panels. **IMPORTANT make sure walls are plumb and square.** Secure together at the corners using (4) four 10d sinkers per corner.
3. Nail siding on each 4' wall panel to the 12' wall panels. Nail along siding edge where it overlaps at corners.
4. Install the 2x4 door header between the front wall panels. Nail through the wall studs into the ends of the header. Toenail into the top wall plates.
5. Temporarily install (2) two 2x4-72" boards at both sides of the door opening to hold the wall straight. These boards will be used later for tie plates.
6. Nail all wall panels to the floor through the bottom plate. Space 10d sinkers 24" apart.

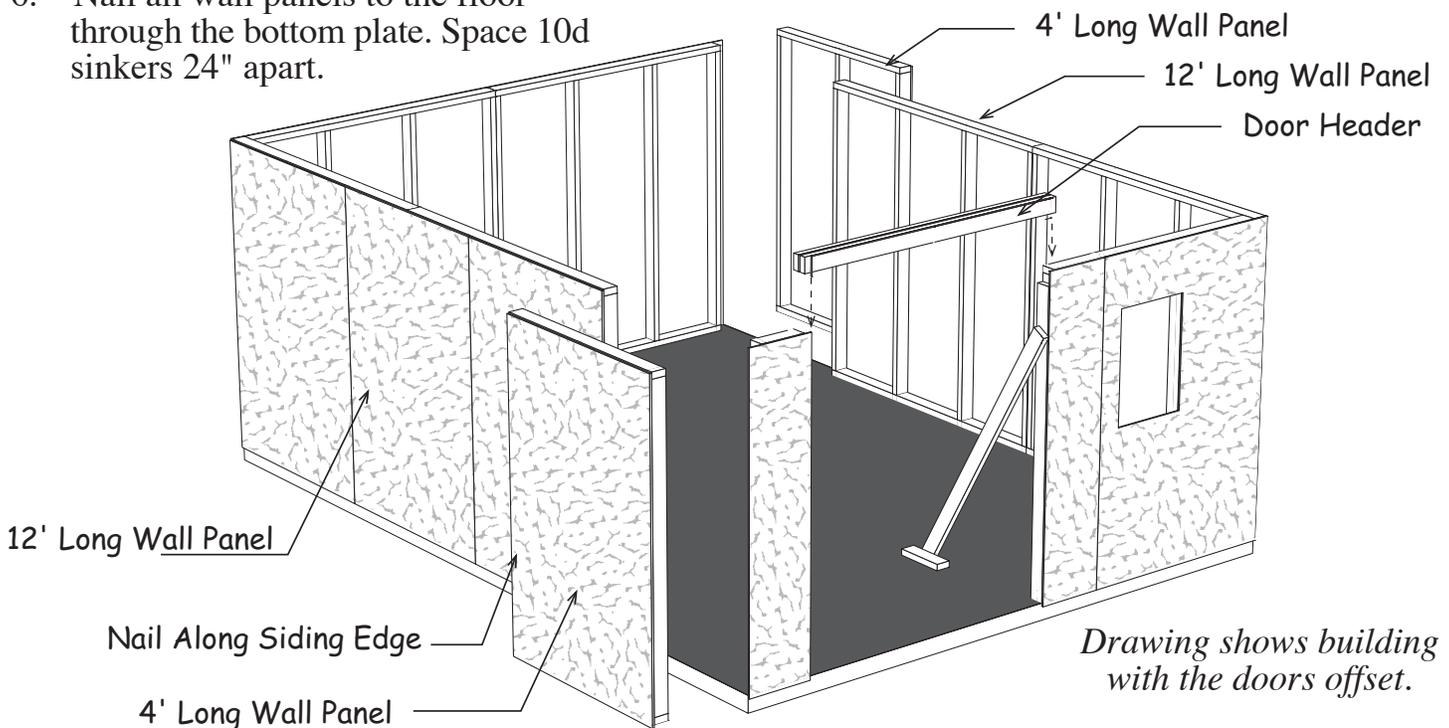

7. Install (2) two 4-1/4" siding panels over the door header. The siding should extend 3/4" below the door header. Cut length to fit. Wall trim, installed later, will hide where the siding butts the front wall siding.

Cut 4-1/4" x 48" Siding Panels to Fit


3/4" Below Bottom of Header

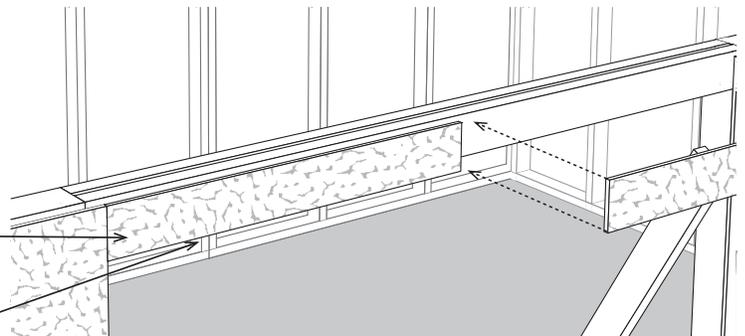

Step 9 Install Trim

 *Tip; Paint the siding and trim boards before installing the trim.*


1. Install (2) two 75-3/4" long 1x3 corner trim boards to the side wall flush with the top 2x4 wall plate and flush with siding on the front and back walls. Use 6d galv. nails, spaced 12" apart.
2. Install a 75-3/4" long 1x4 trim board to the front wall flush with wall plate and with 1x3 trim.

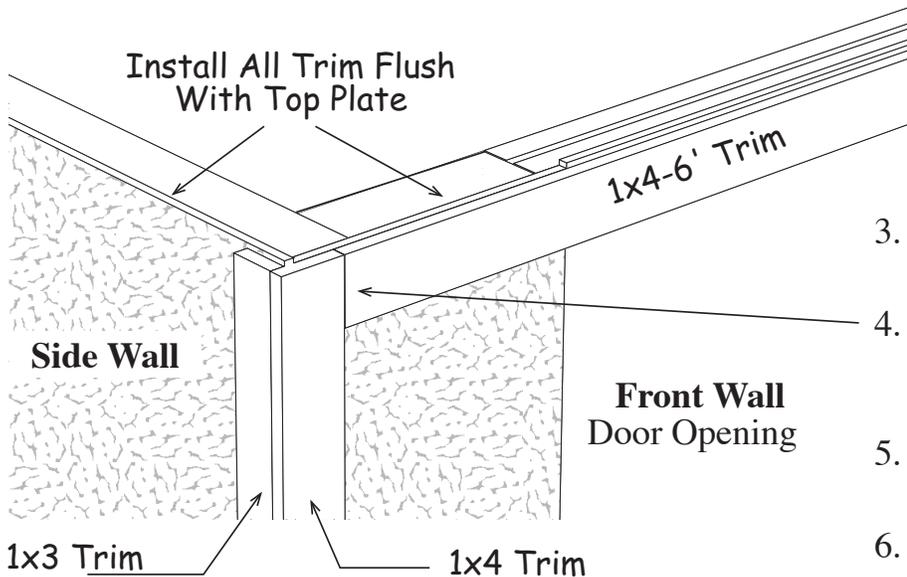

3. Repeat above steps on opposite side wall and front corner.
4. Butt a 1x4-6' trim board against 1x4 corner trim and flush with top plate. Nail along top.
5. Cut a second 1x4-6' trim board to finish at opposite corner.
6. Repeat to install trim on back wall.

Step 10 Install Primed Soffit and Filler

1. Locate (1) one 7" wide x 48-3/4" long siding panel and cut in half. Install one half over the side wall with the primed side facing down. Cut edges should be flush with the inside of the top 2x4 wall plate and flush with the trim on the front wall. Tack the soffit with a couple 6d common nails. Installing 2x4 tie plates in a later step will provide more nailing.
2. Install (3) three more soffit boards for a 12' building or (4) four for a 16' building. Cut the last soffit flush with the back wall trim.
3. Repeat to install soffit boards on the other side wall.

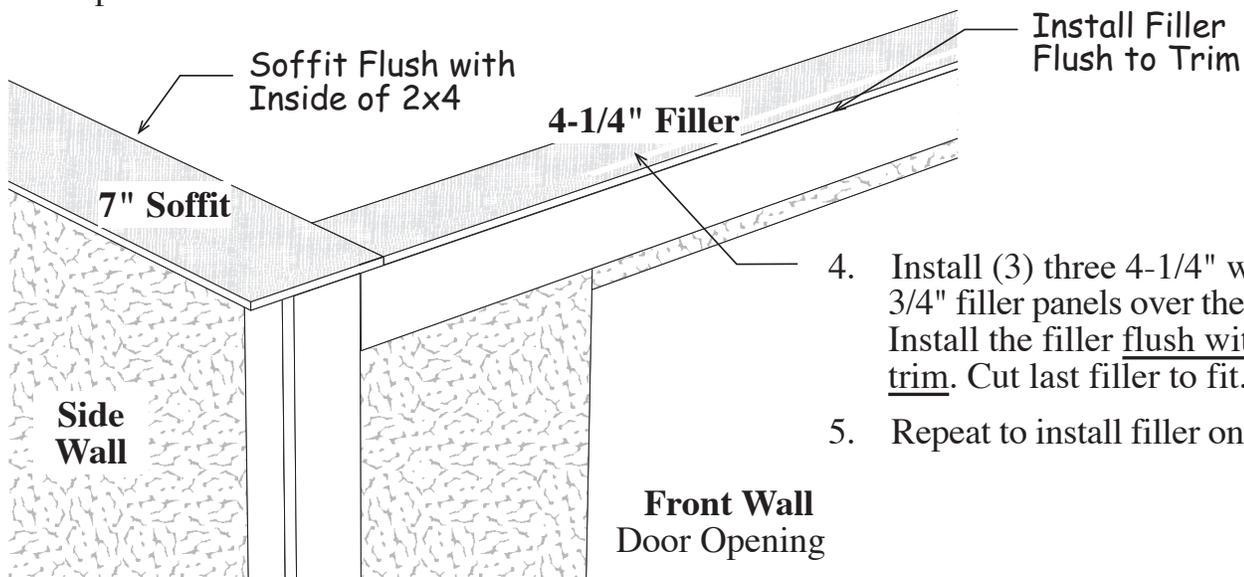


4. Install (3) three 4-1/4" wide x 48-3/4" filler panels over the front wall. Install the filler flush with the 1x4 trim. Cut last filler to fit.
5. Repeat to install filler on back wall.

Step 11 Install Siding on Gables


 Gable siding is factory cut to be installed either working from left to right or right to left. Regardless of the direction always begin with the 'LAP' Edge flush with end of the gable.

1. Select one of the gable frames. Turn the gable over so bottom plate is on edge on floor. Support gable studs and rafters with (2) two 2x4-72" boards stacked. This will give you a solid surface when nailing siding.
2. Install a gable siding panel with the 'LAP' edge flush with the end of of bottom plate. Use 6d galv. nails. The siding will extend 3/4" below the bottom 2x4.
3. Install center panel. Cut last panel flush with end of bottom plate.
4. Repeat to install siding on the other gable frame.

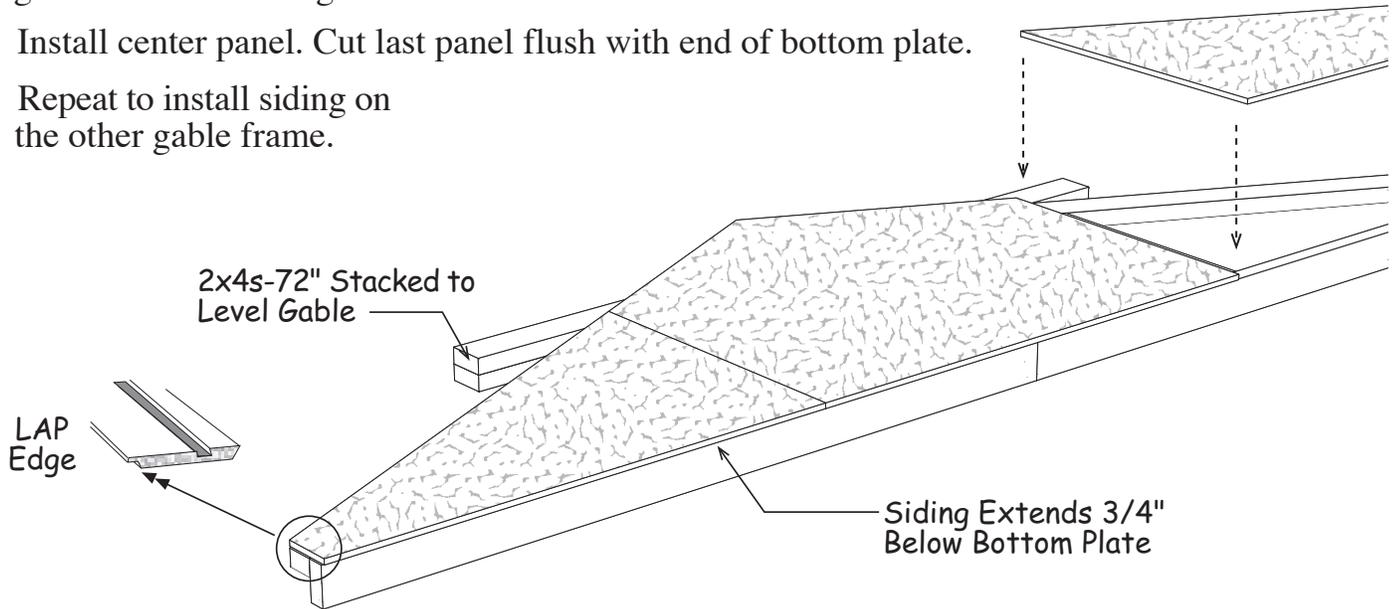

Step 12 Install Gables

1. Install a gable on the rear wall. The gable siding will extend over the 1x4 trim on the lower wall. Secure gable to wall by nailing through the gable plate with 10d sinkers. Nail siding along the 1x4 trim board with 6d galv. nails.
2. Install gable on the front wall.

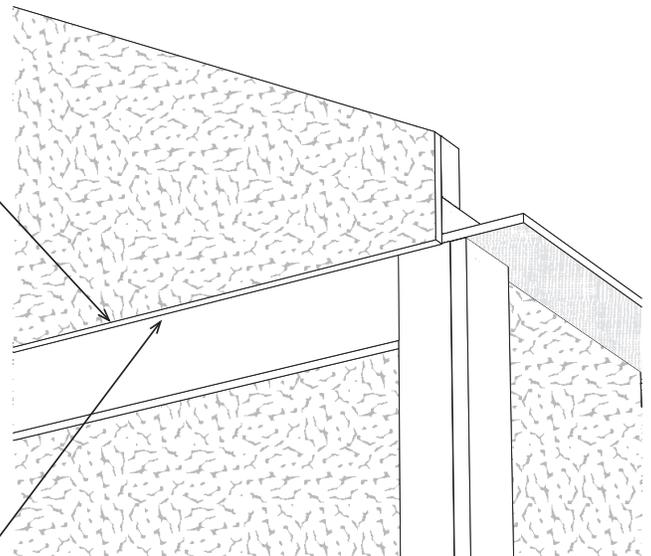


Important: Bottom edge of siding extends over 1x4 trim. Paint this edge.

Step 13 Install 2x4 Tie Plates on Side Walls


 For a 16' Building Length, Skip to Number 4

1. Cut a 2x4-72" in half and install one 3' piece over a side wall, against the front gable plate and flush with the inside of soffit. Use 10d sinkers.
2. If used for a wall brace, remove a 72" long 2x4 and install this next to the 3' long 2x4. Cut a 3' piece to fit against rear gable.
3. Repeat to install tie plates on the oppost side wall.
4. Install a 4' long 2x4 over a side wall, against the front gable plate and flush with the inside of soffit. Use 10d sinkers.
5. If used for a wall brace, remove a 72" long 2x4 and install this next to 4' tie plate. Cut another 72" 2x4 to fit against reart gable.
6. Install tie plates on the opposite side wall.

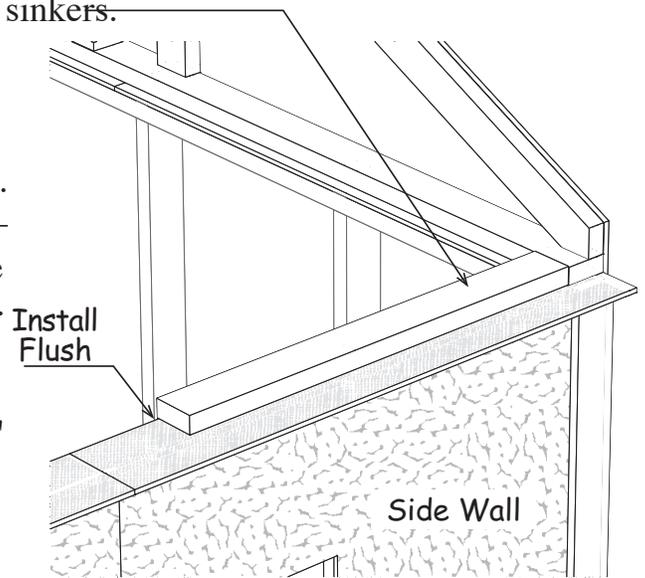

Step 14 Layout Roof Trusses

1. Layout the truss spacing from the left sidewall of the building. Measure from the backside of the 2x4 gable frame when marking the location of the first truss. Continue 24" spacing to other gable. **Important:** When marking the opposite wall, place the 'X' mark on the same side of the line so your trusses are parallel when they are installed.
2. Install metal hangers to the tie plate with hanger nails. The opening should line up with the 'X' mark, the bottom of the opening, flush with the 2x4 tie plate. **Detail 'D'**.

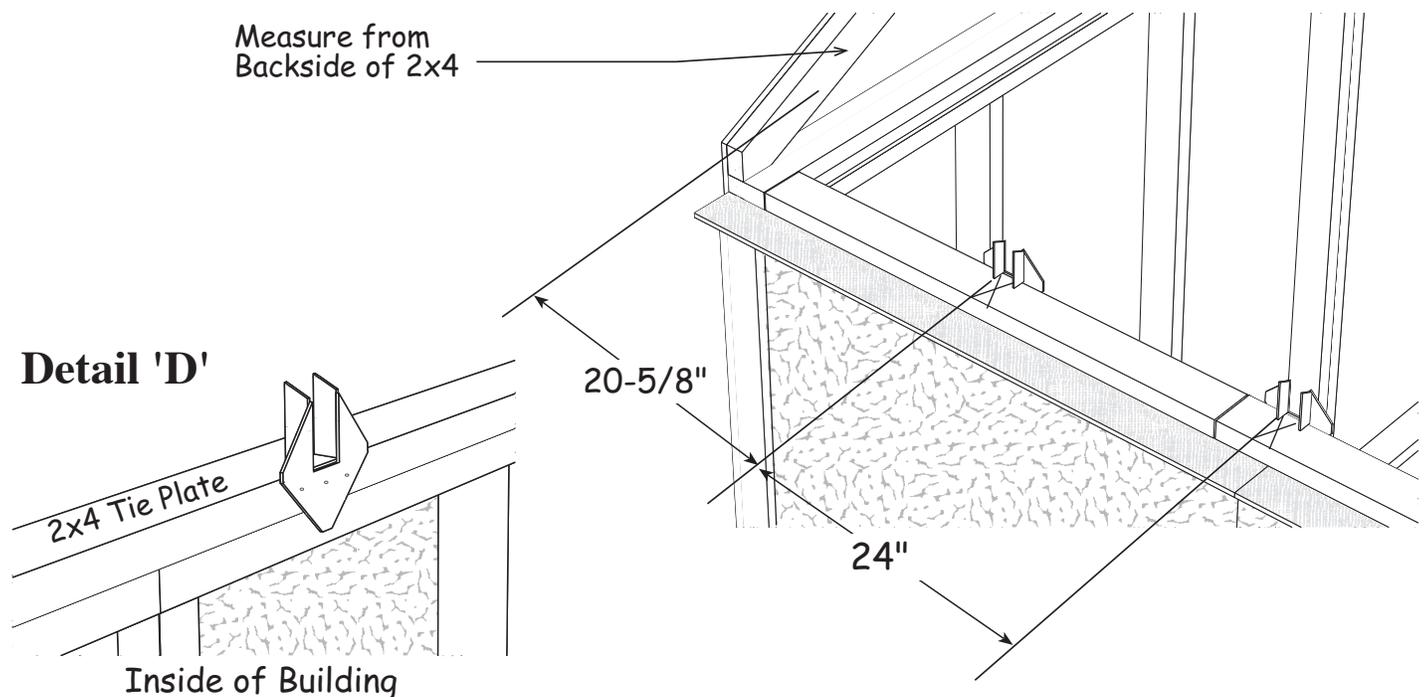


Step 15 Set Roof Trusses and Soffit Blocks

1. Set roof trusses. Secure trusses to metal hangers with hanger nails.


2. Install short 2x4 blocks at both ends of each truss. Secure 2x4 blocks to the soffit panel using (2) two 1-1/2" long exterior screws.

3. Install a 2x4 block at each end of the soffit, flush with the 2x4 gable frame.

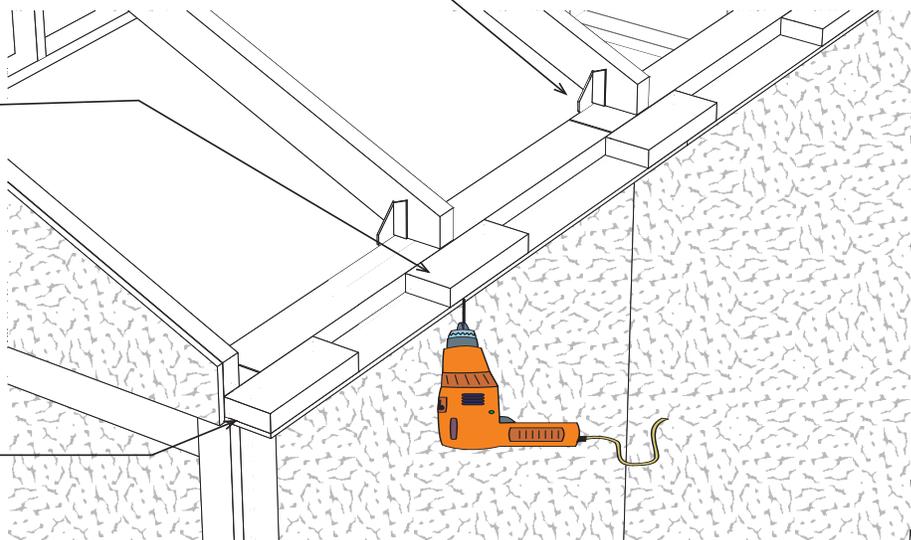


4. Install small primed siding fillers, *packed with the hardware*, over the 2x4 soffit blocks. Siding fillers will be flush with the gable siding. Use 6d galv. nails.

Siding Filler

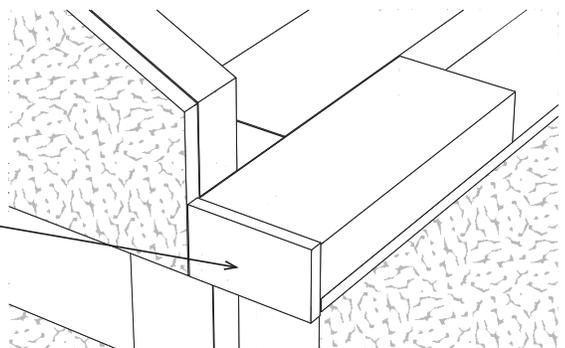


Step 16 Install Rear Gable Trim

1. Install a 8-1/2" long trim board, *called a keystone*, at the top of the gable flush with the top of the gable frame. Use 6d galv. nails.
2. Install (2) two 81" long 1x4 trim boards flush with the top of the gable frame. Use 6d galv. nails.

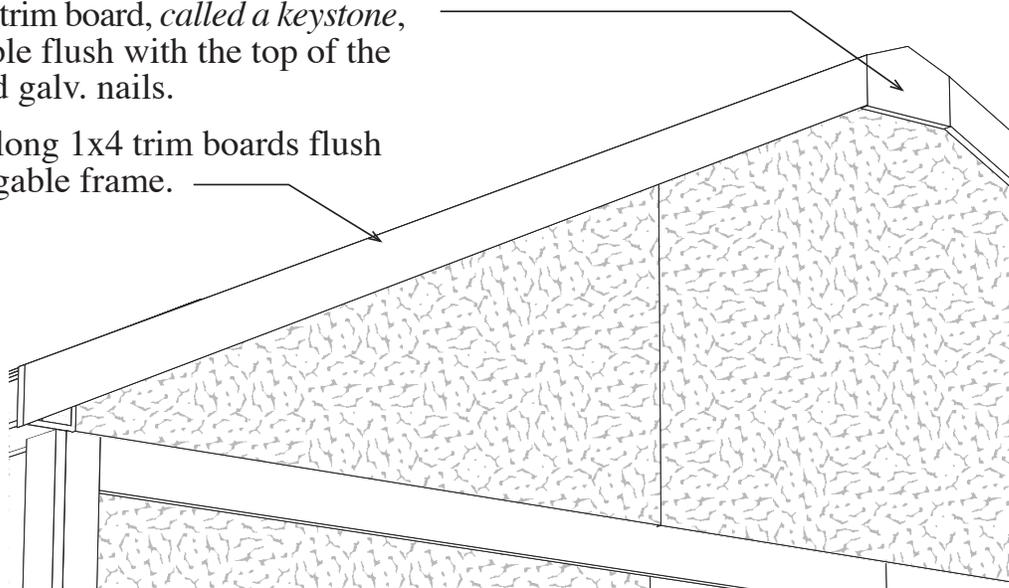


Step 17 Install 1x4 Fascia & Roof Sheathing


- Starting at the rear of the building, install a 1x4-6' fascia board against the rear gable trim. Install the fascia so the bottom edge of the roof sheathing will rest on the edge of the 1x4. See **Detail 'E'**. Use a straight edge to align the 1x4 board with the top of the trusses. Use 6d galv. nails.
- Repeat on opposite side wall.

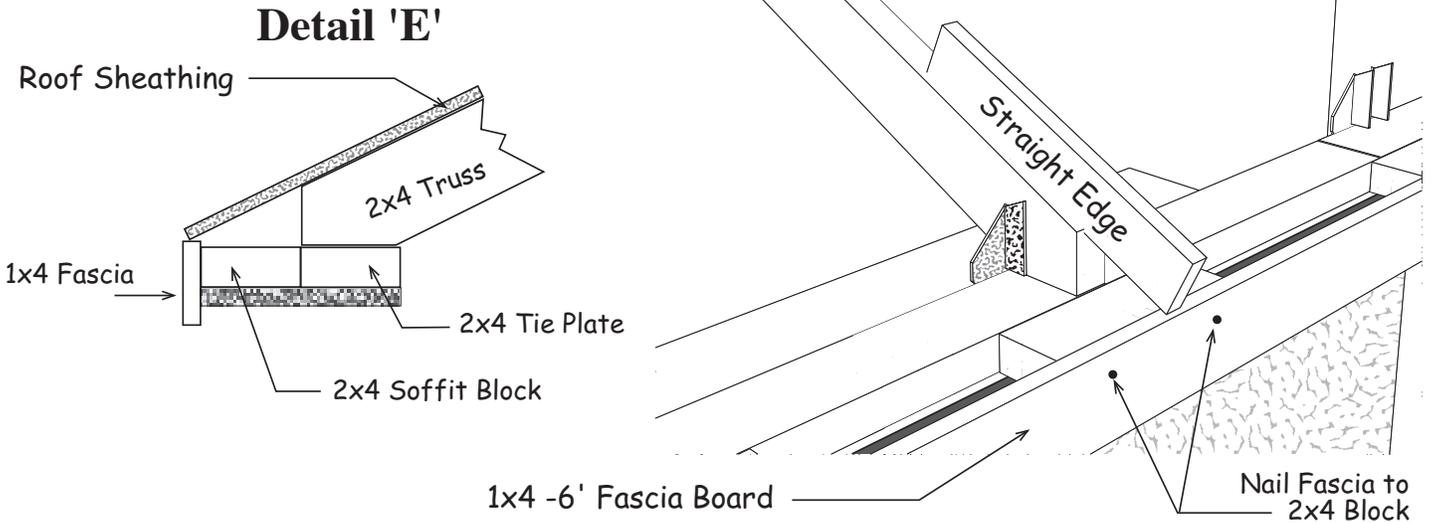


- If you are building a 16' building, butt a 1x4-4' fascia board to the 6' board. See sheathing drawing below. Install another 1x4-4' fascia on the opposite side.
- Do not install last fascia boards until a later step.
- Install roof sheathing per layout below. *See note for 16' building. Starting at rear of building install a 48"x72" OSB roof panel flush with 1x4 gable trim. Plumb each truss and gables. Make sure the sheets meet at center of truss. Use 6d common nails spaced 12" apart. The top row of roof sheathing will be about 1" below the ridge to allow for optional ventilation. **Important:** Make sure the roof sheathing extends 7-1/2" past the siding on the face of the gable.

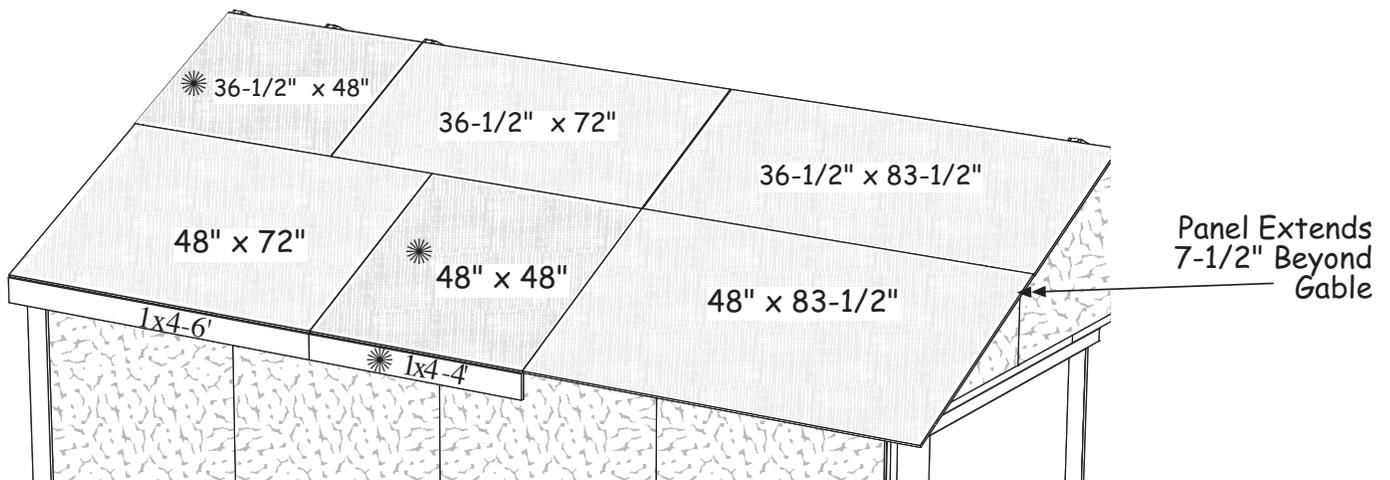

* Cut each 48" x 85-3/4" panel from the extension kit to a 48" x 48" and a 36-1/2" x 48" long panel.



Step 18 Install Front Gable Soffit and Door Trim

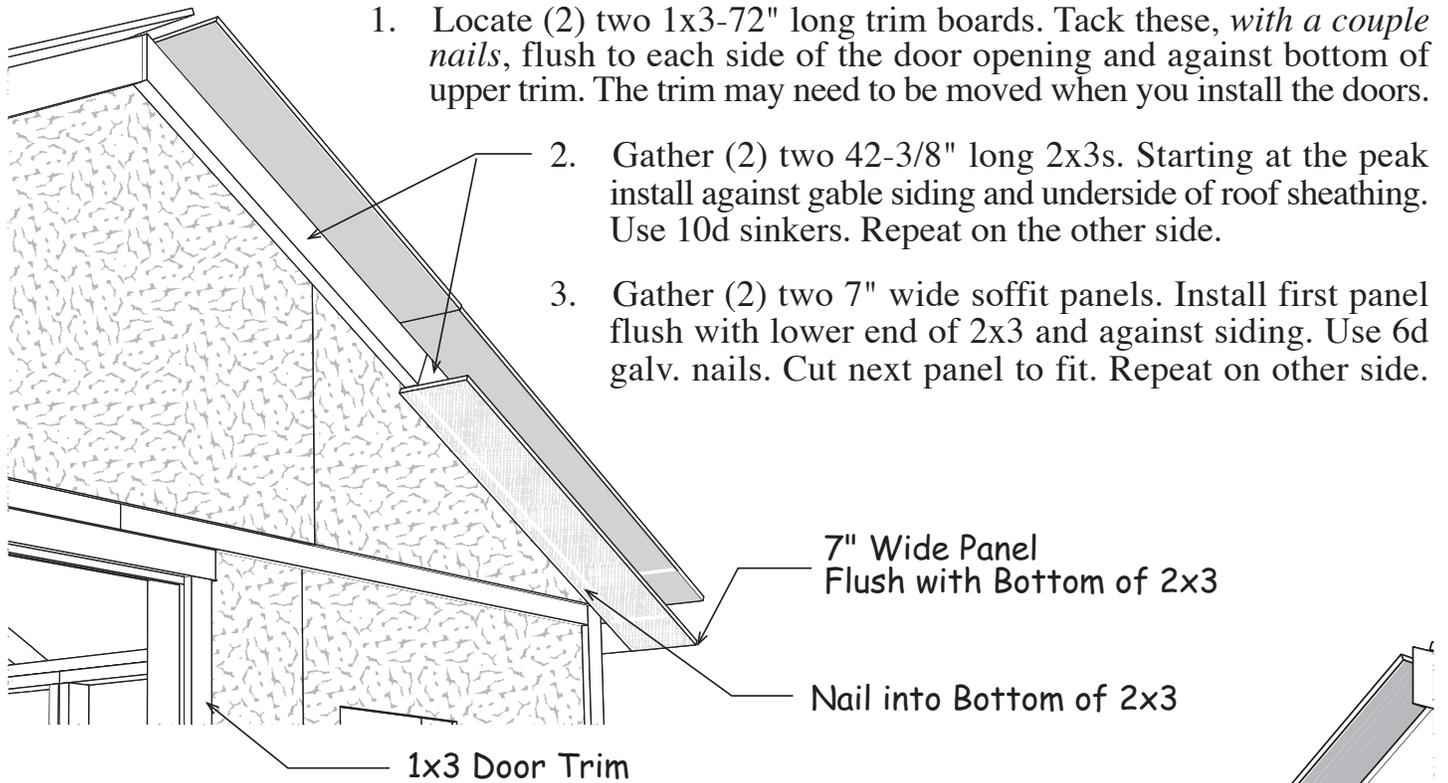


1. Locate (2) two 1x3-72" long trim boards. Tack these, *with a couple nails*, flush to each side of the door opening and against bottom of upper trim. The trim may need to be moved when you install the doors.
2. Gather (2) two 42-3/8" long 2x3s. Starting at the peak install against gable siding and underside of roof sheathing. Use 10d sinkers. Repeat on the other side.
3. Gather (2) two 7" wide soffit panels. Install first panel flush with lower end of 2x3 and against siding. Use 6d galv. nails. Cut next panel to fit. Repeat on other side.


4. Starting at the peak install (2) two 42-3/8" long 2x3s between the roof sheathing and the 7" soffit panels. Use 6d galv. nails on soffit and 6d common nails through roof sheathing. Set these boards flush with soffit panels. Roof sheathing will extend past 2x3 boards. Repeat on other side.
5. Install gable trim and keystone over the 2x3 boards and under the roof sheathing. Use 6d galv. nails.
6. Return to side walls and cut the last 1x4-7' fascia boards to fit.

Nail with 6d common

Nail with 6d Galv.

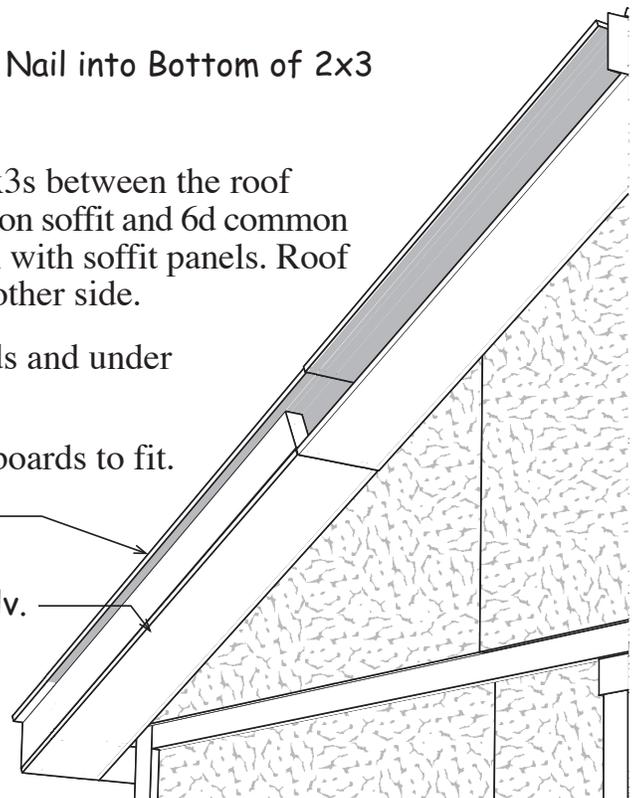


Step 19 Install Roofing Not Supplied in Kit




Optional ridge vent provides ideal ventilation.

1. Install metal roof edging perimeter of the roof area. If you are not installing shingles at this time, you can purchase felt paper to protect the roof sheathing. Install the felt paper before you install the metal roof edge.

Step 20 Install Doors & Hardware

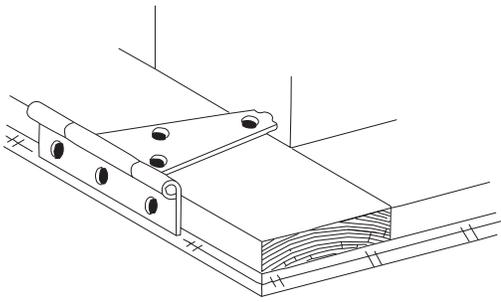

1. Lay the left door with the trim facing up. The siding on the left door extends past the door trim. See detail below.
2. Install 5" hinges to the left side of the door frame. To position the hinge properly, hold the rectangular plate against the frame. Use 1-1/4" black screws.
3. Install hinges to the right side of the other door.

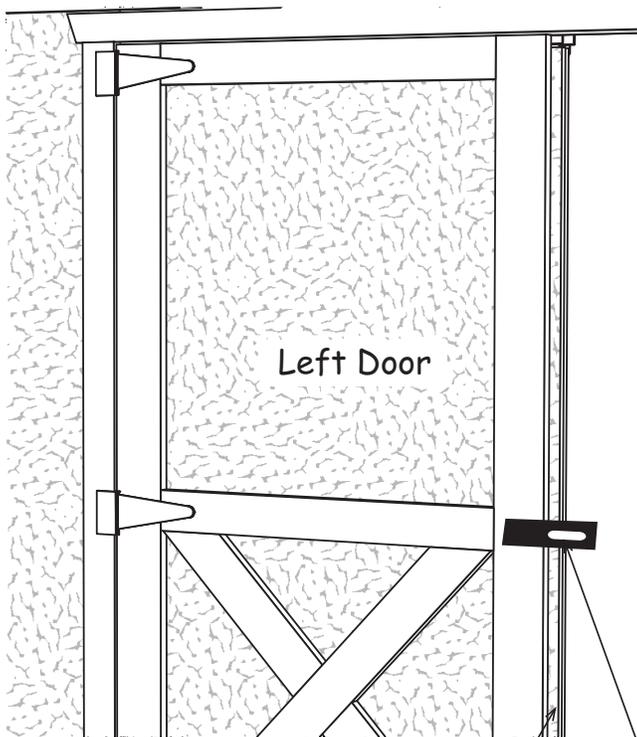


4. Before fastening the hinges to the side trim, temporarily prop the doors in the opening. Leave a space at the top and bottom of the doors and between the doors and the side trim to allow room for the doors to expand due to humidity.

If your door opening is out of square, the space around the doors will not be even. You can remove and re-position the side trim to make allowances for this. The side trim does not have to be flush with the frame of the door opening. You can move the trim in or out to make the door spacing equal.

5. Determine position of hinges and install to side trim with 2" screws.
6. Install door hasp on double doors. When properly installed the hasp will fold in half to receive locking latch and the screw heads will be covered.


Siding Extends Past Trim



Fold Hasp to Cover Screws

Barrel Bolt on the back of left door

7. Install a barrel bolt on the lower back of the door to secure this door in place when closed. You will need to drill a hole for the round shaft to drop into.
8. Install another barrel bolt at the top of the door.

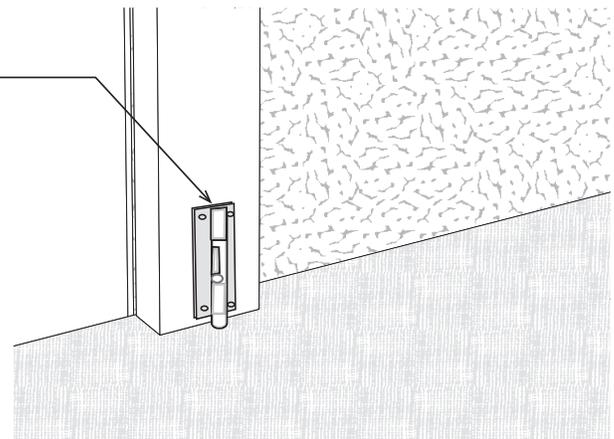

Bld. Length		<i>Material Packaged In Component Kit</i>									
12'	16'										
5	7	Collar Ties	2x4	82"	3	1 lb. box	10d	Sinkers			
14	18	Truss Rafters	2x4	80-1/2"	5	1 lb. box	6d	Galv.			
48	54	Wall Studs	2x4	72"	3	1 lb. box	6d	Common			
4	4	Wall Plates	2x4	68-1/2"	2	1 lb. box	Hanger Nails				
2	2	Wall Plates	2x4	67-1/2"	50	ea.	1-1/2"	Exterior Screws			
2	2	Wall Plates	2x4	58-1/2"	80	ea.	2-1/2"	Deck Screws			
2	2	Wall Plates	2x4	34-3/4"	6	ea.	5"	Door Hinges			
---	6	Wall Plates	2x4	48"	1	ea.	4-1/2"	Door Latch			
4	4	Gable Studs	2x4	23-1/2"	2	ea.	6"	Barrel Bolts			
8	8	Gable Framing	2x3	42-3/8"	25	ea.	2"	Hinge Screws			
10	14	Truss Gussets	7/16"	8" x 16"	25	ea.	1-1/4"	Hinge Screws			
11	13	Soffit Panels	3/8" x	7" x 48"	6	ea.	1x4	Metal Plates			
8	8	Filler Panels	3/8"x 4-1/4" x	48"	2	ea.	OSB Gussets 3-1/2" x 32"				
10	14	2x4 Metal Truss Hangers			1	ea.	OSB Filler 3-1/4" x 67-1/4"				
2	2	Fascia Boards	1x4 x	84"	2	ea.	1x6 Keystone 8-1/2"				
2	2	Fascia Boards	1x4 x	72"	4	ea.	1x4 Gable Trim 81"				
---	2	Fascia Boards	1x4 x	48"	4	ea.	1x4 Corner Trim 75-3/4"				
10	12	Siding Panels	48" x 75-3/4"		4	ea.	1x3 Corner Trim 75-3/4"				
2	2	Siding Panels	16" x 75-3/4"		4	ea.	1x4 Wall Trim 72"				
2	2	Gable Siding Panel	48" x 40"		2	ea.	1x3 Door Trim-sides 72"				
4	4	Gable Siding Panel	48" x 28"		1	ea.	1x3 Board (<i>not used</i>) 72"				
4	4	Roof Sheathing	72" Long		2	ea.	Pre-built Door 32" x 71-1/2"				
---	2	Roof Sheathing	85-3/4" Long		4	ea.	Gable Siding Fillers 2-1/2"x3-1/2"				
4	4	Roof Sheathing	83-1/2" Long		16	ea.	3/4" Pan Head Screws				
18	24	2x4 Truss Jig Blocks 8"									

Roofing Material - Not Included

Building Size		
12x12	12x16	
8 bdl.	10 bdl.	Roof Shingles
7 pcs.	8 pcs.	Roof 'drip' Edge 10'

